


Asbestos Register

(Hazardous Materials and Risk Assessment)

School : Bidwill Public School (4480)
Region : Western Sydney
State Electorate : Mount DrUITt
Local Government Area : Blacktown

Initial Survey : Noel Arnold & Associates : 14 - May - 2008
Reviewed By : Greencap-NAA : 13 - Aug - 2014

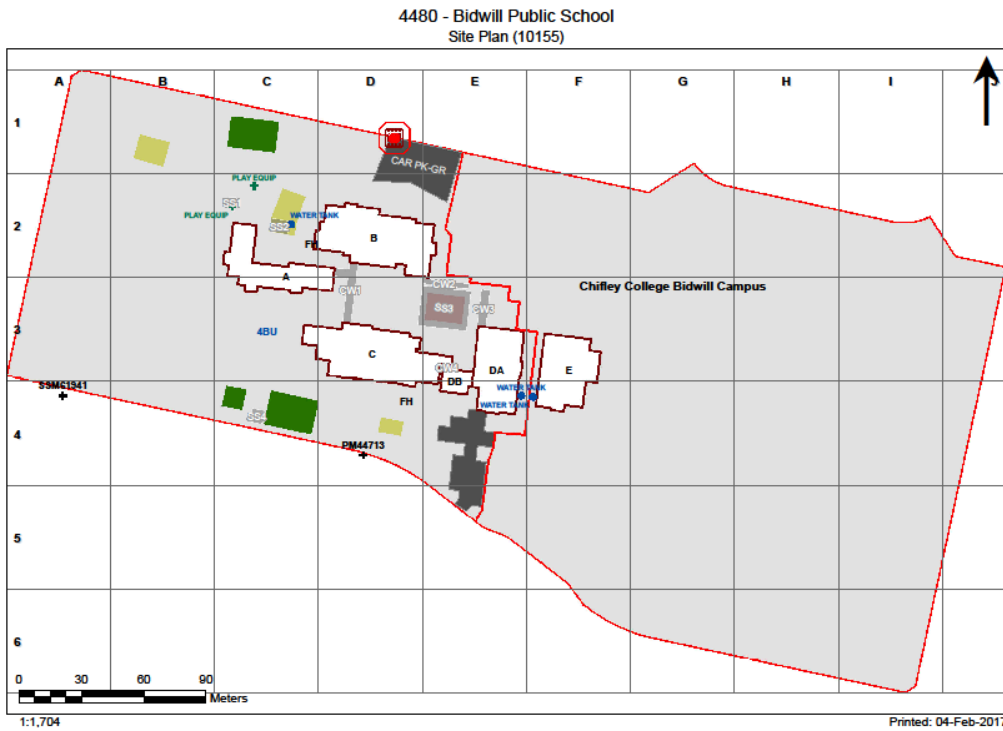

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00A - Pre-School Facilities - 1976 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids - Raked Ceiling No Asbestos Found

Underfloor Voids - Slab on Ground No Asbestos Found

Interior

B00A - R0002 - Home Base Store - P (14.51 m2)

No Asbestos

B00A - R0003 - Toilets-Unisex (12.59 m2)

No Asbestos

B00A - R0004 - Home Base - Pre (75.74 m2)

No Asbestos

B00A - R0005 - Kitchen - Pre (5.05 m2)

No Asbestos

B00A - R0006 - Staff Toilet - Pre (1.67 m2)

No Asbestos

B00A - R0007 - Staff Room - Pre (4.79 m2)

No Asbestos

B00A - R0010 - Cleaning Distributed Store (2.74 m2)

Floor Coverings Res/Textile	Vinyl Tiles	3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00A/R0010/Floor Coverings Res/Textile/S21					Chrysotile (white asbestos)	

Floor Coverings Res/Textile	Tile Adhesive	3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00A/R0010/Floor Coverings Res/Textile/S22					Chrysotile (white asbestos)	

B00A - R0011 - Distribution Board (0.82 m2)

Note: No inspection of live electrical installation.

Wall Linings Internal	Flat AC Sheeting	1m2	back of doors	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B0DB/R0007/Wall Linings Internal/S20					Chrysotile (white asbestos)	

Ceiling Structures/Linings	Flat AC Sheeting	1m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B0DB/R0007/Wall Linings Internal/S20					Chrysotile (white asbestos)	

B00A - R0012 - Home Base Store - P (14.59 m2)

No Asbestos

B00A - R0013 - Toilets-Unisex (12.66 m2)

No Asbestos

B00A - R0014 - Home Base - Pre (75.24 m2)

No Asbestos

B00A - R0015 - Kitchen - Pre (5.05 m2)

No Asbestos

B00A - R0016 - Staff Toilet - Pre (1.65 m2)

No Asbestos

B00A - R0017 - Staff Room - Pre (4.83 m2)

No Asbestos

B00A - R0020 - Movement (9.87 m2)

No Asbestos

B00A - R0021 - Home Base Store - P (27.66 m2)

Floor Coverings Res/Textile	Vinyl Tiles	28m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00A/R0010/Floor Coverings Res/Textile/S21					Chrysotile (white asbestos)	

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Floor Coverings Res/Textile	Tile adhesive	28m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00A/R0010/Floor Coverings Res/Textile/S22					Chrysotile (white asbestos)	

B00A - R0024 - Staff Room - Pre (4.76 m2)						
No Asbestos						
B00A - R0025 - Staff Toilet - Pre (1.67 m2)						
No Asbestos						
B00A - R0026 - Kitchen - Pre (5.03 m2)						
No Asbestos						
B00A - R0027 - Home Base - Pre (75.76 m2)						
No Asbestos						
B00A - R0028 - Home Base Store - P (14.64 m2)						
No Asbestos						
B00A - R0029 - Toilets-Unisex (12.64 m2)						
No Asbestos						
B00A - R0030 - Movement (17.9 m2)						
No Asbestos						
B00A - R0031 - General Storeroom - Pre (10.33 m2)						
No Asbestos						
B00A - R0032 - Movement (205.15 m2)						
No Asbestos						
B00A - R0033 - Personal Effects Storage (26.19 m2)						
Recently Modified Space Requires Inspection						
B00A - R0034 - Personal Effects Storage (26.05 m2)						
Recently Modified Space Requires Inspection						
B00A - R0035 - Personal Effects Storage (26.79 m2)						
Recently Modified Space Requires Inspection						
B00A - R0036 - Home Base Store (10 m2)						
Recently Modified Space Requires Inspection						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00B - General Learning/Pupil Facilities - 1976 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids - Raked Ceiling No Asbestos Found

Underfloor Voids - Slab on Ground No Asbestos Found

Interior

B00B - R0001 - Home Base (52.62 m2)

Ceiling Structures/Linings Vermiculite
 4480/B00B/R0023/Ceiling Structures/Linings/S23 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

B00B - R0003 - Toilets - Boys (14.55 m2)

Partition Walls (Cubicles) Compressed AC Sheet 4m2 South Good Condition (1) Low (1) Low Priority (2-3)
 4480/B00B/R0003/Partition Walls (Cubicles)/S6 **Chrysotile (White asbestos)**

B00B - R0004 - Disabled Toilet (13.54 m2)

Wall Linings Internal Flat AC Sheeting
 4480/B00B/R0004/Wall Linings Internal/S7 **No Asbestos Detected**

B00B - R0005 - Movement (21.81 m2)

No Asbestos

B00B - R0006 - Home Base (54.08 m2)

Ceiling Structures/Linings Vermiculite
 4480/B00B/R0023/Ceiling Structures/Linings/S23 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

B00B - R0007 - Practical Activities (18.58 m2)

Ceiling Structures/Linings Vermiculite
 4480/B00B/R0023/Ceiling Structures/Linings/S23 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

B00B - R0008 - Cleaning Distributed Store (3.98 m2)

No Asbestos

B00B - R0010 - Home Base (53.9 m2)

Ceiling Structures/Linings Vermiculite
 4480/B00B/R0023/Ceiling Structures/Linings/S23 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

B00B - R0011 - Toilets - Girls (15.31 m2)

Partition Walls (Cubicles) Compressed AC Sheet 8m2 West Good Condition (1) Low (1) Low Priority (2-3)
 4480/B00B/R0003/Partition Walls (Cubicles)/S6 **Chrysotile (White asbestos)**

B00B - R0012 - Toilets - Boys (12.91 m2)

Partition Walls (Cubicles) Compressed AC Sheet 10m2 East Good Condition (1) Low (1) Low Priority (2-3)
 4480/B00B/R0003/Partition Walls (Cubicles)/S6 **Chrysotile (White asbestos)**

B00B - R0013 - Distribution Board (0.61 m2)

Note: No inspection of live electrical installation.

No Asbestos

B00B - R0014 - Home Base (56.31 m2)

Ceiling Structures/Linings Vermiculite
 4480/B00B/R0023/Ceiling Structures/Linings/S23 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

B00B - R0016 - Movement (32.97 m2)

No Asbestos

B00B - R0017 - Toilets - Boys (16.07 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Partition Walls (Cubicles)	Compressed AC Sheet	4m2	West	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00B/R0003/Partition Walls (Cubicles)/S6					Chrysotile (White asbestos)	
B00B - R0018 - Toilets - Girls (14.72 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	8m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00B/R0003/Partition Walls (Cubicles)/S6					Chrysotile (White asbestos)	
B00B - R0020 - Home Base (57.36 m2)						
Ceiling Structures/Linings	Vermiculite					
4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0021 - Staff Room (14.01 m2)						
No Asbestos						
B00B - R0022 - Home Base (53.97 m2)						
Ceiling Structures/Linings	Vermiculite					
4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0023 - Practical Activities (18.96 m2)						
Ceiling Structures/Linings	Vermiculite					
4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0024 - Staff Toilet (2.34 m2)						
No Asbestos						
B00B - R0025 - Sports Store (12.65 m2)						
No Asbestos						
B00B - R0026 - Toilets - Boys (11.35 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	8m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00B/R0003/Partition Walls (Cubicles)/S6					Chrysotile (White asbestos)	
B00B - R0027 - Toilets - Girls (10.65 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	10m2	West	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00B/R0003/Partition Walls (Cubicles)/S6					Chrysotile (White asbestos)	
B00B - R0029 - Home Base (54.32 m2)						
Ceiling Structures/Linings	Vermiculite					
4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0030 - Home Base (55.95 m2)						
Ceiling Structures/Linings	Vermiculite					
4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0032 - Movement (412.29 m2)						
No Asbestos						
B00B - R0033 - Stairs (8.85 m2)						
No Asbestos						
B00B - R0034 - Stairs (8.82 m2)						
No Asbestos						
B00B - R0035 - Home Base Store (7.31 m2)						
Ceiling Structures/Linings	Vermiculite					
4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0036 - Practical Activities - 1hb (10.98 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite 4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R0037 - Home Base Store (6.96 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R0038 - Practical Activities - 1hb (10.58 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R0039 - Home Base Store (6.31 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R0040 - Practical Activities - 1hb (9.63 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R0041 - Home Base Store (6.02 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R0042 - Practical Activities - 1hb (9.15 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R0043 - Home Base Store (7.22 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R0044 - Practical Activities - 1hb (10.88 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R0045 - Home Base Store (6.58 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R0046 - Practical Activities - 1hb (9.98 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R1001 - Home Base (54.7 m2)						
No Asbestos						
B00B - R1003 - Toilets - Boys (15.55 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	4m2	South	Good Condition (1)	Low (1)	Low Priority (2-3) 4480/B00B/R0003/Partition Walls (Cubicles)/S6 Chrysotile (White asbestos)
B00B - R1004 - Toilets - Girls (17.04 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	4m2	North	Good Condition (1)	Low (1)	Low Priority (2-3) 4480/B00B/R0003/Partition Walls (Cubicles)/S6 Chrysotile (White asbestos)
B00B - R1005 - Home Base (56.15 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
No Asbestos						
B00B - R1007 - No Access (17.99 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	12m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00C/R0022/Partition Walls (Cubicles)/S2					Chrysotile (White asbestos)	
B00B - R1008 - Toilets - Girls (14.97 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	8m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00B/R0003/Partition Walls (Cubicles)/S6					Chrysotile (White asbestos)	
B00B - R1010 - Home Base (55.82 m2)						
No Asbestos						
B00B - R1011 - Distribution Board (0.62 m2)						
					Note: No inspection of live electrical installation.	
No Asbestos						
B00B - R1012 - Home Base (55.88 m2)						
No Asbestos						
B00B - R1014 - Toilets - Boys (16.7 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	17m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00B/R0003/Partition Walls (Cubicles)/S6					Chrysotile (White asbestos)	
B00B - R1015 - Toilets - Girls (15.65 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	16m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00B/R0003/Partition Walls (Cubicles)/S6					Chrysotile (White asbestos)	
B00B - R1017 - Home Base (59.64 m2)						
No Asbestos						
B00B - R1018 - Deputy Principal (15.13 m2)						
No Asbestos						
B00B - R1019 - Home Base (58.81 m2)						
No Asbestos						
B00B - R1021 - Staff Toilet (1.94 m2)						
Wall Linings Internal	Flat AC Sheeting	4480/B00B/R0004/Wall Linings Internal/S7			No Asbestos Detected	
B00B - R1022 - General Storeroom (12.68 m2)						
No Asbestos						
B00B - R1024 - Home Base (56.67 m2)						
No Asbestos						
B00B - R1025 - Home Base (56.76 m2)						
No Asbestos						
B00B - R1027 - Movement (180.36 m2)						
No Asbestos						
B00B - R1028 - Stairs (12.32 m2)						
No Asbestos						
B00B - R1029 - Stairs (12.46 m2)						
No Asbestos						
B00B - R1030 - Home Base Store (7.32 m2)						
No Asbestos						
B00B - R1031 - Practical Activities - 1hb (11.85 m2)						
No Asbestos						
B00B - R1032 - Home Base Store (7.3 m2)						
No Asbestos						
B00B - R1033 - Practical Activities - 1hb (11.78 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

No Asbestos

B00B - R1034 - Home Base Store (7 m2)

No Asbestos

B00B - R1035 - Practical Activities - 1hb (11.29 m2)

No Asbestos

B00B - R1036 - Home Base Store (7.27 m2)

No Asbestos

B00B - R1037 - Practical Activities - 1hb (11.75 m2)

No Asbestos

B00B - R1038 - Home Base Store (6.02 m2)

No Asbestos

B00B - R1039 - Practical Activities - 1hb (9.8 m2)

No Asbestos

B00B - R1040 - Home Base Store (6.26 m2)

No Asbestos

B00B - R1041 - Practical Activities - 1hb (10.26 m2)

No Asbestos

B00B - R1042 - Home Base Store (7 m2)

No Asbestos

B00B - R1043 - Practical Activities - 1hb (11.29 m2)

No Asbestos

B00B - R1044 - Home Base Store (7 m2)

No Asbestos

B00B - R1045 - Practical Activities - 1hb (11.36 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00C - General Learning/Pupil Facilities - 1976 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids - Raked Ceiling No Asbestos Found

Underfloor Voids - Slab on Ground No Asbestos Found

Interior

B00C - R0001 - Movement (70.13 m2)

No Asbestos

B00C - R0002 - Home Base (63.64 m2)

No Asbestos

B00C - R0004 - Staff Room Annexe (38.47 m2)

No Asbestos

B00C - R0005 - Interview (17.19 m2)

No Asbestos

B00C - R0006 - General Storeroom (14.94 m2)

No Asbestos

B00C - R0007 - Distribution Board (0.8 m2)

Note: No inspection of live electrical installation.

Wall Linings Internal	Flat AC Sheeting	4m2	Back of Door	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B0DB/R0007/Wall Linings Internal/S20					Chrysotile (white asbestos)	

B00C - R0008 - Toilets-Unisex (3.51 m2)

No Asbestos

B00C - R0010 - Home Base (80.77 m2)

Ceiling Structures/Linings	Vermiculite	4480/B00B/R0023/Ceiling Structures/Linings/S23			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

B00C - R0011 - Toilets-Unisex (3.85 m2)

No Asbestos

B00C - R0013 - Home Base (78.65 m2)

Ceiling Structures/Linings	Vermiculite	4480/B00B/R0023/Ceiling Structures/Linings/S23			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

B00C - R0016 - Toilets-Unisex (2.74 m2)

No Asbestos

B00C - R0017 - Movement (5.12 m2)

No Asbestos

B00C - R0018 - Other (14.26 m2)

Floor Coverings Res/Textile	Vinyl Tiles	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00A/R0010/Floor Coverings Res/Textile/S21					Chrysotile (white asbestos)	
Floor Coverings Res/Textile	adhesive	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00A/R0010/Floor Coverings Res/Textile/S22					Chrysotile (white asbestos)	

B00C - R0021 - Toilets-Unisex (2.25 m2)

No Asbestos

B00C - R0022 - Toilets - Girls (18.98 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	8m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00C/R0022/Partition Walls (Cubicles)/S2					Chrysotile (White asbestos)	

B00C - R0023 - Cleaning Distributed Store (3.12 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Floor Coverings Res/Textile	Vinyl Tiles	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00A/R0010/Floor Coverings Res/Textile/S21					Chrysotile (white asbestos)	
Floor Coverings Res/Textile	Adhesive	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00A/R0010/Floor Coverings Res/Textile/S22					Chrysotile (white asbestos)	
B00C - R0024 - Distribution Board (0.76 m2)				Note: No inspection of live electrical installation.		
Wall Linings Internal	Flat AC Sheeting	1m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B0DB/R0007/Wall Linings Internal/S20					Chrysotile (white asbestos)	
B00C - R0025 - Toilets - Boys (18.36 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	10m2	North	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00C/R0022/Partition Walls (Cubicles)/S2					Chrysotile (White asbestos)	
B00C - R0026 - Movement (44.92 m2)						
No Asbestos						
B00C - R0027 - Tiered Learning Space (36.02 m2)						
No Asbestos						
B00C - R0029 - Home Base (56.76 m2)						
No Asbestos						
B00C - R0030 - Home Base (56.84 m2)						
No Asbestos						
B00C - R0032 - Deputy Principal (18.71 m2)						
No Asbestos						
B00C - R0033 - Cleaning Distributed Store (4.98 m2)						
No Asbestos						
B00C - R0034 - Movement (305.71 m2)						
No Asbestos						
B00C - R0035 - Stairs (9.02 m2)						
No Asbestos						
B00C - R0036 - Stairs (8.27 m2)						
No Asbestos						
B00C - R0037 - Home Base Store (6.02 m2)						
No Asbestos						
B00C - R0038 - Practical Activities - 1hb (10.95 m2)						
No Asbestos						
B00C - R0039 - Home Base Store (5.27 m2)						
Ceiling Structures/Linings	Vermiculite	4480/B00B/R0023/Ceiling Structures/Linings/S23			Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00C - R0040 - Practical Activities - 1hb (5.05 m2)						
Ceiling Structures/Linings	Vermiculite	4480/B00B/R0023/Ceiling Structures/Linings/S23			Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00C - R0041 - Home Base Store (6.64 m2)						
Ceiling Structures/Linings	Vermiculite	4480/B00B/R0023/Ceiling Structures/Linings/S23			Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00C - R0042 - Practical Activities - 1hb (6.93 m2)						
Ceiling Structures/Linings	Vermiculite	4480/B00B/R0023/Ceiling Structures/Linings/S23			Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00C - R0043 - Home Base (79.63 m2)						
Ceiling Structures/Linings	Vermiculite					
	4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R0044 - Home Base Store (6.93 m2)						
Ceiling Structures/Linings	Vermiculite					
	4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R0045 - Practical Activities - 1hb (6.75 m2)						
Ceiling Structures/Linings	Vermiculite					
	4480/B00B/R0023/Ceiling Structures/Linings/S23					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R0046 - Home Base (86.39 m2)						
No Asbestos						
B00C - R0047 - Home Base Store (5.94 m2)						
No Asbestos						
B00C - R0048 - Practical Activities - 1hb (5.71 m2)						
No Asbestos						
B00C - R0049 - Home Base Store (6.04 m2)						
No Asbestos						
B00C - R0050 - Home Base Store (9.45 m2)						
No Asbestos						
B00C - R0051 - Home Base Store (8.71 m2)						
No Asbestos						
B00C - R0052 - Practical Activities - 1hb (6.72 m2)						
No Asbestos						
B00C - R1001 - Toilets - Girls (15.22 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	6m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4480/B00C/R0022/Partition Walls (Cubicles)/S2					Chrysotile (White asbestos)
B00C - R1002 - Home Base (60.18 m2)						
No Asbestos						
B00C - R1003 - Movement (124.55 m2)						
No Asbestos						
B00C - R1005 - Toilets - Boys (19.25 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	6m2	North	Good Condition (1)	Low (1)	Low Priority (2-3)
	4480/B00C/R0022/Partition Walls (Cubicles)/S2					Chrysotile (White asbestos)
B00C - R1006 - Distribution Board (0.69 m2)						
Note: No inspection of live electrical installation.						
Wall Linings Internal	Flat AC Sheeting	1m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4480/B00C/R1016/Wall Linings Internal/S4					Chrysotile (White asbestos)
Ceiling Structures/Linings	Flat AC Sheeting	1m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4480/B00C/R1016/Wall Linings Internal/S4					Chrysotile (White asbestos)
B00C - R1009 - Craft Store (72.35 m2)						
No Asbestos						
B00C - R1016 - Staff Toilet (2.31 m2)						
Wall Linings Internal	Flat AC Sheeting	3m2	North	Good Condition (1)	Low (1)	Low Priority (2-3)
	4480/B00C/R1016/Wall Linings Internal/S4					Chrysotile (White asbestos)
B00C - R1017 - General Storeroom (10.98 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

Floor Coverings Res/Textile Vinyl Tiles
 4480/B00C/R0005/Floor Coverings Res/Textile/S3 **No Asbestos Detected**

B00C - R1018 - Stairs (9.02 m2)	No Asbestos
B00C - R1019 - Stairs (11.42 m2)	No Asbestos
B00C - R1020 - Home Base Store (5.65 m2)	No Asbestos
B00C - R1021 - Practical Activities - 1hb (8.57 m2)	No Asbestos
B00C - R1022 - Home Base (56.57 m2)	No Asbestos
B00C - R1023 - Home Base Store (6.74 m2)	No Asbestos
B00C - R1024 - Practical Activities - 1hb (11.06 m2)	No Asbestos
B00C - R1025 - Home Base (54.7 m2)	No Asbestos
B00C - R1026 - Home Base Store (7.45 m2)	No Asbestos
B00C - R1027 - Practical Activities - 1hb (12.2 m2)	No Asbestos
B00C - R1028 - Home Base (52.71 m2)	No Asbestos
B00C - R1029 - Home Base Store (7.43 m2)	No Asbestos
B00C - R1030 - Practical Activities - 1hb (12.27 m2)	No Asbestos
B00C - R1031 - Home Base (57.05 m2)	No Asbestos
B00C - R1032 - Home Base Store (6.88 m2)	No Asbestos
B00C - R1033 - Practical Activities - 1hb (11.28 m2)	No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00E - Library - 1984 - Brick/Block (Brick/Block)

Exterior

Roof	Bituminous membrane 4480/B00E/Roof/S19					No Asbestos Detected
Underfloor Voids - Slab on Ground	No Asbestos Found					
Ceiling Voids - Raked Ceiling	No Asbestos Found					

Interior

B00E - R0001 - Adjoining School (52.3 m2)

Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

B00E - R0002 - Adjoining School (13.55 m2)

No Asbestos

B00E - R0003 - Movement (54 m2)

Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

B00E - R0004 - Adjoining School (44.52 m2)

Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

Floor Coverings Res/Textile	Vinyl Tiles	45m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00E/R0005/Floor Coverings Res/Textile/S16 Chrysotile (white asbestos)						

Floor Coverings Res/Textile	Adhesive 4480/B00E/R0005/Floor Coverings Res/Textile/S24					No Asbestos Detected
-----------------------------	---	--	--	--	--	----------------------

B00E - R0005 - Adjoining School (74.79 m2)

Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

Floor Coverings Res/Textile	Vinyl Tiles	75m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
4480/B00E/R0005/Floor Coverings Res/Textile/S16 Chrysotile (white asbestos)						

Floor Coverings Res/Textile	Adhesive 4480/B00E/R0005/Floor Coverings Res/Textile/S24					No Asbestos Detected
-----------------------------	---	--	--	--	--	----------------------

B00E - R0006 - Adjoining School (11.45 m2)

Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

B00E - R0007 - Reading Area (398.64 m2)

Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

B00E - R0008 - Adjoining School (14.58 m2)

Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

B00E - R0009 - Adjoining School (18 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		
Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00E - R0010 - Toilets - Boys (9.2 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Partition Walls (Cubicles)	Compressed AC Sheet 4480/B00E/R0013/Partition Walls (Cubicles)/S17	5m2	East	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B00E - R0011 - Adjoining School (2.37 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Vinyl Tiles 4480/B00E/R0005/Floor Coverings Res/Textile/S16	3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive 4480/B00E/R0005/Floor Coverings Res/Textile/S24					No Asbestos Detected
B00E - R0012 - Movement (2.56 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00E - R0013 - Toilets - Girls (9.72 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Partition Walls (Cubicles)	Compressed AC Sheet 4480/B00E/R0013/Partition Walls (Cubicles)/S17	5m2	West	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B00E - R0014 - Movement (23.74 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00E - R0015 - Adjoining School (1.17 m2)						
Wall Linings Internal	Flat AC Sheeting 4480/B00E/R0015/Wall Linings Internal/S18					No Asbestos Detected
B00E - R0016 - Movement (2.51 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B00E/R0007/Ceiling Structures/Linings/S15					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00E - R0017 - Movement (26.74 m2)						
No Asbestos						
B00E - R0018 - Adjoining School (15.13 m2)						
No Asbestos						
B00E - R0019 - Adjoining School (0.69 m2)						
No Asbestos						
B00E - R1001 - Adjoining School (500.15 m2)						
No Asbestos						
B00E - R1002 - Adjoining School (12.97 m2)						
No Asbestos						
B00E - R1003 - Adjoining School (15.8 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00E - R1004 - Adjoining School (14.82 m2)						
No Asbestos						
B00E - R1005 - Adjoining School (31.24 m2)						
No Asbestos						
B00E - R1006 - Adjoining School (1.62 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4480/B00E/R0005/Floor Coverings Res/Textile/S16				Chrysotile (white asbestos)	
Floor Coverings Res/Textile	Adhesive					
	4480/B00E/R0005/Floor Coverings Res/Textile/S24				No Asbestos Detected	
B00E - R1007 - Adjoining School (0.77 m2)						
Wall Linings Internal	Flat AC Sheeting					
	4480/B00E/R0015/Wall Linings Internal/S18				No Asbestos Detected	
B00E - R2001 - Adjoining School (3.55 m2)						
No Asbestos						
B00E - R2002 - Adjoining School (18.91 m2)						
No Asbestos						
B00E - R2003 - Adjoining School (15.27 m2)						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B0DA - Administration - 1978 - Brick/Veneer (Brick/Veneer)**Exterior**

Roof	Bituminous membrane 4480/B0DA/Roof/S14					No Asbestos Detected
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior**B0DA - R0001 - Security Store (20.75 m2)**

Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
----------------------------	---	--	--	--	--	--

Floor Coverings Res/Textile	Vinyl Tiles 4480/B0DA/R0013/Floor Coverings Res/Textile/S11					No Asbestos Detected
-----------------------------	--	--	--	--	--	----------------------

B0DA - R0003 - Duplicating Workroom (38.12 m2)

Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
----------------------------	---	--	--	--	--	--

B0DA - R0004 - Clerical Office (45.03 m2)

Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
----------------------------	---	--	--	--	--	--

B0DA - R0005 - Movement (212.57 m2)

Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
----------------------------	---	--	--	--	--	--

B0DA - R0006 - Movement (10.48 m2)

Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
----------------------------	---	--	--	--	--	--

B0DA - R0007 - Movement (8.11 m2)

Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
----------------------------	---	--	--	--	--	--

B0DA - R0008 - Cleaning Supplies (5.13 m2)

Floor Coverings Res/Textile	Vinyl Tiles 4480/B0DA/R0013/Floor Coverings Res/Textile/S11					No Asbestos Detected
-----------------------------	--	--	--	--	--	----------------------

B0DA - R0009 - Distribution Board (0.74 m2)

Note: No inspection of live electrical installation.

Wall Linings Internal	Flat AC Sheeting 4480/B0DA/R0009/Wall Linings Internal/S13	4m2	Back of door	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Ceiling Structures/Linings	Flat AC Sheeting 4480/B0DA/R0009/Wall Linings Internal/S13	1m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)

B0DA - R0010 - Adjoining School (2.57 m2)

Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Partition Walls (Cubicles)	Compressed AC Sheet 4480/B0DA/R0010/Partition Walls (Cubicles)/S12	2m2	South	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)

B0DA - R0011 - Adjoining School (2.57 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Partition Walls (Cubicles)	Compressed AC Sheet 4480/B0DA/R0010/Partition Walls (Cubicles)/S12	3m2	South	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B0DA - R0012 - Adjoining School (15.39 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet) 4480/B0DA/R0013/Floor Coverings Res/Textile/S11					No Asbestos Detected
B0DA - R0013 - Adjoining School (8.11 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Vinyl Tiles 4480/B0DA/R0013/Floor Coverings Res/Textile/S11					No Asbestos Detected
B0DA - R0014 - Adjoining School (16.6 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Vinyl Tiles 4480/B0DA/R0013/Floor Coverings Res/Textile/S11					No Asbestos Detected
B0DA - R0015 - Main Switch Board (10.46 m2)						
Electrical Backing Board	Resinous Board	3Unit	North	Good Condition (1)	Low (1)	Low Priority (2-3) Assumed Asbestos - Electrical Hazard
B0DA - R0016 - External Movement (129.68 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B0DA - R0033 - Other (9.99 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B0DA - R0036 - Other (1.96 m2)						
Floor Coverings Res/Textile	Vinyl Tiles 4480/B0DA/R0013/Floor Coverings Res/Textile/S11					No Asbestos Detected
B0DA - R0037 - Other (12.9 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B0DA - R0038 - External Movement (37.9 m2)						
No Asbestos						
B0DA - R0039 - Movement (10.68 m2)						
No Asbestos						
B0DA - R0040 - Principal (11.34 m2)						
Ceiling Structures/Linings	Vermiculite 4480/B0DA/R0013/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	4480/B0DA/R0013/Floor Coverings Res/Textile/S11				No Asbestos Detected
B0DA - R0041 - General Storeroom (6.62 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	4480/B0DA/R0013/Floor Coverings Res/Textile/S11				No Asbestos Detected
B0DA - R0042 - Sick Bay (5.79 m2)						
Ceiling Structures/Linings	Vermiculite	4480/B0DA/R0013/Ceiling Structures/Linings/S10				Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B0DA - R0043 - Movement (11.38 m2)						
Ceiling Structures/Linings	Vermiculite	4480/B0DA/R0013/Ceiling Structures/Linings/S10				Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B0DA - R0044 - Clerical Office (54.95 m2)						
Ceiling Structures/Linings	Vermiculite	4480/B0DA/R0013/Ceiling Structures/Linings/S10				Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	4480/B0DA/R0013/Floor Coverings Res/Textile/S11				No Asbestos Detected
B0DA - R0045 - Clerical Office (11.17 m2)						
Ceiling Structures/Linings	Vermiculite	4480/B0DA/R0013/Ceiling Structures/Linings/S10				Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	4480/B0DA/R0013/Floor Coverings Res/Textile/S11				No Asbestos Detected
B0DA - R0046 - Duplicating Workroom (26.99 m2)						
Ceiling Structures/Linings	Vermiculite	4480/B0DA/R0013/Ceiling Structures/Linings/S10				Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B0DA - R0047 - General Storeroom (15.28 m2)						
Ceiling Structures/Linings	Vermiculite	4480/B0DA/R0013/Ceiling Structures/Linings/S10				Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B0DA - R0048 - Staff Kitchen (8.06 m2)						
Ceiling Structures/Linings	Vermiculite	4480/B0DA/R0013/Ceiling Structures/Linings/S10				Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B0DA - R0049 - Movement (0.84 m2)						
No Asbestos						
B0DA - R1001 - Staff Room (269.5 m2)						
No Asbestos						
B0DA - R1002 - Adjoining School (36.39 m2)						
No Asbestos						
B0DA - R1006 - Adjoining School (25.97 m2)						
No Asbestos						
B0DA - R1007 - Adjoining School (14.12 m2)						
No Asbestos						
B0DA - R1009 - Movement (132.03 m2)						
No Asbestos						
B0DA - R1010 - Adjoining School (18.55 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

No Asbestos

B0DA - R1011 - Adjoining School (8.63 m2)

No Asbestos

B0DA - R1012 - Adjoining School (15.25 m2)

No Asbestos

B0DA - R1031 - Interview (15.17 m2)

No Asbestos

B0DA - R1032 - Other (14.1 m2)

No Asbestos

B0DA - R1033 - General Storeroom (12.85 m2)

No Asbestos

B0DA - R1034 - Other (25.06 m2)

No Asbestos

B0DA - R1035 - Other (24.84 m2)

No Asbestos

B0DA - R1036 - Other (0.76 m2)

Wall Linings Internal	Flat AC Sheeting	4m2	Back of door	Good Condition (1)	Low (1)	Low Priority (2-3)
-----------------------	------------------	-----	--------------	--------------------	---------	--------------------

4480/B0DA/R0009/Wall Linings Internal/S13

Chrysotile (white asbestos)

Ceiling Structures/Linings	Flat AC Sheeting	1m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
----------------------------	------------------	-----	------------	--------------------	---------	--------------------

4480/B0DA/R0009/Wall Linings Internal/S13

Chrysotile (white asbestos)

B0DA - R1037 - Staff Toilet (9.74 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	4m2	North	Good Condition (1)	Low (1)	Low Priority (2-3)
----------------------------	---------------------	-----	-------	--------------------	---------	--------------------

4480/B0DA/R0010/Partition Walls (Cubicles)/S12

Chrysotile (white asbestos)

B0DA - R1038 - Other (2.27 m2)

No Asbestos

B0DA - R1039 - Staff Toilet (11.52 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	4m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
----------------------------	---------------------	-----	-------	--------------------	---------	--------------------

4480/B0DA/R0010/Partition Walls (Cubicles)/S12

Chrysotile (white asbestos)

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B0DB - Other-Community Use - 1976 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids - Raked Ceiling No Asbestos Found

Underfloor Voids - Slab on Ground No Asbestos Found

Interior

B0DB - R0001 - External Movement (49.58 m2)

No Asbestos

B0DB - R0002 - Community Clinic (33.84 m2)

No Asbestos

B0DB - R0003 - Staff Toilet (3.56 m2)

No Asbestos

B0DB - R0004 - Staff Toilet (2.09 m2)

No Asbestos

B0DB - R0005 - Cleaning Distributed Store (1.6 m2)

Floor Coverings Res/Textile Vinyl Tiles
4480/B0DB/R0006/Floor Coverings Res/Textile/S9

No Asbestos Detected

B0DB - R0006 - Staff Kitchen (9.71 m2)

Floor Coverings Res/Textile Vinyl Tiles
4480/B0DB/R0006/Floor Coverings Res/Textile/S9

No Asbestos Detected

B0DB - R0007 - Distribution Board (0.58 m2)

Note: No inspection of live electrical installation.

Wall Linings Internal Flat AC Sheeting 3m2 back of doors Good Condition (1) Low (1) Low Priority (2-3)
4480/B0DB/R0007/Wall Linings Internal/S20

Chrysotile (white asbestos)

Ceiling Structures/Linings Flat AC Sheeting 1m2 Throughout Good Condition (1) Medium (2) Low Priority (2-3)
4480/B0DB/R0007/Wall Linings Internal/S20

Chrysotile (white asbestos)

B0DB - R0008 - Sick Bay (30.22 m2)

No Asbestos

B0DB - R0009 - General Storeroom (4.48 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Demountables

There are no Demountable(s) located at this school as per the AMS records as of 15 Feb 2017.

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Listing of Electronic Attachments as of 22/03/2017

There are no asbestos related file attachment(s) for this school.

2017
