


# Asbestos Register

(Hazardous Materials and Risk Assessment)

**School :** Katoomba High School (8150)  
**Region :** Western Sydney  
**State Electorate :** Blue Mountains  
**Local Government Area :** Blue Mountains

**Initial Survey :** Noel Arnold & Associates : 23 - May - 2008  
**Reviewed By :** Parsons Brinckerhoff : 06 - Mar - 2015

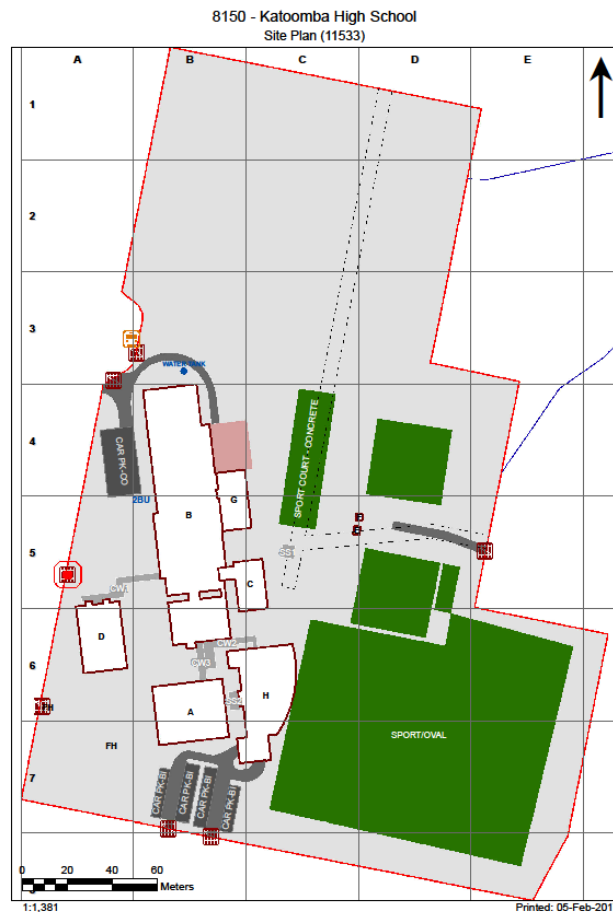

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00A - Library/Science - 1978 - Brick/Block (Brick/Block)**

**Exterior**

Ceiling Voids	No Asbestos Found
Underfloor Voids	No Asbestos Found

**Interior**

**B00A - M1001 - Main Area (181.99 m2)**

No Asbestos

**B00A - M1002 - Lift (1.69 m2)**

No Asbestos

**B00A - M1003 - Stairs (6.76 m2)**

No Asbestos

**B00A - R0001 - Laboratory L.S. (92.85 m2)**

Floor Coverings Res/Textile	Vinyl Tiles					
		8150/B00A/R0001/Floor Coverings Res/Textile/S7				<b>No Asbestos Detected</b>

**B00A - R0002 - Preparation (54.9 m2)**

Floor Coverings Res/Textile	Vinyl Tiles					
		8150/B00A/R0001/Floor Coverings Res/Textile/S7				<b>No Asbestos Detected</b>

**B00A - R0003 - Laboratory L.S. (94.36 m2)**

Floor Coverings Res/Textile	Vinyl Tiles					
		8150/B00A/R0001/Floor Coverings Res/Textile/S7				<b>No Asbestos Detected</b>

**B00A - R0004 - Laboratory L.S. (94.37 m2)**

Floor Coverings Res/Textile	Vinyl Tiles					
		8150/B00A/R0001/Floor Coverings Res/Textile/S7				<b>No Asbestos Detected</b>

**B00A - R0006 - Laboratory L.S. (92.86 m2)**

Floor Coverings Res/Textile	Vinyl Tiles					
		8150/B00A/R0001/Floor Coverings Res/Textile/S7				<b>No Asbestos Detected</b>

**B00A - R0007 - Apparatus Store (24.63 m2)**

No Asbestos

**B00A - R0008 - Main Switchroom (9.21 m2)**

No Asbestos

**B00A - R0009 - Movement (160.89 m2)**

No Asbestos

**B00A - R0010 - Preparation (47.65 m2)**

Floor Coverings Res/Textile	Vinyl Tiles					
		8150/B00A/R0001/Floor Coverings Res/Textile/S7				<b>No Asbestos Detected</b>

**B00A - R0011 - Chemical Store (6.44 m2)**

Floor Coverings Res/Textile	Vinyl Tiles					
		8150/B00A/R0001/Floor Coverings Res/Textile/S7				<b>No Asbestos Detected</b>

**B00A - R0012 - Stairs (17.19 m2)**

No Asbestos

**B00A - R1001 - Movement (44.4 m2)**

No Asbestos

**B00A - R1002 - Staff Study (35.57 m2)**

No Asbestos

**B00A - R1003 - Staff - Toilet (8.06 m2)**

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result
						No Asbestos
						<b>B00A - R1004 - Cleaning Store - Distributed (2.86 m2)</b>
						No Asbestos
						<b>B00A - R1005 - Staff - Toilet (11.41 m2)</b>
						No Asbestos
						<b>B00A - R1006 - Staff - Toilet (3.36 m2)</b>
						No Asbestos
						<b>B00A - R1007 - Workroom (37.33 m2)</b>
						No Asbestos
						<b>B00A - R1008 - Workroom (36.81 m2)</b>
						No Asbestos
						<b>B00A - R1009 - Administration - Clerical (10.92 m2)</b>
						No Asbestos
						<b>B00A - R1010 - Librarian (11.2 m2)</b>
						No Asbestos
						<b>B00A - R1011 - Computer Learning Space (35.5 m2)</b>
						No Asbestos
						<b>B00A - R1012 - Workroom (19.93 m2)</b>
						No Asbestos
						<b>B00A - R1013 - Distribution Board Cupboard (0.63 m2)</b> <span style="float: right;">Note: No inspection of live electrical installation.</span>
						No Asbestos
						<b>B00A - R1014 - Seminar (14.99 m2)</b>
						No Asbestos
						<b>B00A - R1015 - Seminar (14.52 m2)</b>
						No Asbestos
						<b>B00A - R1016 - Seminar (14.92 m2)</b>
						No Asbestos
						<b>B00A - R1018 - Lift (1.69 m2)</b>
						No Asbestos
						<b>B00A - R1019 - Stairs (2.7 m2)</b>
						No Asbestos
						<b>B00A - R1020 - Main Area (397.98 m2)</b>
						No Asbestos
						<b>B00A - R1021 - Stairs (16.96 m2)</b>
						No Asbestos
						<b>B00A - R9001 - General Storeroom (111.48 m2)</b>
						No Asbestos
						<b>B00A - R9002 - Movement (17.19 m2)</b>
						No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

**B00B - Administration/Various - 1962 - Brick/Veneer (Brick/Veneer)****Exterior**

Underfloor Voids	No Asbestos Found					
Ceiling Voids	Vermiculite 8150/B00B/Ceiling Voids/S12					Limited Samples Taken

*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**Interior****B00B - R0001 - Music Store (17.4 m2)**

No Asbestos

**B00B - R0002 - Practice/Seminar (11.09 m2)**

No Asbestos

**B00B - R0003 - Distribution Board Cupboard (0.41 m2)**

Note: No inspection of live electrical installation.

Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
----------------------------	--	--	--	--	--	-----------------------

*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R0004 - Music Learning Space (59.2 m2)**

Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
----------------------------	--	--	--	--	--	-----------------------

*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R0005 - Music Learning Space (56.1 m2)**

Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
----------------------------	--	--	--	--	--	-----------------------

*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R0006 - Music Store (12.05 m2)**

Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
----------------------------	--	--	--	--	--	-----------------------

*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R0007 - Self Help Toilet (24.25 m2)**

Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
----------------------------	--	--	--	--	--	-----------------------

*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R0008 - Movement (97.9 m2)**

Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
----------------------------	--	--	--	--	--	-----------------------

*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R0009 - Staff - Toilet (10.8 m2)**

Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
----------------------------	--	--	--	--	--	-----------------------

*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R0010 - Laboratory L.S. (83.7 m2)**

Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
----------------------------	--	--	--	--	--	-----------------------

*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R0011 - Preparation (22.89 m2)**

Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
----------------------------	--	--	--	--	--	-----------------------

*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R0012 - Apparatus Store (8.23 m2)**

Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
----------------------------	--	--	--	--	--	-----------------------

*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R0013 - Materials Technology L.S. (70.79 m2)**

No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
<b>B00B - R0014 - Materials Store (18.72 m2)</b>						
No Asbestos						
<b>B00B - R0015 - Dust Extraction Space (4.42 m2)</b>						
No Asbestos						
<b>B00B - R0016 - Materials Store (14.1 m2)</b>						
No Asbestos						
<b>B00B - R0017 - Materials Technology L.S. (92.72 m2)</b>						
No Asbestos						
<b>B00B - R0018 - Movement (3.83 m2)</b>						
Ceiling Structures/Linings	Vermiculite		8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Tiles		8150/B00B/R0018/Floor Coverings Res/Textile/S2			No Asbestos Detected
<b>B00B - R0019 - Movement (51.85 m2)</b>						
Ceiling Structures/Linings	Vermiculite		8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Tiles		8150/B00B/R0018/Floor Coverings Res/Textile/S2			No Asbestos Detected
<b>B00B - R0020 - Materials Technology L.S. (100.91 m2)</b>						
No Asbestos						
<b>B00B - R0021 - Welding Area (6.37 m2)</b>						
No Asbestos						
<b>B00B - R0023 - Materials Store (17.22 m2)</b>						
No Asbestos						
<b>B00B - R0025 - Materials Technology L.S. (99.76 m2)</b>						
No Asbestos						
<b>B00B - R0026 - Movement (32.15 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles		8150/B00B/R0018/Floor Coverings Res/Textile/S2			No Asbestos Detected
<b>B00B - R0027 - Cleaning Store - Distributed (8.52 m2)</b>						
No Asbestos						
<b>B00B - R0028 - Movement (11.45 m2)</b>						
No Asbestos						
<b>B00B - R0029 - General Storeroom (21.69 m2)</b>						
No Asbestos						
<b>B00B - R0030 - Maintenance Bulk Store (50.07 m2)</b>						
No Asbestos						
<b>B00B - R0031 - Movement (385.2 m2)</b>						
No Asbestos						
<b>B00B - R0032 - Materials Store (15.66 m2)</b>						
No Asbestos						
<b>B00B - R0033 - Cleaning Supplies Store (36.32 m2)</b>						
No Asbestos						
<b>B00B - R0034 - Toilets-Boys (54.48 m2)</b>						
Partition Walls (Cubicles)	Compressed AC Sheet		8150/B00B/R0034/Partition Walls (Cubicles)/S4			No Asbestos Detected

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
<b>B00B - R0035 - Movement (249.44 m2)</b>						
No Asbestos						
<b>B00B - R0036 - Toilets-Girls (60.6 m2)</b>						
Partition Walls (Cubicles)		Compressed AC Sheet				
		8150/B00B/R0034/Partition Walls (Cubicles)/S4				<b>No Asbestos Detected</b>
<b>B00B - R0038 - Movement (28.68 m2)</b>						
No Asbestos						
<b>B00B - R0039 - Movement (191.29 m2)</b>						
No Asbestos						
<b>B00B - R0040 - General Storeroom (16.85 m2)</b>						
No Asbestos						
<b>B00B - R0041 - General Assistants (34.45 m2)</b>						
No Asbestos						
<b>B00B - R0042 - Cleaning Supplies Store (15.92 m2)</b>						
No Asbestos						
<b>B00B - R0043 - Main Switchroom (4.87 m2)</b>						
No Asbestos						
<b>B00B - R0044 - General Storeroom (20.85 m2)</b>						
No Asbestos						
<b>B00B - R0045 - Sport Equipment Store (12.66 m2)</b>						
No Asbestos						
<b>B00B - R0046 - Cleaning Store - Distributed (5.15 m2)</b>						
No Asbestos						
<b>B00B - R0048 - Shower/Change (55.99 m2)</b>						
No Asbestos						
<b>B00B - R0049 - Sport Equipment Store (5.78 m2)</b>						
No Asbestos						
<b>B00B - R0050 - Movement (7.77 m2)</b>						
No Asbestos						
<b>B00B - R0051 - Sport Equipment Store (7.94 m2)</b>						
No Asbestos						
<b>B00B - R0052 - Shower/Change (56.77 m2)</b>						
No Asbestos						
<b>B00B - R0053 - Sport Equipment Store (5.82 m2)</b>						
No Asbestos						
<b>B00B - R0054 - Student Canteen (41.4 m2)</b>						
Floor Coverings Res/Textile		Vinyl Tiles				
		8150/B00B/R0053/Floor Coverings Res/Textile/S5				<b>No Asbestos Detected</b>
<b>B00B - R0055 - General Storeroom (2.41 m2)</b>						
Floor Coverings Res/Textile		Vinyl Tiles				
		8150/B00B/R0053/Floor Coverings Res/Textile/S5				<b>No Asbestos Detected</b>
<b>B00B - R0056 - Staff - Toilet (4.97 m2)</b>						
Floor Coverings Res/Textile		Vinyl Tiles				
		8150/B00B/R0053/Floor Coverings Res/Textile/S5				<b>No Asbestos Detected</b>
<b>B00B - R0057 - Distribution Board Cupboard (0.15 m2)</b>						
						Note: No inspection of live electrical installation.
No Asbestos						
<b>B00B - R0058 - Lift (1.62 m2)</b>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
No Asbestos						
<b>B00B - R0059 - Plant (3.28 m2)</b>						
No Asbestos						
<b>B00B - R0060 - Movement (12.97 m2)</b>						
No Asbestos						
<b>B00B - R0061 - Other-Vacant (10.29 m2)</b>						
No Asbestos						
<b>B00B - R0062 - Movement (55.21 m2)</b>						
No Asbestos						
<b>B00B - R0063 - Movement (51.61 m2)</b>						
No Asbestos						
<b>B00B - R0064 - Movement (85.32 m2)</b>						
No Asbestos						
<b>B00B - R0065 - Movement (107.48 m2)</b>						
No Asbestos						
<b>B00B - R0066 - Plant (6.08 m2)</b>						
No Asbestos						
<b>B00B - R0067 - Stairs (6.16 m2)</b>						
No Asbestos						
<b>B00B - R0068 - Stairs (2.44 m2)</b>						
No Asbestos						
<b>B00B - R0069 - General Storeroom (14.33 m2)</b>						
No Asbestos						
<b>B00B - R0070 - General Storeroom (8.69 m2)</b>						
Electrical Backing Board	Resinous Board	1m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8150/B00B/R0070/Electrical Backing Board/S15					<b>Chrysotile (white asbestos)</b>	
<b>B00B - R0071 - Stairs (5.46 m2)</b>						
No Asbestos						
<b>B00B - R0072 - Stairs (5.24 m2)</b>						
No Asbestos						
<b>B00B - R0073 - Stairs (10.62 m2)</b>						
No Asbestos						
<b>B00B - R0074 - Stairs (10.62 m2)</b>						
No Asbestos						
<b>B00B - R0075 - Materials Technology L.S. (20.08 m2)</b>						
No Asbestos						
<b>B00B - R0076 - Welding/Hot Metals Area (5.75 m2)</b>						
No Asbestos						
<b>B00B - R0077 - Welding/Hot Metals Area (6 m2)</b>						
No Asbestos						
<b>B00B - R1004 - General Learning Space (67.16 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						
<b>B00B - R1006 - Design L.S. (66.98 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						
<b>B00B - R1007 - Staff Study (32.98 m2)</b>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1008 - Design L.S. (66.98 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1009 - General Learning Space (66.97 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1010 - General Learning Space (66.98 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1011 - General Learning Space (66.98 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1012 - Staff Study (32.89 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1013 - General Storeroom (3.01 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1014 - Commonroom (135.65 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1015 - Cleaning Store - Distributed (3.01 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1017 - Administration - Clerical (13.62 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1018 - Movement (12.75 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1019 - Careers Advisers Office (19.16 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1020 - Staff - Toilet (9.35 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1021 - Clinic - Boys (10.36 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						



Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
<b>B00B - R1024 - General Storeroom (2.72 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1025 - Staff - Toilet (3.14 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1026 - Principal Office (20.38 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1027 - Public Entry (8.14 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1033 - Bulk Store (15.14 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1034 - Darkroom Space (11.71 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1035 - Art Learning Space (80.09 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1036 - Preparation (21.9 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1037 - Preparation (15.13 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1038 - Performance Workshop (96.49 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1039 - Laboratory L.S. (97.31 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1040 - Preparation (26.47 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1050 - General Learning Space (55.7 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R1051 - Cleaning Store - Distributed (2.85 m2)</b>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1052 - General Learning Space (59.96 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1053 - Resources Store (9.77 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1054 - General Storeroom (5.35 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1058 - Computer Learning Space (68.67 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1059 - Movement (2.69 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1060 - Computer Resource (10.55 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1061 - General Storeroom (6.73 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1062 - Leading Teacher (20.34 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1063 - Deputy Principal Office (13.74 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1064 - Pupil Entry (12.45 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1065 - Distribution Board Cupboard (0.41 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1				Note: No inspection of live electrical installation.	Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Wall Linings Internal	Flat AC Sheeting 8150/B00B/R1065/Wall Linings Internal/S6	3m2	Throughout	Some Damage / Unsealed (3)	Low (1)	Low Priority (2-3)  Chrysotile (white asbestos)
<b>B00B - R1066 - Lift (1.62 m2)</b>						
No Asbestos						
<b>B00B - R1068 - Toilets-Disabled (3.73 m2)</b>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
<b>B00B - R1069 - Toilets-Disabled (10.12 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
<b>B00B - R1070 - Main Entry (23.53 m2)</b>						
Ceiling Structures/Linings	Flat AC Sheeting					
	8150/B00B/R1070/Ceiling Structures/Linings/S16					No Asbestos Detected
Floor Coverings Res/Textile	Vinyl Tiles	23m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8150/B00B/R1070/Floor Coverings Res/Textile/S17					Chrysotile (white asbestos)
<b>B00B - R1071 - Administration - Clerical (103.09 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	103m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8150/B00B/R1071/Floor Coverings Res/Textile/S18					Chrysotile (white asbestos)
<b>B00B - R1072 - Administration - Executive (18.22 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	18m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8150/B00B/R1072/Floor Coverings Res/Textile/S19					Chrysotile (white asbestos)
<b>B00B - R1073 - Duplicating Workroom (22.73 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	23m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8150/B00B/R1073/Floor Coverings Res/Textile/S20					Chrysotile (white asbestos)
<b>B00B - R1074 - Secure Storeroom (7.69 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	8m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8150/B00B/R1074/Floor Coverings Res/Textile/S21					Chrysotile (white asbestos)
<b>B00B - R1075 - Movement (13.04 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	13m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8150/B00B/R1075/Floor Coverings Res/Textile/S22					Chrysotile (white asbestos)
<b>B00B - R1076 - Clinic (8.82 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	9m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8150/B00B/R1076/Floor Coverings Res/Textile/S23					Chrysotile (white asbestos)
<b>B00B - R1077 - Clinic (5.8 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8150/B00B/R1077/Floor Coverings Res/Textile/S24					Chrysotile (white asbestos)
<b>B00B - R1078 - Toilets-Boys/Girls (2.07 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8150/B00B/R1078/Floor Coverings Res/Textile/S25					Chrysotile (white asbestos)
<b>B00B - R1079 - Toilets-Boys/Girls (3.21 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8150/B00B/R1079/Floor Coverings Res/Textile/S26					Chrysotile (white asbestos)
<b>B00B - R1080 - Toilets-Disabled (5.3 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8150/B00B/R1080/Floor Coverings Res/Textile/S27					Chrysotile (white asbestos)
<b>B00B - R1081 - Plant (1.75 m2)</b>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		
Floor Coverings Res/Textile	Vinyl Tiles	2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8150/B00B/R1081/Floor Coverings Res/Textile/S28				<b>Chrysotile (white asbestos)</b>		
<b>B00B - R1083 - Office/Store (12.96 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	13m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8150/B00B/R1083/Floor Coverings Res/Textile/S30				<b>Chrysotile (white asbestos)</b>		
<b>B00B - R1084 - Uniform Shop (19.5 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	20m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8150/B00B/R1084/Floor Coverings Res/Textile/S31				<b>Chrysotile (white asbestos)</b>		
<b>B00B - R1085 - Careers Advisers Office (12.86 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	13m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8150/B00B/R1085/Floor Coverings Res/Textile/S32				<b>Chrysotile (white asbestos)</b>		
<b>B00B - R1086 - Careers Advisers Office (19.68 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	20m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8150/B00B/R1086/Floor Coverings Res/Textile/S33				<b>Chrysotile (white asbestos)</b>		
<b>B00B - R1087 - Stairs (29.77 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	29m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8150/B00B/R1087/Floor Coverings Res/Textile/S34				<b>Chrysotile (white asbestos)</b>		
<b>B00B - R1088 - Stairs (21.61 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	22m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8150/B00B/R1088/Floor Coverings Res/Textile/S35				<b>Chrysotile (white asbestos)</b>		
<b>B00B - R1089 - Stairs (21.61 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles	22m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8150/B00B/R1089/Floor Coverings Res/Textile/S36				<b>Chrysotile (white asbestos)</b>		
<b>B00B - R1091 - Stairs (30.39 m2)</b>						
No Asbestos						
<b>B00B - R1092 - Hospitality Space (52.5 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R1094/Ceiling Structures/Linings/S43			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						
<b>B00B - R1093 - Preparation/Printing (24.24 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R1094/Ceiling Structures/Linings/S43			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						
<b>B00B - R1094 - Food Technology L.S. (103.31 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R1094/Ceiling Structures/Linings/S43			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						
<b>B00B - R1095 - Movement (4.52 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R1094/Ceiling Structures/Linings/S43			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						
<b>B00B - R1096 - Toilets-Girls (4.02 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R1094/Ceiling Structures/Linings/S43			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						
<b>B00B - R1097 - Toilets-Boys (4.07 m2)</b>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite 8150/B00B/R1094/Ceiling Structures/Linings/S43					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1098 - Pantry (15.53 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R1094/Ceiling Structures/Linings/S43					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1099 - Laundry (8.02 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R1094/Ceiling Structures/Linings/S43					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1100 - Movement (5.12 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R1094/Ceiling Structures/Linings/S43					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1101 - Movement (296.63 m2)</b>						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet) 8150/B00B/R1101/Floor Coverings Res/Textile/S42	297m2	Throughout	Minimal Damage (2)	Low (1)	Low Priority (2-3) <b>Chrysotile (white asbestos)</b>
Ceiling Structures/Linings	Vermiculite 8150/B00B/R1094/Ceiling Structures/Linings/S43					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R1102 - Kitchen - Type 1 (120.18 m2)</b>						
Recently Modified Space	Requires Inspection					
<b>B00B - R1103 - Movement (51.68 m2)</b>						
Recently Modified Space	Requires Inspection					
<b>B00B - R1104 - Movement (31.64 m2)</b>						
Recently Modified Space	Requires Inspection					
<b>B00B - R2001 - Stage (24.43 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R2002 - Performance Workspace (53.45 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R2003 - Secure Storeroom (6.14 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R2004 - General Storeroom (9.35 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R2005 - General Learning Space (53.45 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R2006 - General Learning Space (66.91 m2)</b>						
Ceiling Structures/Linings	Vermiculite 8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
<b>B00B - R2007 - General Learning Space (66.9 m2)</b>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2008 - General Learning Space (66.91 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2009 - General Learning Space (66.9 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2010 - General Learning Space (66.9 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2011 - Staff Study (36.14 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2012 - General Learning Space (53.89 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2013 - General Learning Space (40.11 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2014 - General Learning Space (40.24 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2015 - Cleaning Store - Distributed (2.99 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2016 - General Learning Space (53.89 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2017 - General Storeroom (9.34 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2018 - General Learning Space (52.69 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2019 - Sport Equipment Store (9.97 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2020 - Interview/Office - Type 1 (10.09 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
<b>B00B - R2021 - Administration - Clerical (9.56 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2022 - Administration - Clerical (44.22 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2023 - Staff - Toilet (3.22 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2024 - Ancillary Staff (5.11 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2025 - Staff - Toilet (4.34 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2026 - Duplicating Workroom (15.09 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2027 - Duplicating Workroom (16.41 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2030 - Distribution Board Cupboard (0.14 m2)</b>						
					Note: No inspection of live electrical installation.	
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2033 - Kiln Space (5.05 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2035 - General Storeroom (15.67 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2036 - Resources Store (6.22 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2037 - Art Learning Space (100.97 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2038 - Resources Store (4.5 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
		8150/B00B/R0018/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2039 - Art Learning Space (53.89 m2)</b>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2040 - Movement (3.17 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2041 - Staff Study (20.01 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2042 - General Storeroom (2.99 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2043 - General Learning Space (67.6 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2044 - General Learning Space (66.7 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2045 - General Storeroom (3.82 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2046 - General Storeroom (3.82 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2047 - Computer Resource (8.23 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2048 - Staff Study (65.31 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2049 - Staff Study (23.98 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2050 - Movement (388.53 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2051 - General Learning Space (62.89 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2052 - General Learning Space (59.66 m2)</b>						
Ceiling Structures/Linings	Vermiculite	8150/B00B/R0018/Ceiling Structures/Linings/S1			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						



Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
<b>B00B - R2053 - General Storeroom (12.27 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2054 - Interview/Office - Type 1 (28.1 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2055 - Staff Study (40.18 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2056 - General Learning Space (70.23 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2057 - General Storeroom (13.5 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2058 - Computer Learning Space (12.23 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2059 - Movement (73.43 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2060 - Distribution Board Cupboard (0.41 m2)</b>						
Note: No inspection of live electrical installation.						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R0018/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Wall Linings Internal	Flat AC Sheeting	3m2	Throughout	Some Damage / Unsealed (3)	Low (1)	Low Priority (2-3)
	8150/B00B/R1065/Wall Linings Internal/S6					Chrysotile (white asbestos)
<b>B00B - R2061 - Lift (1.62 m2)</b>						
No Asbestos						
<b>B00B - R2062 - Stairs (6.22 m2)</b>						
Ceiling Structures/Linings	Vermiculite	6m2	Throughout	Friable Asbestos (5)	Medium (2)	High Priority (6-8)
	8150/B00B/R2062/Ceiling Structures/Linings/S37					Chrysotile (white asbestos)
<b>B00B - R2063 - Stairs (6.24 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R2063/Ceiling Structures/Linings/S38					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2064 - Stairs (6.24 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R2064/Ceiling Structures/Linings/S39					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2065 - Stairs (6.24 m2)</b>						
Ceiling Structures/Linings	Vermiculite					
	8150/B00B/R2065/Ceiling Structures/Linings/S40					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
<b>B00B - R2066 - Stairs (20.71 m2)</b>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Ceiling Structures/Linings Vermiculite  
 8150/B00B/R2066/Ceiling Structures/Linings/S41 **Limited Samples Taken**  
*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R2067 - Stairs (20.78 m2)**

Ceiling Structures/Linings Vermiculite  
 8150/B00B/R2067/Ceiling Structures/Linings/S11 **Limited Samples Taken**  
*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00B - R2068 - Staff Study (49.52 m2)**

Recently Modified Space Requires Inspection

**B00B - R2069 - General Learning Space (49.75 m2)**

Recently Modified Space Requires Inspection

**B00B - R2070 - General Learning Space (66.79 m2)**

Recently Modified Space Requires Inspection

**B00B - R2071 - General Learning Space (50.1 m2)**

Recently Modified Space Requires Inspection

**B00B - R2072 - General Learning Space (61.13 m2)**

Recently Modified Space Requires Inspection

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00C - Physical Education - 1962 - Brick/Veneer (Brick/Veneer)**

**Exterior**

Eaves Linings	Flat AC Sheeting 8150/B00C/Eaves Linings/S43					<b>No Asbestos Detected</b>
Ceiling Voids	No Asbestos Found					
Underfloor Voids	No Asbestos Found					
Window putty	Mastic 8150/B00C/Window putty/S44	400m	Throughout	Minimal Damage (2)	Low (1)	Low Priority (2-3) <b>Chrysotile (white asbestos)</b>

**Interior**

**B00C - R0001 - Movement (23.26 m2)**

No Asbestos

**B00C - R0002 - Staff - Toilet (4.05 m2)**

No Asbestos

**B00C - R0003 - Sport Equipment Store (8.76 m2)**

No Asbestos

**B00C - R0004 - Gymnasium (263.59 m2)**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

**B00D - Performing Arts - 1962 - Brick/Block (Brick/Block)****Exterior**

Ceiling Voids	No Asbestos Found
Underfloor Voids	No Asbestos Found

**Interior****B00D - M0001 - Control Room (22.12 m2)**

No Asbestos

**B00D - M0002 - Chair Store (22.12 m2)**

No Asbestos

**B00D - R0001 - Cleaning Store - Distributed (3.65 m2)**

No Asbestos

**B00D - R0002 - Chair Store (3.65 m2)**

No Asbestos

**B00D - R0004 - Staff Kitchen (10.72 m2)**

No Asbestos

**B00D - R0005 - General Storeroom (4.23 m2)**

No Asbestos

**B00D - R0007 - Performing Arts Store (15.05 m2)**

No Asbestos

**B00D - R0011 - Stairs (6.41 m2)**

No Asbestos

**B00D - R0012 - Stairs (6.44 m2)**

No Asbestos

**B00D - R0013 - Stage (111.47 m2)**

No Asbestos

**B00D - R0014 - Multi-Purpose Space (374.81 m2)**

No Asbestos

**B00D - R0015 - Movement (2.06 m2)**

No Asbestos

**B00D - R0016 - Lift (1.15 m2)**

No Asbestos

**B00D - R9001 - General Storeroom (4.1 m2)**

No Asbestos

**B00D - R9002 - Shower/Change (36.34 m2)**

No Asbestos

**B00D - R9003 - Gymnasium (44.18 m2)**

No Asbestos

**B00D - R9004 - Shower/Change (36.33 m2)**

No Asbestos

**B00D - R9005 - General Storeroom (4.1 m2)**

No Asbestos

**B00D - R9006 - Stairs (2.11 m2)**

No Asbestos

**B00D - R9007 - Stairs (2.21 m2)**

No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00E - Building Services - 2001 - Brick/Block (Brick/Block)**

**Exterior**

Ceiling Voids            No Asbestos Found

Underfloor Voids        No Asbestos Found

**Interior**

**B00E - R0001 - General Assistants (9.36 m2)**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00F - Building Services - 2001 - Brick/Block (Brick/Block)**

**Exterior**

Ceiling Voids	No Asbestos Found
Underfloor Voids	No Asbestos Found

**Interior**

**B00F - R0001 - Cleaning Supplies Store (7.84 m2)**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00G - Pupil Facilities - 2003 - Brick/Veneer (Brick/Veneer)**

**Exterior**

Ceiling Voids	No Asbestos Found
Underfloor Voids	No Asbestos Found

**Interior**

**B00G - R0001 - Covered Area (289.06 m2)**

No Asbestos

**B00G - R0002 - Movement (40.14 m2)**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

**B00H - Support Unit - 1962 - Brick/Veneer (Brick/Veneer)****Exterior**

Ceiling Voids	No Asbestos Found
Underfloor Voids	No Asbestos Found

**Interior****B00H - R0001 - Practical Activity Area (17.26 m2)**

No Asbestos

**B00H - R0002 - General Learning Space - S/P (46.2 m2)**

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

**B00H - R0003 - Seminar - Type 3 (8.74 m2)**

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

**B00H - R0004 - Home Base Store - S (8.16 m2)**

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

**B00H - R0005 - Practical Activity Area (79.43 m2)**

No Asbestos

**B00H - R0006 - Practical Activity Area (16.64 m2)**

No Asbestos

**B00H - R0007 - General Learning Space - S/P (48.04 m2)**

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

**B00H - R0008 - Seminar - Type 3 (8.3 m2)**

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

**B00H - R0009 - Home Base Store - S (7.93 m2)**

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

**B00H - R0010 - Staff - Toilet (6.41 m2)**

No Asbestos

**B00H - R0011 - Wheelchair Store-Special Ed (61.14 m2)**

No Asbestos

**B00H - R0012 - Covered Vehicle Area/Porte Cochere (143.7 m2)**

No Asbestos

**B00H - R0013 - Distribution Board Cupboard (0.69 m2)**

Note: No inspection of live electrical installation.

No Asbestos

**B00H - R0014 - Commonroom (32.45 m2)**

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

**B00H - R0015 - Cleaning Store - Distributed (2.76 m2)**

No Asbestos

**B00H - R0016 - Practical Activity Area (16.69 m2)**

No Asbestos

**B00H - R0017 - General Learning Space - S/P (42.85 m2)**

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

**B00H - R0018 - Toilets-Disabled (29.01 m2)**

No Asbestos

**B00H - R0019 - Student Laundry - Type 3 (11.32 m2)**

No Asbestos



Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
<b>B00H - R0020 - Toilets-Disabled (29.21 m2)</b>						
No Asbestos						
<b>B00H - R0021 - Practical Activity Area (17.09 m2)</b>						
No Asbestos						
<b>B00H - R0022 - General Learning Space - S/P (45.83 m2)</b>						
Vinyl Tiles (Under Floor Covering/Carpet)      No Asbestos Found						
<b>B00H - R0023 - Home Base Store - S (6.56 m2)</b>						
Vinyl Tiles (Under Floor Covering/Carpet)      No Asbestos Found						
<b>B00H - R0024 - Seminar - Type 3 (8.65 m2)</b>						
Vinyl Tiles (Under Floor Covering/Carpet)      No Asbestos Found						
<b>B00H - R0025 - Movement (54.68 m2)</b>						
No Asbestos						
<b>B00H - R0026 - Movement (7.49 m2)</b>						
No Asbestos						
<b>B00H - R0027 - Outdoor Learning Area (227.14 m2)</b>						
No Asbestos						
<b>B00H - R0028 - Distribution Board Cupboard (1.12 m2)</b>					Note: No inspection of live electrical installation.	
No Asbestos						
<b>B00H - R0029 - Movement (10.19 m2)</b>						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

***Demountables***

**There are no Demountable(s) located at this school as per the AMS records as of 15 Feb 2017.**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

***Listing of Electronic Attachments as of 22/03/2017***

**Available Asbestos Related Electronic Files**

8150\_ASB\_100913\_AMP.pdf

\* Note : Refer to AMS for details of the attachment(s).

2017
