


Asbestos Register

(Hazardous Materials and Risk Assessment)

School : Picnic Point High School (8377)
Region : South Western Sydney
State Electorate : East Hills
Local Government Area : Bankstown

Initial Survey : Noel Arnold & Associates : 04 - May - 2008
Reviewed By : Greencap-NAA : 13 - Aug - 2014

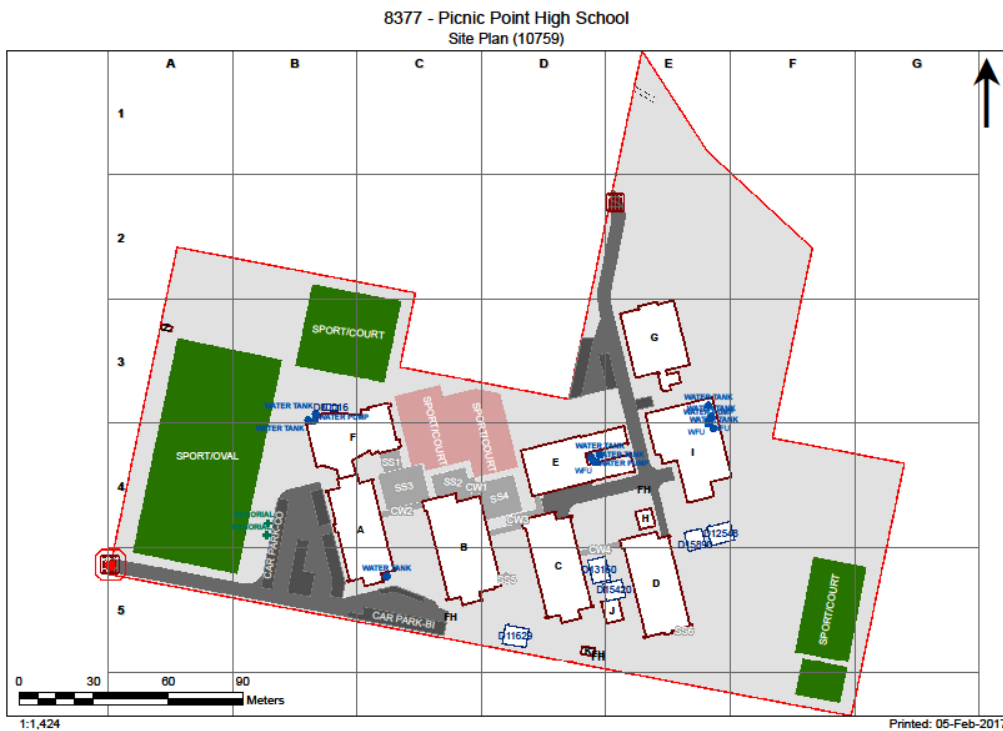

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00A - Administration/General Learning/Music - 1961 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids	No Asbestos Found					
Ceiling Voids - Flat Roof	Vermiculite					Limited Samples Taken
	8377/B00B/Ceiling Voids/S21					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Eaves Linings	Flat AC Sheeting	72m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00F/R0011/Ceiling Structures/Linings/S3					Chrysotile (white asbestos)

Interior

B00A - R0002 - Ancillary Staff (11.76 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00A/R0012/Ceiling Structures/Linings/S1					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>

Floor Coverings Res/Textile	Adhesive under Lenolium					No Asbestos Detected
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					

B00A - R0003 - Resources Store (4.69 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00A/R0012/Ceiling Structures/Linings/S1					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>

B00A - R0004 - Printing/Photocopying (19.42 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00A/R0012/Ceiling Structures/Linings/S1					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>

Floor Coverings Res/Textile	Adhesive					No Asbestos Detected
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					

B00A - R0006 - External Movement (13.18 m2)

Ceiling Structures/Linings	Flat AC Sheeting	13.87m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00A/R0006/Ceiling Structures/Linings/S24					Chrysotile (white asbestos) , Amosite (brown asbestos)

B00A - R0007 - Resources Store (6.46 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00A/R0012/Ceiling Structures/Linings/S1					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>

B00A - R0008 - Deputy Principal Office (11.04 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00A/R0012/Ceiling Structures/Linings/S1					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>

Floor Coverings Res/Textile	Adhesive under lenolium					No Asbestos Detected
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					

B00A - R0010 - Special Learning Space (39.16 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00A/R0012/Ceiling Structures/Linings/S1					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>

B00A - R0011 - General Learning Space (53.22 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00A/R0012/Ceiling Structures/Linings/S1					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>

B00A - R0012 - Special Learning Space (53.74 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Floor Coverings Res/Textile	Adhesive under Lenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R0013 - Cleaning Store - Distributed (4.61 m2)						
No Asbestos						
B00A - R0015 - Resources Store (6.28 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
B00A - R0016 - Art Learning Space (53.15 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
B00A - R0017 - Movement (58.3 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
B00A - R0018 - Office/Store (9.68 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
B00A - R0019 - Deputy Principal Office (9.27 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Floor Coverings Res/Textile	Adhesive under lenolium found under the carpet					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R0021 - Distribution Board Cupboard (0.87 m2)						
					Note: No inspection of live electrical installation.	
Floor Coverings Res/Textile	Vinyl Tiles	0.84m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00B/R1011/Floor Coverings Res/Textile/S19					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive					
	8377/B00B/R1011/Floor Coverings Res/Textile/S20					No Asbestos Detected
B00A - R0022 - Principal Office (19.14 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Floor Coverings Res/Textile	Adhesive under Lenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R0023 - General Storeroom (3.48 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Floor Coverings Res/Textile	Adhesive under Lenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R0025 - Administration - Executive (11.87 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Floor Coverings Res/Textile	Adhesive under lenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R0026 - Archive Store (12.08 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Floor Coverings Res/Textile	Adhesive undermlenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R0027 - External Movement (19.43 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	20m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00A/R0006/Ceiling Structures/Linings/S24					Chrysotile (white asbestos) , Amosite (brown asbestos)
Wall Linings Internal	Infill Panel Lower	7Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00B/R0024/In-fill-panel/S6					Chrysotile (white asbestos)
B00A - R0029 - External Movement (2.66 m2)						
No Asbestos						
B00A - R0030 - External Movement (7.04 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00A/R0006/Ceiling Structures/Linings/S24					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00A - R0031 - External Movement (2.5 m2)						
No Asbestos						
B00A - R0032 - External Movement (2.48 m2)						
No Asbestos						
B00A - R0033 - Toilets-Disabled (6.19 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
B00A - R0034 - Staff - Toilet (3.18 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
B00A - R0035 - Toilet - Lobby (2.18 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
B00A - R0038 - Resources Store (3.71 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
B00A - R0039 - Art Learning Space (62.51 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
B00A - R0040 - Stairs (6.55 m2)						
No Asbestos						
B00A - R0041 - Movement (13.81 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		
No Asbestos						
B00A - R0042 - Staff - Toilet (1.16 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R0043 - Handwashing Facilities (3.17 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R0044 - Stairs (0.38 m2)						
No Asbestos						
B00A - R0045 - Administration - Clerical (6.6 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)					
	8377/B00B/R1011/Floor Coverings Res/Textile/S20					No Asbestos Detected
Floor Coverings Res/Textile	Adhesive					
	8377/B00B/R1011/Floor Coverings Res/Textile/S20					No Asbestos Detected
B00A - R0046 - Handwashing Facilities (3.16 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R0047 - Staff - Toilet (1.09 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R0048 - Administration - Clerical (21.68 m2)						
Chalk Board	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	21.68m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00B/R1011/Floor Coverings Res/Textile/S19					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive					
	8377/B00B/R1011/Floor Coverings Res/Textile/S20					No Asbestos Detected
B00A - R0049 - Movement (35.3 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	35.3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00B/R1011/Floor Coverings Res/Textile/S19					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive					
	8377/B00B/R1011/Floor Coverings Res/Textile/S20					No Asbestos Detected
B00A - R0050 - Movement (23.05 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R0051 - Movement (34.44 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite	8377/B00A/R0012/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R1002 - Music Learning Space (53.56 m2)						
Ceiling Structures/Linings	Vermiculite	8377/B00A/R0012/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under grey mottled lenolium	8377/B00A/R1015/Floor Coverings Res/Textile/S25				No Asbestos Detected
B00A - R1003 - Music Store (7.13 m2)						
Ceiling Structures/Linings	Vermiculite	8377/B00A/R0012/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under grey mottled lenolium	8377/B00A/R1015/Floor Coverings Res/Textile/S25				No Asbestos Detected
B00A - R1004 - Distribution Board Cupboard (0.51 m2)						
					Note: No inspection of live electrical installation.	
No Asbestos						
B00A - R1005 - Music Learning Space (66.9 m2)						
Ceiling Structures/Linings	Vermiculite	8377/B00A/R0012/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under grey mottled lenolium	8377/B00A/R1015/Floor Coverings Res/Textile/S25				No Asbestos Detected
B00A - R1006 - Music Store (6.14 m2)						
Ceiling Structures/Linings	Vermiculite	8377/B00A/R0012/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under grey mottled Lenolium	8377/B00A/R1015/Floor Coverings Res/Textile/S25				No Asbestos Detected
B00A - R1008 - Staff Study (24.77 m2)						
Ceiling Structures/Linings	Vermiculite	8377/B00A/R0012/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R1010 - System Administrators Office (19.15 m2)						
Ceiling Structures/Linings	Vermiculite	8377/B00A/R0012/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive underdark green/grey Lenolium	8377/B00B/R1015/Floor Coverings Res/Textile/S18				No Asbestos Detected
B00A - R1011 - General Learning Space (53 m2)						
Ceiling Structures/Linings	Vermiculite	8377/B00A/R0012/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under Lenolium	8377/B00B/R1015/Floor Coverings Res/Textile/S18				No Asbestos Detected
B00A - R1012 - Resources Store (9.51 m2)						
Ceiling Structures/Linings	Vermiculite	8377/B00A/R0012/Ceiling Structures/Linings/S1				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Floor Coverings Res/Textile	Adhesive under lenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R1013 - General Learning Space (53.6 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under lenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R1014 - Resources Store (9.54 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under dark green/grey Lenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R1015 - General Learning Space (53.74 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under Dark green\ grey Lenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
Floor Coverings Res/Textile	Adhesive under grey mottled lenium					
	8377/B00A/R1015/Floor Coverings Res/Textile/S25					No Asbestos Detected
B00A - R1016 - General Learning Space (66.77 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under Lenolium undr carpet					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R1017 - General Storeroom (6.21 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesice under Dark green/grey lenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R1018 - Computer Room (11.84 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive undervlenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00A - R1019 - General Learning Space (39.62 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under Grey mottled lenolium under capet					
	8377/B00A/R1015/Floor Coverings Res/Textile/S25					No Asbestos Detected
B00A - R1020 - Resources Store (6.25 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite		8377/B00A/R0012/Ceiling Structures/Linings/S1			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under grey mottled lenolium		8377/B00A/R1015/Floor Coverings Res/Textile/S25			No Asbestos Detected
B00A - R1021 - Cleaning Store - Distributed (6.31 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00A/R0012/Ceiling Structures/Linings/S1			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under grey mottled lenolium		8377/B00A/R1015/Floor Coverings Res/Textile/S25			No Asbestos Detected
B00A - R1022 - Movement (90.17 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00A/R0012/Ceiling Structures/Linings/S1			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R1024 - Movement (9.45 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00A/R0012/Ceiling Structures/Linings/S1			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under grey mottled Lenolium		8377/B00A/R1015/Floor Coverings Res/Textile/S25			No Asbestos Detected
B00A - R1025 - Staff - Toilet (1.06 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00A/R0012/Ceiling Structures/Linings/S1			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R1026 - Handwashing Facilities (3.16 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00A/R0012/Ceiling Structures/Linings/S1			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R1027 - Stairs (15.06 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00A/R0012/Ceiling Structures/Linings/S1			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R1028 - Stairs (10.44 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00A/R0012/Ceiling Structures/Linings/S1			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00A - R1029 - Staff Study (34.36 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00A/R0012/Ceiling Structures/Linings/S1			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under grey mottled Lenolium		8377/B00A/R1015/Floor Coverings Res/Textile/S25			No Asbestos Detected

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		

B00B - Technological & Applied Studies/General Learning - 1961 - Brick/Block (Brick/Block)**Exterior**

Ceiling Voids	Encapsulated Insulation material within unit 8377/B00B/Ceiling Voids/S21					No Asbestos Detected
Underfloor Voids	No Asbestos Found					
Eaves Linings	Flat AC Sheeting 8377/B00F/R0011/Ceiling Structures/Linings/S3	70m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Wall Cladding	Infill Panel - Lower 8377/B00B/R0024/In-fill-panel/S6	70m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Wall Cladding	Infill panel - Higher 8377/B00B/R0024/In-fill-panel/S6	70m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Dust Extractor	Gasket material 8377/B00B/Dust Extractor/S31					No Asbestos Detected

Interior**B00B - R0001 - General Storeroom (4.65 m2)**

No Asbestos

B00B - R0002 - Art Learning Space (67.2 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Infill Panels - Lower	Compressed AC Sheet 8377/B00B/R0002/Infill Panels - Lower/S17					No Asbestos Detected

B00B - R0003 - General Storeroom (10.52 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	---

B00B - R0005 - General Storeroom (1.04 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	---

B00B - R0008 - Office/Store (9.6 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	---

B00B - R0009 - Computer Learning Space (74.13 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	---

B00B - R0010 - Cleaning Store - Distributed (4.61 m2)

No Asbestos

B00B - R0011 - Seminar (33.58 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	---

B00B - R0012 - Main Switchroom (4.8 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	---

B00B - R0013 - Food Technology L.S. (88.67 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
No Asbestos						
B00B - R0014 - Preparation - Materials (18.63 m2)						
No Asbestos						
B00B - R0017 - Movement (111.86 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0018 - Movement (9.79 m2)						
No Asbestos						
B00B - R0019 - External Movement (3.51 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	3.65m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00B/R0024/In-fill-panel/S6					Chrysotile (white asbestos)
B00B - R0020 - External Movement (4.4 m2)						
No Asbestos						
B00B - R0021 - External Movement (4.4 m2)						
No Asbestos						
B00B - R0022 - External Movement (20.06 m2)						
No Asbestos						
B00B - R0024 - External Movement (134.59 m2)						
In-fill-panel	Flat AC Sheeting	22m	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00B/R0024/In-fill-panel/S6					Chrysotile (white asbestos)
B00B - R0025 - Laundry (2.2 m2)						
No Asbestos						
B00B - R0026 - Pantry (4.49 m2)						
No Asbestos						
B00B - R0027 - Stairs (0.22 m2)						
No Asbestos						
B00B - R0028 - Stairs (5.83 m2)						
No Asbestos						
B00B - R0029 - Stairs (6.02 m2)						
No Asbestos						
B00B - R0030 - Darkroom Space (2.65 m2)						
Chalk Board	Vermiculite					
	8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0031 - Dark Room (16.71 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0032 - Food Technology L.S. (108.47 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0033 - Store - Coolroom (3.77 m2)						
No Asbestos						
B00B - R0034 - Plant (0.59 m2)						
No Asbestos						
B00B - R0035 - Staff Study (62.42 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite		8377/B00B/R0008/Ceiling Structures/Linings/S4			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1001 - General Learning Space (53.6 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00B/R0008/Ceiling Structures/Linings/S4			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1002 - Resources Store (7.44 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00B/R0008/Ceiling Structures/Linings/S4			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive		8377/B00B/R1015/Floor Coverings Res/Textile/S18			No Asbestos Detected
B00B - R1003 - Cleaning Store - Distributed (4.18 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00B/R0008/Ceiling Structures/Linings/S4			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1004 - Interview/Meeting (25.13 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00B/R0008/Ceiling Structures/Linings/S4			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1006 - Textiles Technology L.S. (72.07 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00B/R0008/Ceiling Structures/Linings/S4			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Wall Linings Internal	Infill panel lower		8377/B00B/R0002/Infill Panels - Lower/S17			No Asbestos Detected
B00B - R1007 - Distribution Board Cupboard (0.27 m2)						
					Note: No inspection of live electrical installation.	
No Asbestos						
B00B - R1008 - Design L.S. (73.93 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00B/R0008/Ceiling Structures/Linings/S4			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Wall Linings Internal	Infill panels lower		8377/B00B/R0002/Infill Panels - Lower/S17			No Asbestos Detected
B00B - R1009 - General Learning Space (53.52 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00B/R0008/Ceiling Structures/Linings/S4			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under lenolium		8377/B00B/R1015/Floor Coverings Res/Textile/S18			No Asbestos Detected
B00B - R1010 - General Learning Space (52.49 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00B/R0008/Ceiling Structures/Linings/S4			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	53.87m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
					Chrysotile (white asbestos)	
Floor Coverings Res/Textile	Adhesive		8377/B00B/R1011/Floor Coverings Res/Textile/S20			No Asbestos Detected
B00B - R1011 - Computer Learning Space (53.3 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet) 8377/B00B/R1011/Floor Coverings Res/Textile/S19	53.64m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive 8377/B00B/R1011/Floor Coverings Res/Textile/S20					No Asbestos Detected
B00B - R1012 - Staff Study (26.1 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Adhesive 8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00B - R1013 - Resources Store (12.82 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Adhesive under lenolium 8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00B - R1014 - Resources Store (12.96 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Adhesive 8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00B - R1015 - General Learning Space (53.52 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Adhesive under old lenolium 8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00B - R1016 - Movement (116.85 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
B00B - R1017 - Stairs (11.5 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
B00B - R1018 - Stairs (11.09 m2)						
No Asbestos						
B00B - R1019 - Stairs (11.35 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
B00B - R1020 - Staff - Toilet (1.34 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00B/R0008/Ceiling Structures/Linings/S4					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00B - R1021 - Handwashing Facilities (5.19 m2)

Ceiling Structures/Linings Vermiculite
 8377/B00B/R0008/Ceiling Structures/Linings/S4 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00C - General Learning/Science Learning - 1962 - Brick/Block (Brick/Block)**Exterior**

In-fill-panel	Flat AC Sheeting 8377/B00C/In-fill-panel/S8	64m2	West, Upper portion	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Ceiling Voids	Encapsulated Insulation material within unit 8377/B00C/Ceiling Voids/S28					No Asbestos Detected
Underfloor Voids	No Asbestos Found					
Eaves Linings	Flat AC Sheeting	80m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Assumed Asbestos - Height Restriction - Height

Interior**B00C - R0001 - General Storeroom (4.65 m2)**

No Asbestos

B00C - R0002 - General Learning Space (53.45 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	--

B00C - R0003 - Staff Study (45.53 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	--

B00C - R0004 - Cleaning Store - Distributed (4.88 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	--

B00C - R0005 - Distribution Board Cupboard (0.51 m2)

Note: No inspection of live electrical installation.

No Asbestos

B00C - R0006 - Resources Store (26.13 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	--

B00C - R0008 - General Learning Space (53.08 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	--

B00C - R0009 - General Learning Space (53.82 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	--

B00C - R0010 - General Learning Space (53.59 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	--

B00C - R0011 - Laboratory L.S. (93.94 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	--

B00C - R0012 - Preparation - Science (25.57 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
----------------------------	--	--	--	--	--	--

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00C - R0013 - Laboratory L.S. (94.73 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R0015 - Movement (9.94 m2)						
No Asbestos						
B00C - R0016 - External Movement (3.56 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00E/R1015/Ceiling Structures/Linings/S22					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00C - R0017 - External Movement (4.18 m2)						
No Asbestos						
B00C - R0018 - External Movement (4.15 m2)						
No Asbestos						
B00C - R0019 - External Movement (19.72 m2)						
No Asbestos						
B00C - R0020 - Staff - Toilet (2 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R0021 - Handwashing Facilities (3.71 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R0022 - Stairs (6.09 m2)						
No Asbestos						
B00C - R0023 - Stairs (0.23 m2)						
No Asbestos						
B00C - R0024 - Movement (109.65 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R0025 - Stairs (6.25 m2)						
No Asbestos						
B00C - R0026 - General Storeroom (4.65 m2)						
No Asbestos						
B00C - R1001 - General Learning Space (53.52 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under green lenolium					
	8377/B00C/R1013/Floor Coverings Res/Textile/S27					No Asbestos Detected
B00C - R1002 - Staff Study (45.46 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00C/R0007/Ceiling Structures/Linings/S7					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under green lenolium					
	8377/B00C/R1013/Floor Coverings Res/Textile/S27					No Asbestos Detected
B00C - R1003 - Cleaning Store - Distributed (4.95 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R1004 - Distribution Board Cupboard (0.54 m2)					Note: No inspection of live electrical installation.	
No Asbestos						
B00C - R1005 - Staff Study (26.1 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive unde green lenolium		8377/B00C/R1013/Floor Coverings Res/Textile/S27			No Asbestos Detected
B00C - R1007 - General Learning Space (51.09 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under green lenolium		8377/B00C/R1013/Floor Coverings Res/Textile/S27			No Asbestos Detected
B00C - R1008 - General Learning Space (53.52 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under lenolium		8377/B00C/R1013/Floor Coverings Res/Textile/S27			No Asbestos Detected
B00C - R1009 - General Learning Space (53.45 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under green lenolium		8377/B00C/R1013/Floor Coverings Res/Textile/S27			No Asbestos Detected
B00C - R1010 - General Learning Space (53.01 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive nder green lenolium		8377/B00C/R1013/Floor Coverings Res/Textile/S27			No Asbestos Detected
B00C - R1011 - General Learning Space (53.01 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive undercgreen lenolium		8377/B00C/R1013/Floor Coverings Res/Textile/S27			No Asbestos Detected
B00C - R1012 - General Learning Space (53.15 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under green lenolium		8377/B00C/R1013/Floor Coverings Res/Textile/S27			No Asbestos Detected
B00C - R1013 - General Learning Space (53.52 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under green/grey lenolium		8377/B00C/R1013/Floor Coverings Res/Textile/S27			No Asbestos Detected
B00C - R1014 - Movement (114.1 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adhesive under green lenolium		8377/B00C/R1014/Floor Coverings Res/Textile/S26			No Asbestos Detected
B00C - R1015 - General Storeroom (5.12 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R1016 - Stairs (11.01 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R1017 - Stairs (11.71 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R1018 - Handwashing Facilities (3.76 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R1019 - Staff - Toilet (1.99 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R0007/Ceiling Structures/Linings/S7			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00C - R1020 - Stairs (11.19 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00C/R1013/Floor Coverings Res/Textile/S27			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00D - Technological & Applied Studies - 1961 - Brick/Block (Brick/Block)

Exterior

In-fill-panel	Flat AC Sheeting	82m2	East, West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00D/In-fill-panel/S11					Chrysotile (white asbestos)
Ceiling Voids - Flat Roof	Encapsulated Insulation material within unit					No Asbestos Detected
	8377/B00B/Ceiling Voids/S21					
Eaves Linings	Flat AC Sheeting	85m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00F/R0011/Ceiling Structures/Linings/S3					Chrysotile (white asbestos)
Underfloor Voids	Corrugated AC Sheeting	12m2	South East	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00D/Underfloor Voids/S29					Chrysotile (white asbestos) , Amosite (brown asbestos)

Interior

B00D - R0002 - Class Tools Storage (13.67 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00D/R0001/Ceiling Structures/Linings/S10					Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

B00D - R0010 - Staff Study (26.02 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00D/R0001/Ceiling Structures/Linings/S10					Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

Floor Coverings Res/Textile	Adhesive under green lenolium					No Asbestos Detected
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					

B00D - R0012 - Project Store - Type 1 (19.47 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00D/R0001/Ceiling Structures/Linings/S10					Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

B00D - R0013 - Distribution Board Cupboard (0.53 m2) Note: No inspection of live electrical installation.

No Asbestos

B00D - R0014 - Design L.S. (39.14 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00D/R0001/Ceiling Structures/Linings/S10					Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

B00D - R0015 - Movement (89.51 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00D/R0001/Ceiling Structures/Linings/S10					Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

B00D - R0016 - External Movement (5.29 m2)

No Asbestos

B00D - R0017 - External Movement (2.34 m2)

No Asbestos

B00D - R0020 - External Movement (42.46 m2)

No Asbestos

B00D - R0021 - Handwashing Facilities (2.39 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8377/B00D/R0001/Ceiling Structures/Linings/S10					Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

B00D - R0022 - Staff - Toilet (1.5 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite 8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00D - R0023 - Dust Extraction Space (5.25 m2)						
No Asbestos						
B00D - R0025 - Project Store - Type 1 (19.35 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00D - R0026 - Project Store - Type 1 (13.37 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00D - R0027 - Dust Extraction Space (5.07 m2)						
No Asbestos						
B00D - R0028 - Wood Technology L.S. (79.12 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00D - R0029 - Handwashing Facilities (1.16 m2)						
Chalk Board	Vermiculite 8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Adhesive under lenolium 8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00D - R0030 - Materials Technology L.S. (83.08 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00D - R0031 - Handwashing Facilities (1.73 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Adhesive under lenolium 8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00D - R0032 - Handwashing Facilities (1.98 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Adhesive under lenolium 8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00D - R0033 - Metal Technology L.S. (97.11 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Wall Linings Internal	Infill panel lower 8377/B00D/In-fill-panel/S11	4m2	East	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B00D - R0034 - Welding Area (7.53 m2)						
Ceiling Structures/Linings	Vermiculite 8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Floor Coverings Res/Textile	Adhesive					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00D - R0035 - Handwashing Facilities (2.05 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Adheive under lenolium					
	8377/B00B/R1015/Floor Coverings Res/Textile/S18					No Asbestos Detected
B00D - R0036 - Wood Technology L.S. (78.64 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00D - R0037 - Handwashing Facilities (1.62 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00D - R0038 - Materials Store (21.82 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00D - R0039 - Resources Store (4.48 m2)						
Ceiling Structures/Linings	Vermiculite					
	8377/B00D/R0001/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00E - Pupil Facilities/Physical Education - 1962 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids	No Asbestos Found					
Eaves Linings	Flat AC Sheeting	72m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00F/R0011/Ceiling Structures/Linings/S3				Chrysotile (white asbestos)	
Ceiling Voids	Flat AC Sheeting	1200m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00E/R1015/Ceiling Structures/Linings/S22				Chrysotile (white asbestos) , Amosite (brown asbestos)	

Interior

B00E - R0001 - General Storeroom (33.91 m2)

Water Proof Membrane	Bituminous Material	8377/B00E/R0002/Water Proof Membrane/S23				No Asbestos Detected
----------------------	---------------------	--	--	--	--	----------------------

B00E - R0002 - General Storeroom (33.33 m2)

Water Proof Membrane	Bituminous Material	8377/B00E/R0002/Water Proof Membrane/S23				No Asbestos Detected
----------------------	---------------------	--	--	--	--	----------------------

B00E - R0003 - Sport Equipment Store (9.28 m2)

No Asbestos

B00E - R0004 - Sport Equipment Store (7.65 m2)

No Asbestos

B00E - R0005 - Movement Studio (87.65 m2)

Ceiling Structures/Linings	Flat AC Sheeting	8377/B00E/R1010/Ceiling Structures/Linings/S14				No Asbestos Detected
Wall Linings Internal	Infill panel - Higher	1m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00B/R0024/In-fill-panel/S6				Chrysotile (white asbestos)	

B00E - R0006 - Performance Workshop (78.79 m2)

Ceiling Structures/Linings	Flat AC Sheeting	8377/B00E/R1010/Ceiling Structures/Linings/S14				No Asbestos Detected
Wall Linings Internal	Infill panel Higher	1m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00B/R0024/In-fill-panel/S6				Chrysotile (white asbestos)	

B00E - R0007 - Staff - Toilet (1.73 m2)

Ceiling Structures/Linings	Flat AC Sheeting	8377/B00E/R1010/Ceiling Structures/Linings/S14				No Asbestos Detected
----------------------------	------------------	--	--	--	--	----------------------

B00E - R0008 - General Storeroom (5.99 m2)

Ceiling Structures/Linings	Flat AC Sheeting	8377/B00E/R1010/Ceiling Structures/Linings/S14				No Asbestos Detected
Wall Linings Internal	Infill Panel - Higher	1m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00B/R0024/In-fill-panel/S6				Chrysotile (white asbestos)	

B00E - R0009 - Sport Equipment Store (9.22 m2)

No Asbestos


B00E - R0010 - Sport Equipment Store (7.64 m2)

No Asbestos

B00E - R1001 - Toilets-Girls (97.97 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	8377/B00E/R1003/Partition Walls (Cubicles)/S15				No Asbestos Detected
Ceiling Structures/Linings	Compressed AC Sheet	99.74m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00E/R1015/Ceiling Structures/Linings/S22				Chrysotile (white asbestos) , Amosite (brown asbestos)	

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00E - R1002 - Plant (10.13 m2)						
No Asbestos						
B00E - R1003 - Toilets-Boys (110.35 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet					No Asbestos Detected
	8377/B00E/R1003/Partition Walls (Cubicles)/S15					
Ceiling Structures/Linings	Compressed AC Sheet	111.83m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00E/R1015/Ceiling Structures/Linings/S22					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00E - R1004 - Plant (12.57 m2)						
No Asbestos						
B00E - R1005 - Sport Equipment Store (4.04 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	3.81m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00E/R1015/Ceiling Structures/Linings/S22					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00E - R1006 - Pantry (9.28 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	9.02m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00E/R1015/Ceiling Structures/Linings/S22					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00E - R1007 - Student Canteen (41.02 m2)						
No Asbestos						
B00E - R1009 - General Storeroom (13.43 m2)						
No Asbestos						
B00E - R1010 - External Movement (47.61 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	48.56m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00E/R1015/Ceiling Structures/Linings/S22					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00E - R1013 - Handwashing Facilities (2.58 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	2.6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00E/R1015/Ceiling Structures/Linings/S22					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00E - R1014 - Staff - Toilet (1.56 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	1.52m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00E/R1015/Ceiling Structures/Linings/S22					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00E - R1015 - Covered Area (309.95 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	306.98m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8377/B00E/R1015/Ceiling Structures/Linings/S22					Chrysotile (white asbestos) , Amosite (brown asbestos)

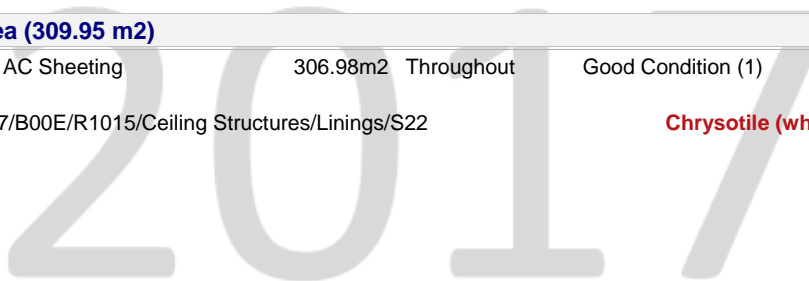

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00F - Multi Purpose Facilities - 1961 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids	Non Accessible Area - Extreme Access Issue - No personal access point into ceiling.					
Underfloor Voids - Slab on Ground	No Asbestos Found					
Ceiling Voids	Non Accessible Area - Height Restriction - Extreme Access Issue - No personal access point into ceiling.					
Eaves Linings	Flat AC Sheeting	60m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8377/B00F/R0011/Ceiling Structures/Linings/S3					Chrysotile (white asbestos)	

Interior

B00F - M0001 - General Storeroom (19.24 m2)

No Asbestos

B00F - M0002 - General Storeroom (19.16 m2)

No Asbestos

B00F - M0003 - Movement (11.29 m2)

No Asbestos

B00F - R0001 - General Storeroom (14.07 m2)

No Asbestos

B00F - R0002 - Staff - Toilet (1.39 m2)

No Asbestos

B00F - R0003 - Movement (2.99 m2)

No Asbestos

B00F - R0005 - Movement (3.03 m2)

No Asbestos

B00F - R0006 - General Storeroom (13.98 m2)

No Asbestos

B00F - R0007 - Staff - Toilet (1.37 m2)

No Asbestos

B00F - R0008 - Multi-Purpose Space (392.72 m2)

No Asbestos

B00F - R0009 - Staff Kitchen (13.7 m2)

No Asbestos

B00F - R0010 - Toilets-Girls (13.85 m2)

No Asbestos

B00F - R0011 - External Movement (23.11 m2)

Ceiling Structures/Linings	Flat AC Sheeting	23m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8377/B00F/R0011/Ceiling Structures/Linings/S3					Chrysotile (white asbestos)	

B00F - R0012 - Movement (32.31 m2)

Ceiling Structures/Linings	Vermiculite				
8377/B00A/R0012/Ceiling Structures/Linings/S1					Limited Samples Taken
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					

B00F - R0013 - External Movement (5.98 m2)

Infill panel -Higher	Compressed AC Sheet				
8377/B00F/R0013/Infill panel -Higher/S16					No Asbestos Detected

B00F - R0014 - External Movement (1.37 m2)

No Asbestos

B00F - R0015 - External Movement (3.55 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

No Asbestos

B00F - R0016 - External Movement (5.99 m2)

No Asbestos

B00F - R0018 - Stage (89.3 m2)

No Asbestos

B00F - R0019 - Stairs (0.48 m2)

No Asbestos

B00F - R0020 - Stairs (0.47 m2)

No Asbestos

B00F - R9002 - Fitness Laboratory (51.64 m2)

No Asbestos

B00F - R9003 - General Assistants (34.68 m2)

No Asbestos

B00F - R9004 - General Assistants (13.18 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00G - Library/Science Learning - 1971 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids - Slab on Ground	No Asbestos Found					
Ceiling Voids	No Asbestos Found					
Air Conditioning unit	Encapsulated Insulation material within unit Assumed Asbestos - Encased in unit	1Unit	South	Good Condition (1)	Low (1)	Low Priority (2-3)

Interior

B00G - M1003 - Careers Advisers Office (38.5 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00G/R0006/Ceiling Structures/Linings/S13					Limited Samples Taken
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

B00G - M1004 - Interview/Office - Type 1 (15.29 m2)

No Asbestos

B00G - M1005 - Movement (2.79 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00G/R0006/Ceiling Structures/Linings/S13					Limited Samples Taken
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

B00G - M1006 - Stairs (1.54 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00G/R0006/Ceiling Structures/Linings/S13					Limited Samples Taken
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

B00G - M1007 - Stairs (63.47 m2)

No Asbestos

B00G - M1008 - Senior Study (1.53 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00G/R0006/Ceiling Structures/Linings/S13					Limited Samples Taken
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

B00G - M1009 - Movement (2.79 m2)

Ceiling Structures/Linings	Vermiculite 8377/B00G/R0006/Ceiling Structures/Linings/S13					Limited Samples Taken
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

B00G - M1010 - Plant (4.63 m2)

No Asbestos

B00G - M1011 - General Storeroom (61.43 m2)

No Asbestos

B00G - M1012 - General Storeroom (23.17 m2)

No Asbestos

B00G - M1013 - General Storeroom (23.1 m2)

No Asbestos

B00G - R0001 - Laboratory L.S. (91.06 m2)

No Asbestos

B00G - R0004 - Laboratory L.S. (91.15 m2)

No Asbestos

B00G - R0005 - Laboratory L.S. (91.24 m2)

No Asbestos

B00G - R0008 - Laboratory L.S. (91.15 m2)

No Asbestos

B00G - R0009 - Chemical Store (16.88 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		
Floor Coverings Res/Textile	Vinyl Tiles	17m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8377/B00G/R0011/Floor Coverings Res/Textile/S12				Chrysotile (white asbestos)		
B00G - R0010 - Distribution Board Cupboard (0.49 m2)				Note: No inspection of live electrical installation.		
No Asbestos						
B00G - R0011 - Movement (40.58 m2)						
No Asbestos						
B00G - R0012 - Cleaning Store - Distributed (8.15 m2)						
No Asbestos						
B00G - R0013 - External Movement (3.13 m2)						
No Asbestos						
B00G - R0014 - Plant (8.76 m2)						
Flue	Fibre Cement Pipe	3m	South	Good Condition (1)	Low (1)	Low Priority (2-3)
8377/B00G/R0014/Flue/S30				Chrysotile (white asbestos) , Amosite (brown asbestos)		
B00G - R0015 - Distribution Board Cupboard (1.78 m2)				Note: No inspection of live electrical installation.		
No Asbestos						
B00G - R0016 - External Movement (27.06 m2)						
No Asbestos						
B00G - R0017 - Stairs (7.9 m2)						
No Asbestos						
B00G - R0018 - Preparation - Science (48.9 m2)						
No Asbestos						
B00G - R0019 - Tea Room (3.96 m2)						
Ceiling Structures/Linings	Vermiculite					
8377/B00G/R0006/Ceiling Structures/Linings/S13				Limited Samples Taken		
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00G - R0020 - Staff Study (44.46 m2)						
Ceiling Structures/Linings	Vermiculite					
8377/B00G/R0006/Ceiling Structures/Linings/S13				Limited Samples Taken		
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	44.65m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8377/B00G/R0011/Floor Coverings Res/Textile/S12				Chrysotile (white asbestos)		
B00G - R1003 - Cleaning Store - Distributed (0.34 m2)						
No Asbestos						
B00G - R1004 - Movement (4.62 m2)						
No Asbestos						
B00G - R1005 - Distribution Board Cupboard (0.28 m2)				Note: No inspection of live electrical installation.		
No Asbestos						
B00G - R1006 - Interview/Office - Type 1 (12.02 m2)						
No Asbestos						
B00G - R1007 - Interview/Office - Type 1 (12.45 m2)						
No Asbestos						
B00G - R1008 - Plant (5.2 m2)						
No Asbestos						
B00G - R1009 - Plant (5.22 m2)						
No Asbestos						
B00G - R1011 - Audio Visual Workroom (27.89 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00G - R1012 - Librarian (11.36 m2)						
No Asbestos						
B00G - R1013 - Library Administration (17.84 m2)						
No Asbestos						
B00G - R1014 - Office/Store (12.38 m2)						
No Asbestos						
B00G - R1017 - General Learning Space (70.27 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00G/R0006/Ceiling Structures/Linings/S13			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1018 - External Movement (1.78 m2)						
No Asbestos						
B00G - R1019 - External Movement (24.69 m2)						
No Asbestos						
B00G - R1020 - Stairs (16.47 m2)						
No Asbestos						
B00G - R1021 - Handwashing Facilities (1.73 m2)						
No Asbestos						
B00G - R1022 - Staff - Toilet (1.18 m2)						
No Asbestos						
B00G - R1023 - Handwashing Facilities (1.76 m2)						
No Asbestos						
B00G - R1024 - Staff - Toilet (1.16 m2)						
No Asbestos						
B00G - R1026 - Main Area (320.74 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00G/R0006/Ceiling Structures/Linings/S13			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1027 - Stairs (1.49 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00G/R0006/Ceiling Structures/Linings/S13			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1028 - Stairs (1.49 m2)						
Ceiling Structures/Linings	Vermiculite		8377/B00G/R0006/Ceiling Structures/Linings/S13			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1029 - Seminar (11.52 m2)						
No Asbestos						
B00G - R1030 - Office/Store (12.88 m2)						
No Asbestos						
B00G - R1031 - External Movement (6.77 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00H - Technological & Applied Studies - 2004 - Steel (Steel)

Exterior

Ceiling Voids - Flat Roof	No Asbestos Found
Underfloor Voids - Slab on Ground	No Asbestos Found

Interior

B00H - R0002 - Covered Outdoor Space (20.07 m2)

No Asbestos

B00H - R0003 - Kiln Space (13.18 m2)

No Asbestos

B00H - R0004 - Class Tools Storage (12.96 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00I - Physical Education - 2009 - Brick/Veneer (Brick/Veneer)**Exterior**

Ceiling Voids - Flat Roof	No Asbestos Found
Underfloor Voids	No Asbestos Found

Interior**B00I - R0001 - Multi-Purpose Space (620.24 m2)**

No Asbestos

B00I - R0002 - Staff Study (25 m2)

No Asbestos

B00I - R0003 - Tea Room (8.18 m2)

No Asbestos

B00I - R0004 - Sport Equipment Store (25.15 m2)

No Asbestos

B00I - R0005 - Change (29.25 m2)

No Asbestos

B00I - R0006 - Change (28.57 m2)

No Asbestos

B00I - R0007 - Distribution Board Cupboard (0.73 m2)

Note: No inspection of live electrical installation.

No Asbestos

B00I - R0008 - Cleaning Store - Distributed (3.18 m2)

No Asbestos

B00I - R0009 - Plant (0.75 m2)

No Asbestos

B00I - R0010 - Access Student Shower/Toilet/Change (8.96 m2)

No Asbestos

B00I - R0011 - First Aid (12.07 m2)

No Asbestos

B00I - R0012 - Plant (0.73 m2)

No Asbestos

B00I - R0013 - External Movement (66.07 m2)

No Asbestos

B00I - R9001 - Plant (54.4 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00J - Storage - 2009 - Metal Shed (Metal Shed)

Exterior

Ceiling Voids	No Asbestos Found
Underfloor Voids - Slab on Ground	No Asbestos Found

Interior

B00J - R0001 - Machine Storage (56.85 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00K - Building Services - 2009 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids	No Asbestos Found
Underfloor Voids - Slab on Ground	No Asbestos Found

Interior

B00K - R0001 - Plant (14.74 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00Z - Building Services - 1961 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids	No Asbestos Found
Underfloor Voids - Slab on Ground	No Asbestos Found

Interior

B00Z - R0001 - Plant (6.67 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Demountables

Demountable details as per the AMS records as of 15 Feb 2017.

OS 601 - D11629 - Learning Unit - Standard/Withdrawal : Placement Date - 14/02/2008

Exterior

Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos	11.52 m2

Interior

R1 - Entry

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	8 m2

R2 - General Learning Space

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	55 m2

R3 - Store

Ceiling	Flat AC Sheet	Assumed Asbestos	10 m2
---------	---------------	------------------	-------

OS 601 - D12548 - Learning Unit - Standard/Withdrawal : Placement Date - 10/05/2010

Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.

Exterior

No Asbestos Found.

Interior

R1 - Entry

No Asbestos Found.

R2 - General Learning Space

No Asbestos Found.

R3 - Store

No Asbestos Found.

NS 110 - D13160 - Learning Unit - Single Secondary/Secure : Placement Date - 9/10/2001

Exterior

No Asbestos Found.

Interior

R1 - General Learning Space

No Asbestos Found.

R2 - Entry

No Asbestos Found.

R3 - Secure Storeroom

No Asbestos Found.

OS 600 - D15420 - Learning Unit - Small : Placement Date - 16/06/2005

Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.

Exterior

No Asbestos Found.

Interior

R1 - General Learning Space

No Asbestos Found.

OS 600 - D15890 - Learning Unit - Small : Placement Date - 29/12/2004

Exterior

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Step Treads	Compressed AC Sheet	Assumed Asbestos				1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos				1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos				8.64 m2
Interior						
R1 - General Learning Space						
End wall panel	Flat AC Sheet	Assumed Asbestos				50 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				55 m2
OS 971 - D80016 - Shed - Container (Garden/Sports/Bulk) : Placement Date - 30/06/1995						
Exterior						
No Asbestos Found.						
Interior						
R1 - Garden Store						
No Asbestos Found.						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Listing of Electronic Attachments as of 22/03/2017

Available Asbestos Related Electronic Files

8377_ASB_150514_AMP.pdf

* Note : Refer to AMS for details of the attachment(s).

2017
