


# Asbestos Register

(Hazardous Materials and Risk Assessment)

**School :** Wewak Street School (5653)  
**Region :** Riverina  
**State Electorate :** Albury  
**Local Government Area :** Albury

**Initial Survey :** Noel Arnold & Associates : 12 - Mar - 2008  
**Reviewed By :** AECOM : 29 - Oct - 2014

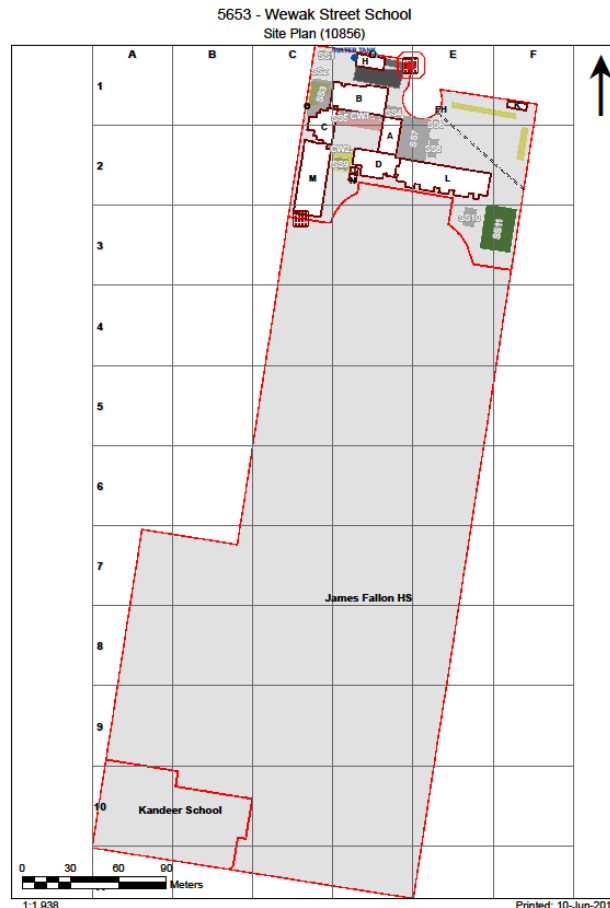

# 2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00A - Administration - 1976 - Brick/Block (Brick/Block)****Exterior**

Underfloor Voids - Slab on Ground

Ceiling Voids No Asbestos Found

**Interior****B00A - R0002 - External Movement (76.11 m2)**

No Asbestos

**B00A - R0003 - Entry Vestibule (18.94 m2)**

Ceiling Structures/Linings Vermiculite  
 5653/B00A/R0004/Ceiling Structures/Linings/S2 **Limited Samples Taken**  
*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00A - R0004 - General Storeroom (12.52 m2)**

Floor Coverings Res/Textile Vinyl Tiles 13m2 All surfaces Good Condition (1) Low (1) Low Priority (2-3)  
 5653/B00A/R0004/Floor Coverings Res/Textile/S1 **Chrysotile (white asbestos)**

Ceiling Structures/Linings Vermiculite  
 5653/B00A/R0004/Ceiling Structures/Linings/S2 **Limited Samples Taken**  
*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00A - R0005 - Distribution Board (5.05 m2)**

Note: No inspection of live electrical installation.

Ceiling Structures/Linings Vermiculite  
 5653/B00A/R0004/Ceiling Structures/Linings/S2 **Limited Samples Taken**  
*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00A - R0006 - Staff Toilet (5.92 m2)**

Ceiling Structures/Linings Vermiculite  
 5653/B00A/R0004/Ceiling Structures/Linings/S2 **Limited Samples Taken**  
*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00A - R0009 - General Storeroom (12.62 m2)**

Ceiling Structures/Linings Vermiculite  
 5653/B00A/R0004/Ceiling Structures/Linings/S2 **Limited Samples Taken**  
*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

Floor Coverings Res/Textile Vinyl Tiles 13m2 All surfaces Good Condition (1) Low (1) Low Priority (2-3)  
 5653/B00A/R0004/Floor Coverings Res/Textile/S1 **Chrysotile (white asbestos)**

**B00A - R0010 - Movement (22.45 m2)**

Ceiling Structures/Linings Vermiculite  
 5653/B00A/R0004/Ceiling Structures/Linings/S2 **Limited Samples Taken**  
*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00A - R0011 - Interview (18.98 m2)**

Ceiling Structures/Linings Vermiculite  
 5653/B00A/R0004/Ceiling Structures/Linings/S2 **Limited Samples Taken**  
*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00A - R0012 - Duplicating Workroom (9.21 m2)**

Floor Coverings Res/Textile Vinyl Tiles 10m2 All surfaces Good Condition (1) Low (1) Low Priority (2-3)  
 5653/B00A/R0004/Floor Coverings Res/Textile/S1 **Chrysotile (white asbestos)**

Ceiling Structures/Linings Vermiculite  
 5653/B00A/R0004/Ceiling Structures/Linings/S2 **Limited Samples Taken**  
*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00A - R0013 - Staff Room Annexe (9.17 m2)**

Ceiling Structures/Linings Vermiculite  
 5653/B00A/R0004/Ceiling Structures/Linings/S2 **Limited Samples Taken**  
*Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works*

**B00A - R0016 - General Storeroom (0.86 m2)**

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Flat AC Sheeting	1m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
5653/B00A/R0016/Ceiling Structures/Linings/S3					<b>Chrysotile (white asbestos)</b>	

**B00A - R0017 - Duplicating Workroom (12.81 m2)**

Ceiling Structures/Linings	Vermiculite	5653/B00A/R0017/Ceiling Structures/Linings/S15				<b>Limited Samples Taken</b>	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>							

**B00A - R0018 - Clerical Office (26.23 m2)**

Ceiling Structures/Linings	Vermiculite	5653/B00A/R0017/Ceiling Structures/Linings/S15				<b>Limited Samples Taken</b>	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>							

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00B - Communal Facilities/Pupil Facilities - 1976 - Brick/Block (Brick/Block)****Exterior**

Eaves Linings	Flat AC Sheeting 5653/B00B/Eaves Linings/S14					<b>No Asbestos Detected</b>
Underfloor Voids - Slab on Ground						
Ceiling Voids	No Asbestos Found					

**Interior****B00B - R0001 - Movement (31.37 m2)**

Ceiling Structures/Linings	Flat AC Sheeting 5653/B00B/R0011/Ceiling Structures/Linings/S7	32m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
				<b>Chrysotile (white asbestos) , Amosite (brown asbestos)</b>		

**B00B - R0009 - Hydrotherapy - Pool (13.95 m2)**

Ceiling Structures/Linings	Flat AC Sheeting 5653/B00B/R0011/Ceiling Structures/Linings/S7	14m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
				<b>Chrysotile (white asbestos) , Amosite (brown asbestos)</b>		

**B00B - R0010 - Toilets - Boys (11.15 m2)**

Ceiling Structures/Linings	Flat AC Sheeting 5653/B00B/R0011/Ceiling Structures/Linings/S7	12m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
				<b>Chrysotile (white asbestos) , Amosite (brown asbestos)</b>		

Partition Walls (Cubicles)	Flat AC Sheeting 5653/B00D/R0003/Partition Walls (Cubicles)/S11	8m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
				<b>Chrysotile (white asbestos)</b>		

**B00B - R0011 - Toilets - Girls (17.05 m2)**

Ceiling Structures/Linings	Flat AC Sheeting 5653/B00B/R0011/Ceiling Structures/Linings/S7	18m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
				<b>Chrysotile (white asbestos) , Amosite (brown asbestos)</b>		

Partition Walls (Cubicles)	Flat AC Sheeting 5653/B00D/R0003/Partition Walls (Cubicles)/S11	8m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
				<b>Chrysotile (white asbestos)</b>		

**B00B - R0013 - Kitchen - Type 1 (50.87 m2)**

Floor Coverings Res/Textile	Vinyl Tiles 5653/B00B/R0013/Floor Coverings Res/Textile/S6	51m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
				<b>Chrysotile (white asbestos)</b>		

**B00B - R0014 - Movement (10.71 m2)**

Ceiling Structures/Linings	Flat AC Sheeting 5653/B00B/R0011/Ceiling Structures/Linings/S7	11m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
				<b>Chrysotile (white asbestos) , Amosite (brown asbestos)</b>		

**B00B - R0016 - Movement (2.91 m2)**

No Asbestos

**B00B - R0017 - Toilets - Boys/Girls (1.64 m2)**

Wall Linings Internal	Flat AC Sheeting 5653/B00B/R0017/Wall Linings Internal/S5	6m2	East facing	Good Condition (1)	Low (1)	Low Priority (2-3)
				<b>Chrysotile (white asbestos) , Amosite (brown asbestos)</b>		

**B00B - R0021 - Toilet - Lobby (7.55 m2)**

Wall Linings Internal	Flat AC Sheeting 5653/B00B/R0021/Wall Linings Internal/S12					<b>No Asbestos Detected</b>
Ceiling Structures/Linings	Flat AC Sheeting 5653/B00B/R0021/Ceiling Structures/Linings/S13					<b>No Asbestos Detected</b>

**B00B - R0022 - Staff Toilet (1.38 m2)**

--	--	--	--	--	--	--

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Wall Linings Internal	Flat AC Sheeting	5653/B00B/R0021/Wall Linings Internal/S12				No Asbestos Detected
Ceiling Structures/Linings	Flat AC Sheeting	5653/B00B/R0021/Ceiling Structures/Linings/S13				No Asbestos Detected
<b>B00B - R0023 - Staff Change (20.08 m2)</b>						
Wall Linings Internal	Flat AC Sheeting	5653/B00B/R0021/Wall Linings Internal/S12				No Asbestos Detected
Ceiling Structures/Linings	Flat AC Sheeting	5653/B00B/R0021/Ceiling Structures/Linings/S13				No Asbestos Detected
<b>B00B - R0024 - Disabled Shower/Toilet (4.26 m2)</b>						
Ceiling Structures/Linings	Flat AC Sheeting	5653/B00B/R0021/Ceiling Structures/Linings/S13				No Asbestos Detected
Wall Linings Internal	Flat AC Sheeting	5653/B00B/R0021/Wall Linings Internal/S12				No Asbestos Detected
<b>B00B - R0025 - Therapy (24.4 m2)</b>						
Ceiling Structures/Linings	Flat AC Sheeting	5653/B00B/R0021/Ceiling Structures/Linings/S13				No Asbestos Detected
Wall Linings Internal	Flat AC Sheeting	5653/B00B/R0021/Wall Linings Internal/S12				No Asbestos Detected
<b>B00B - R0026 - Movement (8.14 m2)</b>						
Ceiling Structures/Linings	Flat AC Sheeting	5653/B00B/Eaves Linings/S14				No Asbestos Detected
<b>B00B - R0027 - General Storeroom (5.15 m2)</b>						
Non Accessible						
<b>B00B - R0028 - External Movement (89.82 m2)</b>						
No Asbestos						
<b>B00B - R0029 - Communal Space (142.99 m2)</b>						
No Asbestos						
<b>B00B - R0030 - Ramp (5.76 m2)</b>						
No Asbestos						
<b>B00B - R0031 - Raised Platform (34.15 m2)</b>						
No Asbestos						
<b>B00B - R0032 - Movement (4.14 m2)</b>						
No Asbestos						
<b>B00B - R0033 - Movement (8.7 m2)</b>						
No Asbestos						
<b>B00B - R0034 - Staff Room Annexe (8.1 m2)</b>						
No Asbestos						
<b>B00B - R0035 - Staff Room Annexe (16.57 m2)</b>						
No Asbestos						
<b>B00B - Room+1 - Added Room</b>						
No Asbestos						
<b>B00B - Room+2 - Added Room</b>						
No Asbestos						
<b>B00B - Room+3 - Added Room</b>						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00C - Support Unit/General Learning - 1976 - Brick/Block (Brick/Block)****Exterior**

Underfloor Voids - Slab on Ground

Ceiling Voids Non Accessible Area  
- Height Restriction 3m. Manhole located toward middle of room.

**Interior****B00C - R0001 - Movement (52.05 m2)**

No Asbestos

**B00C - R0002 - Practical Activities - P - 1hb (15.14 m2)**

Floor Coverings Res/Textile	Vinyl Tiles	16m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
5653/B00A/R0004/Floor Coverings Res/Textile/S1					<b>Chrysotile (white asbestos)</b>	

Ceiling Structures/Linings	Vermiculite	5653/B00A/R0004/Ceiling Structures/Linings/S2			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						

**B00C - R0003 - Home Base - P (53.77 m2)**

Ceiling Structures/Linings	Vermiculite	5653/B00A/R0004/Ceiling Structures/Linings/S2			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						

**B00C - R0004 - Movement (5.47 m2)**

Ceiling Structures/Linings	Vermiculite	5653/B00A/R0004/Ceiling Structures/Linings/S2			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						

**B00C - R0005 - Home Base - P (48.9 m2)**

Ceiling Structures/Linings	Vermiculite	5653/B00A/R0004/Ceiling Structures/Linings/S2			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						

**B00C - R0006 - Practical Activities - P - 1hb (14.95 m2)**

Floor Coverings Res/Textile	Vinyl Tiles	15m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
5653/B00A/R0004/Floor Coverings Res/Textile/S1					<b>Chrysotile (white asbestos)</b>	

Ceiling Structures/Linings	Vermiculite	5653/B00A/R0004/Ceiling Structures/Linings/S2			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						

**B00C - R0007 - Withdrawal Space - 1hb (4.39 m2)**

Ceiling Structures/Linings	Vermiculite	5653/B00A/R0004/Ceiling Structures/Linings/S2			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						

**B00C - R0008 - Movement (5.26 m2)**

Ceiling Structures/Linings	Vermiculite	5653/B00A/R0004/Ceiling Structures/Linings/S2			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						

**B00C - R0009 - Toilet - P (46.17 m2)**

Ceiling Structures/Linings	Vermiculite	5653/B00A/R0004/Ceiling Structures/Linings/S2			<b>Limited Samples Taken</b>	
<b>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</b>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00D - Support Unit/Pupil Facilities - 1976 - Brick/Block (Brick/Block)****Exterior**

Underfloor Voids - Slab on Ground

Ceiling Voids No Asbestos Found

**Interior****B00D - R0001 - External Movement (45.23 m2)**

No Asbestos

**B00D - R0005 - Practical Activities - P - 1hb (15.05 m2)**

Ceiling Structures/Linings	Vermiculite					
	5653/B00A/R0004/Ceiling Structures/Linings/S2					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Floor Coverings Res/Textile	Vinyl Tiles	16m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/B00A/R0004/Floor Coverings Res/Textile/S1					Chrysotile (white asbestos)

**B00D - R0006 - Home Base Store (6.91 m2)**

Ceiling Structures/Linings	Vermiculite					
	5653/B00A/R0004/Ceiling Structures/Linings/S2					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Floor Coverings Res/Textile	Vinyl Tiles	7m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/B00A/R0004/Floor Coverings Res/Textile/S1					Chrysotile (white asbestos)

**B00D - R0007 - Home Base - P (53.7 m2)**

Ceiling Structures/Linings	Vermiculite					
	5653/B00A/R0004/Ceiling Structures/Linings/S2					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					

**B00D - R0008 - Home Base - P (53.27 m2)**

Ceiling Structures/Linings	Vermiculite					
	5653/B00A/R0004/Ceiling Structures/Linings/S2					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					

**B00D - R0009 - Practical Activities - P - 1hb (14.53 m2)**

Ceiling Structures/Linings	Vermiculite					
	5653/B00A/R0004/Ceiling Structures/Linings/S2					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Floor Coverings Res/Textile	Vinyl Tiles	15m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/B00A/R0004/Floor Coverings Res/Textile/S1					Chrysotile (white asbestos)

**B00D - R0010 - Home Base Store - P (7.06 m2)**

Ceiling Structures/Linings	Vermiculite					
	5653/B00A/R0004/Ceiling Structures/Linings/S2					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Floor Coverings Res/Textile	Vinyl Tiles	8m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/B00A/R0004/Floor Coverings Res/Textile/S1					Chrysotile (white asbestos)

**B00D - R0016 - Toilets - Girls/Disabled Cubicle (20.45 m2)**

No Asbestos

**B00D - R0017 - Toilets - Boys/Disabled Cubicle (20.46 m2)**

No Asbestos

**B00D - R0018 - External Movement (32.08 m2)**

No Asbestos

**B00D - R0019 - Staff Toilet (3.54 m2)**

No Asbestos

**B00D - R0020 - Staff Toilet (3.54 m2)**

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

No Asbestos

**B00D - R0021 - Sports Store (4.07 m2)**

No Asbestos

**B00D - R0022 - Practical Activities (83.19 m2)**

No Asbestos

2017



Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00H - Other - 2008 - Steel (Steel)**

**Exterior**

Underfloor Voids - Slab on Ground

Ceiling Voids                      No Asbestos Found

**Interior**

**B00H - R0002 - General Storeroom (29.49 m2)**

No Asbestos

**B00H - R0003 - Garden Store (22.49 m2)**

No Asbestos

**B00H - R0004 - Garage/Carport (77.95 m2)**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00J - Building Services - 2010 - Brick/Veneer (Brick/Veneer)**

**Exterior**

No Asbestos

**Interior**

**B00J - R0001 - Sports Store (17.38 m2)**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00K - Pupil Facilities - 2014 - Metal Shed (Metal Shed)**

**Exterior**

Ceiling Void	No Asbestos Found
Underfloor Void	No Asbestos Found

**Interior**

**B00K - R0001 - General Storeroom (11.39 m2)**

No Asbestos

**B00K - R0002 - General Assistant/Bulk Store (34.83 m2)**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00L - General Learning - 2013 - Brick/Veneer (Brick/Veneer)****Exterior**

Ceiling Void	No Asbestos Found
Underfloor Void	No Asbestos Found

**Interior****B00L - R0001 - General Assistant/Bulk Store (53.44 m2)**

No Asbestos

**B00L - R0002 - Home Base Store - M (7.58 m2)**

No Asbestos

**B00L - R0003 - Home Base - M (75.26 m2)**

No Asbestos

**B00L - R0004 - Breakout Area (12.4 m2)**

No Asbestos

**B00L - R0005 - Access Shower/Toilet - Type 2 (19.85 m2)**

No Asbestos

**B00L - R0006 - Practical Activities - M - 2hb (38.07 m2)**

No Asbestos

**B00L - R0007 - Access Shower/Toilet/Change (6.94 m2)**

No Asbestos

**B00L - R0008 - Laundry - P (5.99 m2)**

No Asbestos

**B00L - R0009 - Breakout Area (12.4 m2)**

No Asbestos

**B00L - R0010 - Home Base - M (75.08 m2)**

No Asbestos

**B00L - R0011 - Home Base Store - M (7.58 m2)**

No Asbestos

**B00L - R0012 - Home Base Store - M (7.52 m2)**

No Asbestos

**B00L - R0013 - Home Base - M (75.32 m2)**

No Asbestos

**B00L - R0014 - Practical Activities - M - 2hb (38.18 m2)**

No Asbestos

**B00L - R0015 - Access Shower/Toilet - Type 2 (19.93 m2)**

No Asbestos

**B00L - R0016 - Breakout Area (12.43 m2)**

No Asbestos

**B00L - R0017 - Breakout Area (12.4 m2)**

No Asbestos

**B00L - R0018 - Laundry - P (5.73 m2)**

No Asbestos

**B00L - R0019 - Access Shower/Toilet/Change (6.93 m2)**

No Asbestos

**B00L - R0020 - Home Base - M (74.99 m2)**

No Asbestos

**B00L - R0021 - Home Base Store - M (14.41 m2)**

No Asbestos

**B00L - R0022 - Staff Room (51.17 m2)**

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	<b>Sample No</b>					<b>Test Result</b>

No Asbestos

**B00L - R0023 - Staff Room Annexe (25.02 m2)**

No Asbestos

**B00L - R0024 - External Movement (171.35 m2)**

No Asbestos

**B00L - R0025 - Distribution Board (0.48 m2)**

Note: No inspection of live electrical installation.

No Asbestos

**B00L - R0026 - Plant (7.34 m2)**

No Asbestos

**B00L - R0027 - Distribution Board (0.42 m2)**

Note: No inspection of live electrical installation.

No Asbestos

**B00L - R0028 - Distribution Board (0.39 m2)**

Note: No inspection of live electrical installation.

No Asbestos

**B00L - R0029 - Staff Kitchen (8.39 m2)**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

**B00M - General Learning - 2014 - Brick/Veneer (Brick/Veneer)****Exterior**

Ceiling Void	No Asbestos Found
Underfloor Void	No Asbestos Found

**Interior****B00M - R0001 - Home Base - M (75.05 m2)**

No Asbestos

**B00M - R0002 - Cleaning Distributed Store (14.29 m2)**

No Asbestos

**B00M - R0003 - Home Base Store - M (12.4 m2)**

No Asbestos

**B00M - R0004 - Breakout Area (12.72 m2)**

No Asbestos

**B00M - R0005 - Practical Activities - M - 1hb (37.84 m2)**

No Asbestos

**B00M - R0006 - Access Shower/Toilet/Change (6.65 m2)**

No Asbestos

**B00M - R0007 - Access Shower/Toilet - Type 2 (19.17 m2)**

No Asbestos

**B00M - R0008 - Laundry - P (5.15 m2)**

No Asbestos

**B00M - R0009 - Breakout Area (12.6 m2)**

No Asbestos

**B00M - R0010 - Reading Area (91.41 m2)**

No Asbestos

**B00M - R0011 - Library Office/Workroom (15.62 m2)**

No Asbestos

**B00M - R0012 - Communications Room (7.51 m2)**

No Asbestos

**B00M - R0013 - K.L.A. Store (18.68 m2)**

No Asbestos

**B00M - R0014 - Special Programs Room (30.89 m2)**

No Asbestos

**B00M - R0015 - Communal Space (58.23 m2)**

No Asbestos

**B00M - R0016 - Staff Kitchen (34.51 m2)**

No Asbestos

**B00M - R0017 - General Storeroom (9.87 m2)**

No Asbestos

**B00M - R0018 - General Storeroom (9.84 m2)**

No Asbestos

**B00M - R0019 - General Assistant/Bulk Store (59.73 m2)**

No Asbestos

**B00M - R0020 - P.E. Store (14.95 m2)**

No Asbestos

**B00M - R0021 - General Storeroom (14.95 m2)**

No Asbestos

**B00M - R0022 - External Movement (125.42 m2)**

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	<b>Sample No</b>					<b>Test Result</b>

No Asbestos

<b>B00M - R0023 - Distribution Board (0.54 m2)</b>	Note: No inspection of live electrical installation.
--	--

No Asbestos

<b>B00M - R0024 - Distribution Board (0.52 m2)</b>	Note: No inspection of live electrical installation.
--	--

No Asbestos

<b>B00M - R0025 - External Movement (26.32 m2)</b>	
--	--

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00N - Building Services - 2013 - Metal Shed (Metal Shed)**

**Exterior**

Ceiling Void	No Asbestos Found
Underfloor Void	No Asbestos Found

**Interior**

**B00N - R0001 - General Storeroom (17.5 m2)**

No Asbestos

2017



Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B000 - Storage - 2016 - Metal Shed (Metal Shed)**

**Exterior**

Ceiling Void	No Asbestos Found
Underfloor Void	No Asbestos Found

**Interior**

**B000 - R0001 - Sports Store (4.11 m2)**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**Build+2 - Class rooms****Exterior**

Entry Steps	Compressed AC Sheet					
	5653/Build+1/Entry Steps/S9					<b>No Asbestos Detected</b>

**Interior****Build+2 - Room+1 - Movement**

Ceiling Structures/Linings	Flat AC Sheeting	4m2	Middle portion	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/Build+2/Room+1/Ceiling Structures/Linings/S10					<b>Chrysotile (white asbestos)</b>

**Build+2 - Room+2 - Store room**

Ceiling Structures/Linings	Flat AC Sheeting	4m2	Middle portion	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/Build+2/Room+1/Ceiling Structures/Linings/S10					<b>Chrysotile (white asbestos)</b>

**Build+2 - Room+3 - Classroom**

Ceiling Structures/Linings	Flat AC Sheeting	8m2	Middle portion	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/Build+2/Room+1/Ceiling Structures/Linings/S10					<b>Chrysotile (white asbestos)</b>

**Build+2 - Room+4 - Classroom 2**

No Asbestos

**Build+2 - Room+5 - Store room 2**

Floor Coverings Res/Textile	Vinyl Tiles	8m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/Build+1/Room+1/Floor Coverings Res/Textile/S8					<b>Chrysotile (white asbestos)</b>

**Build+2 - Room+6 - Movement 2**

No Asbestos

**Build+2 - Room+7 - Classroom 3**

No Asbestos

**Build+2 - Room+8 - Store room 3**

Floor Coverings Res/Textile	Vinyl Tiles	8m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/Build+1/Room+1/Floor Coverings Res/Textile/S8					<b>Chrysotile (white asbestos)</b>

**Build+2 - Room+9 - Movement 3**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**Build+3 - Class rooms****Exterior**

Entry Steps	Compressed AC Sheet 5653/Build+1/Entry Steps/S9					<b>No Asbestos Detected</b>
-------------	--	--	--	--	--	-----------------------------

**Interior****Build+3 - Room+1 - Classroom**

Ceiling Structures/Linings	Flat AC Sheeting	25m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/Build+2/Room+1/Ceiling Structures/Linings/S10					<b>Chrysotile (white asbestos)</b>

**Build+3 - Room+2 - Store room**

Ceiling Structures/Linings	Flat AC Sheeting	8m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/Build+2/Room+1/Ceiling Structures/Linings/S10					<b>Chrysotile (white asbestos)</b>

**Build+3 - Room+3 - Movement**

Ceiling Structures/Linings	Flat AC Sheeting	6m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/Build+2/Room+1/Ceiling Structures/Linings/S10					<b>Chrysotile (white asbestos)</b>

**Build+3 - Room+4 - Library**

Ceiling Structures/Linings	Flat AC Sheeting	30m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/Build+2/Room+1/Ceiling Structures/Linings/S10					<b>Chrysotile (white asbestos)</b>

**Build+3 - Room+5 - Audio/visual room**

Ceiling Structures/Linings	Flat AC Sheeting	20m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/Build+2/Room+1/Ceiling Structures/Linings/S10					<b>Chrysotile (white asbestos)</b>

**Build+3 - Room+6 - Movement**

Ceiling Structures/Linings	Flat AC Sheeting	8m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	5653/Build+2/Room+1/Ceiling Structures/Linings/S10					<b>Chrysotile (white asbestos)</b>

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

***Demountables***

**There are no Demountable(s) located at this school as per the AMS records as of 15 Feb 2017.**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

*Listing of Electronic Attachments as of 22/03/2017*

**There are no asbestos related file attachment(s) for this school.**

2017
