


# Asbestos Register

(Hazardous Materials and Risk Assessment)

**School :** Afterlee Public School (3640)  
**Region :** North Coast  
**State Electorate :** Lismore  
**Local Government Area :** Kyogle

**Initial Survey :** Noel Arnold & Associates : 11 - Jun - 2008  
**Register Issue Date :** 23 - Mar - 2017

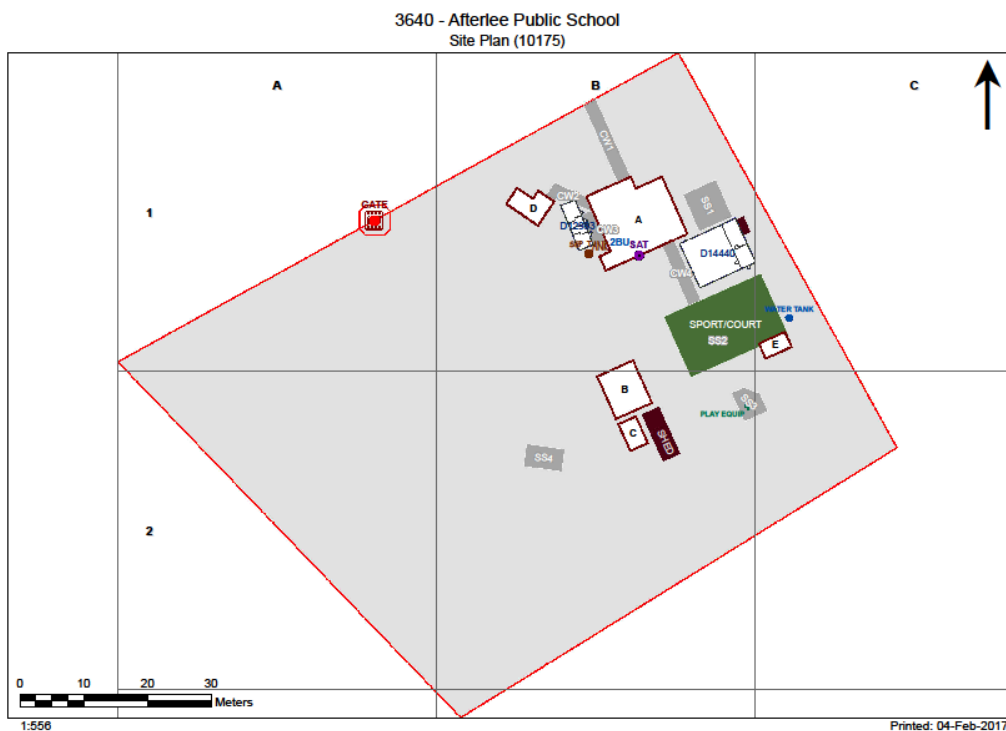

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		

**B00A - Library - 1950 - Timber (Timber)****Exterior**

Eaves Linings	Flat AC Sheeting	20m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
---------------	------------------	------	------------	--------------------	---------	--------------------

**Assumed Asbestos**

Ceiling Voids	Requires Inspection
---------------	---------------------

Underfloor Voids	Requires Inspection
------------------	---------------------

**Interior****B00A - R0001 - Reading Area**

Floor Coverings Res/Textile	Vinyl Tiles					
		3640/B00A/R0002/Floor Coverings Res/Textile/S1				<b>No Asbestos Detected</b>

**B00A - R0002 - Staff Kitchen**

Floor Coverings Res/Textile	Vinyl Tiles					
		3640/B00A/R0002/Floor Coverings Res/Textile/S1				<b>No Asbestos Detected</b>

**B00A - R0003 - Staff Room Annexe**

No Asbestos

**B00A - R0005 - External Movement**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No	Test Result				

**B00B - Building Services - 1950 - Timber (Timber)****Exterior**

Ceiling Voids Requires Inspection

Underfloor Voids Requires Inspection

**Interior****B00B - R0001 - External Movement**

No Asbestos

**B00B - R0002 - General Storeroom**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No	Test Result				

**B00C - Building Services - 1950 - Metal Shed (Metal Shed)****Exterior**

Ceiling Voids Requires Inspection

Underfloor Voids Requires Inspection

**Interior****B00C - R0001 - P.E. Store**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

**B00D - Administration - 2008 - Fibre Cement Clad (Fibre Cement Clad)****Exterior**

Ceiling Voids	No Asbestos Found
Underfloor Voids	Requires Inspection

**Interior****B00D - R0001 - External Movement**

No Asbestos

**B00D - R0002 - Clerical Office**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No	Test Result				

**B00E - Other - 2010 - Brick/Veneer (Brick/Veneer)****Exterior**

Ceiling Voids No Asbestos Found

Underfloor Voids Requires Inspection

**Interior****B00E - R0001 - Sports Store**

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

## Demountables

**Demountable details as per the AMS records as of 15 Feb 2017.**

**OS 842 - D12983 - Country Toilet - Relta - Boys/Girls : Placement Date - 3/03/2003**

Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.

### Exterior

No Asbestos Found.

### Interior

#### R1 - Toilets-Girls

No Asbestos Found.

#### R2 - Staff Toilet

No Asbestos Found.

#### R3 - Toilets-Boys

No Asbestos Found.

#### R4 - Staff Toilet

No Asbestos Found.

**OS 601 - D14440 - Learning Unit - Standard/Withdrawal : Placement Date - 30/06/1995**

### Exterior

Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos	11.52 m2

### Interior

#### R1 - Entry

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	8 m2

#### R2 - General Learning Space

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	55 m2

#### R3 - Store

Ceiling	Flat AC Sheet	Assumed Asbestos	10 m2
---------	---------------	------------------	-------

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

***Listing of Electronic Attachments as of 22/03/2017***

**There are no asbestos related file attachment(s) for this school.**

2017
