


Asbestos Register

(Hazardous Materials and Risk Assessment)

School : Glen Innes High School (8114)
Region : New England
State Electorate : Northern Tablelands
Local Government Area : Glen Innes Severn

Initial Survey : Noel Arnold & Associates : 20 - May - 2008
Reviewed By : Greencap-NAA : 01 - Apr - 2015

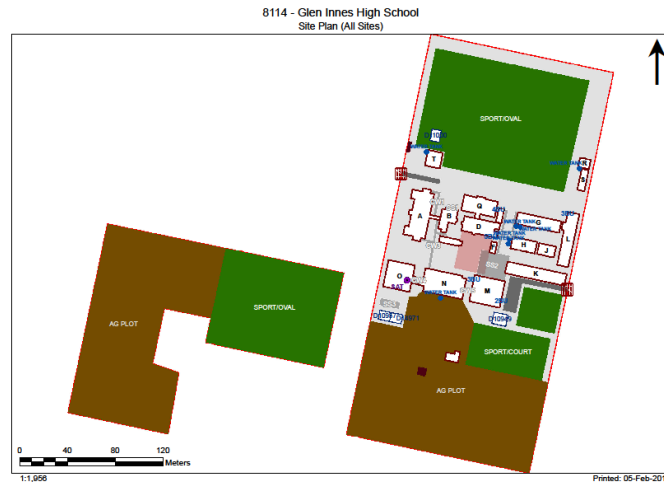

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00A - Administration/General Learning - 1926 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids	Non Accessible Area Assumed Asbestos - Height Restriction					
Underfloor Voids	Non Accessible Area 8114/B00D/R0004/Cement Pipe Through Ceiling/S7 - Area inaccessible					Chrysotile (white asbestos)

Interior

B00A - R0001 - General Learning Space (45.55 m2)

No Asbestos

B00A - R0002 - Movement (33.7 m2)

No Asbestos

B00A - R0003 - General Learning Space (56.56 m2)

No Asbestos

B00A - R0004 - General Learning Space (45.62 m2)

No Asbestos

B00A - R0005 - General Learning Space (50.06 m2)

No Asbestos

B00A - R0006 - Staff - Toilet (3.44 m2)

No Asbestos

B00A - R0007 - Cleaning Store - Distributed (2.04 m2)

No Asbestos

B00A - R0008 - Clinic - Boys (7.01 m2)

No Asbestos

B00A - R0009 - Deputy Principal Office (16.81 m2)

No Asbestos

B00A - R0010 - Principal Office (17.3 m2)

No Asbestos

B00A - R0011 - Administration - Clerical (16.7 m2)

No Asbestos

B00A - R0012 - Administration - Clerical (12.88 m2)

No Asbestos

B00A - R0013 - Duplicating Workroom (50.08 m2)

Floor Coverings Res/Textile	Adhesive	51m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00A/R0013/Floor Coverings Res/Textile/S5					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive	51m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00A/R0013/Floor Coverings Res/Textile/S5					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	51m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00A/R0013/Floor Coverings Res/Textile/S39					Chrysotile (white asbestos)

B00A - R0014 - General Learning Space (56.68 m2)

No Asbestos

B00A - R0015 - Commonroom (76.72 m2)

No Asbestos

B00A - R0016 - General Storeroom (7.66 m2)

No Asbestos

B00A - R0017 - Computer Resource (7.67 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No						Test Result

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	8114/B00A/R0016/Floor Coverings Res/Textile/S4				No Asbestos Detected
-----------------------------	---	--	--	--	--	----------------------

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	8114/B00A/R0016/Floor Coverings Res/Textile/S4				No Asbestos Detected
-----------------------------	---	--	--	--	--	----------------------

B00A - R0018 - Movement (33.6 m2)

No Asbestos

B00A - R0019 - Movement (66.12 m2)

No Asbestos

B00A - R0020 - Stairs (2.04 m2)

No Asbestos

B00A - R0021 - Movement (22.47 m2)

Ceiling Structures/Linings	Flat AC Sheeting	23m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8114/B00D/R0004/Wall Linings Internal/S8						Chrysotile (white asbestos)

B00A - R1001 - Senior Study (25.93 m2)

No Asbestos

B00A - R1002 - Staff Kitchen (12.24 m2)

No Asbestos

B00A - R1003 - Movement (8.45 m2)

No Asbestos

B00A - R1004 - Stairs (10.06 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00B - Staff Facilities - 1889 - Brick/Block (Brick/Block)

Exterior

Eaves Linings	Flat AC Sheeting 8114/B00B/Ceiling Voids - Abandon Pipe/S40					No Asbestos Detected
Panel Covering Window	Compressed AC Sheet 8114/B00B/R0011/Wall Linings Internal/S6					No Asbestos Detected

Interior

B00B - R0001 - Staff - Toilet (5.1 m2)

No Asbestos

B00B - R0002 - Staff - Toilet (3.77 m2)

No Asbestos

B00B - R0004 - Movement (22.78 m2)

No Asbestos

B00B - R0005 - Interview/Office - Type 1 (6.68 m2)

No Asbestos

B00B - R0006 - General Storeroom (7.61 m2)

No Asbestos

B00B - R0007 - General Storeroom (34 m2)

No Asbestos

B00B - R0008 - G.L.S. Store (14.45 m2)

Ceiling Structures/Linings	Flat AC Sheeting	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
----------------------------	------------------	------	------------	--------------------	---------	--------------------

Assumed Asbestos - Height Restriction

B00B - R0009 - Deputy Principal (19.1 m2)

Ceiling Structures/Linings	Flat AC Sheeting	20m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
----------------------------	------------------	------	------------	--------------------	---------	--------------------

Assumed Asbestos - Height Restriction

B00B - R0010 - Staff Study (37.01 m2)

No Asbestos

B00B - R0011 - Movement (22.94 m2)

Wall Linings Internal	Flat AC Sheeting 8114/B00B/R0011/Wall Linings Internal/S6					No Asbestos Detected
-----------------------	--	--	--	--	--	-----------------------------

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00C - Staff Facilities - 1884 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids	Non Accessible Area - Height Restriction
Underfloor Voids	Non Accessible Area - Area inaccessible

Interior

B00C - R0001 - Staff Study (47.94 m2)

No Asbestos

B00C - R0002 - General Storeroom (19.34 m2)

No Asbestos

B00C - R0003 - Covered Area (7.92 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00D - Performing Arts - 1955 - Brick/Block (Brick/Block)**Exterior**

Ceiling Voids	Non Accessible Area - Extreme Access Issue - No Access Point into ceiling void identified					
Cement Pipe Through Roof	Fibre Cement Pipe	1m	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00D/R0004/Cement Pipe Through Ceiling/S7				Chrysotile (white asbestos)	
Kick Board Panels	Flat AC Sheeting 8114/B00D/Kick Board Panels/S11 No Asbestos Detected					
Ceiling Voids	Non Accessible Area - Height Restriction - Extreme Access Issue - No Access Point into ceiling void identified					
Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible					

Interior**B00D - R0001 - Cleaning Store - Distributed (17.51 m2)**

No Asbestos

B00D - R0002 - Cleaning Supplies Store (14.94 m2)

Floor Coverings Res/Textile	Vinyl Sheet 8114/B00D/R0005/Floor Coverings Res/Textile/S9 No Asbestos Detected					
Ceiling Structures/Linings	Flat AC Sheeting	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00D/R0004/Wall Linings Internal/S8				Chrysotile (white asbestos)	

B00D - R0003 - Movement (9.35 m2)

Ceiling Structures/Linings	Flat AC Sheeting	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00D/R0004/Wall Linings Internal/S8				Chrysotile (white asbestos)	
Electrical Mounting Board	Resinous Board	1Unit	North	Good Condition (1)	Low (1)	Low Priority (2-3)

Assumed Asbestos - Electrical Hazard**B00D - R0004 - General Assistants (17.4 m2)**

Cement Pipe Through Ceiling	Fibre Cement Pipe	1m	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00D/R0004/Cement Pipe Through Ceiling/S7				Chrysotile (white asbestos)	
Wall Linings Internal	Flat AC Sheeting	15m2	North, South, East, Lower portion	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00D/R0004/Wall Linings Internal/S8				Chrysotile (white asbestos)	

B00D - R0005 - Performing Arts Changeroom (14.93 m2)

Ceiling Structures/Linings	Flat AC Sheeting	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00D/R0004/Wall Linings Internal/S8				Chrysotile (white asbestos)	
Floor Coverings Res/Textile	Vinyl Sheet 8114/B00D/R0005/Floor Coverings Res/Textile/S9 No Asbestos Detected					

B00D - R0006 - Stage (48.46 m2)

No Asbestos

B00D - R0007 - Multi-Purpose Space (199.82 m2)

No Asbestos

B00D - R0008 - Covered Area (3.09 m2)

No Asbestos

B00D - R0009 - Covered Area (3.09 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00E - Pupil Facilities - 1884 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids - Slab on Ground Non Accessible Area
 - Area inaccessible

Ceiling Voids Non Accessible Area
 - Area inaccessible

Interior

B00E - R0001 - General Storeroom (7.23 m2)

No Asbestos

B00E - R0002 - Toilets-Boys (32.7 m2)

No Asbestos

B00E - R0003 - Cleaning Store - Distributed (1.87 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00F - Pupil Facilities - 1884 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids - Slab on Ground Non Accessible Area
 - Area inaccessible

Ceiling Voids Non Accessible Area
 - Area inaccessible

Interior

B00F - R0001 - Toilets-Girls (31.59 m2)

No Asbestos

B00F - R0002 - Cleaning Store - Distributed (1.93 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00G - Technological & Applied Studies - 1955 - Timber (Timber)**Exterior**

Ceiling Voids	Non Accessible Area - Extreme Access Issue - No Access Point into ceiling void identified					
Eaves Linings	Flat AC Sheeting	60m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00G/R0002/Ceiling Structures/Linings/S12					Chrysotile (white asbestos)
Ceiling Voids	Non Accessible Area - Height Restriction - Extreme Access Issue - No Access Point into ceiling void identified					
Underfloor Voids	No Asbestos Found					

Interior**B00G - R0001 - Materials Store (8.37 m2)**

No Asbestos

B00G - R0002 - Movement (80.16 m2)

Ceiling Structures/Linings	Flat AC Sheeting	81m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00G/R0002/Ceiling Structures/Linings/S12					Chrysotile (white asbestos)

B00G - R0003 - Workshop Area (45.52 m2)

No Asbestos

B00G - R0004 - Materials Technology L.S. (88.84 m2)

No Asbestos

B00G - R0005 - Wood Technology Bay (33.18 m2)

No Asbestos

B00G - R0006 - Materials Technology L.S. (95.52 m2)

No Asbestos

B00G - R0007 - Dust Extraction Space (4.8 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00H - Computer Learning - 1922 - Timber (Timber)

Exterior

Eaves Linings	Flat AC Sheeting	40m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00H/Eaves Linings/S33				Chrysotile (white asbestos) , Amosite (brown asbestos) , Crocidolite (blue asbestos)	
Ceiling Voids	Non Accessible Area - Height Restriction					
Underfloor Voids	No Asbestos Found					

Interior

B00H - R0001 - Movement (46.85 m2)

Ceiling Structures/Linings	Flat AC Sheeting	47m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00G/R0002/Ceiling Structures/Linings/S12				Chrysotile (white asbestos)	

B00H - R0002 - Staff Study (53.95 m2)

No Asbestos

B00H - R0003 - General Storeroom (15.19 m2)

No Asbestos

B00H - R0004 - Staff - Toilet (4.23 m2)

No Asbestos

B00H - R0005 - Computer Learning Space (76.12 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00J - Technological & Applied Studies - 1884 - Timber (Timber)

Exterior

Ceiling Voids	Non Accessible Area - Extreme Access Issue - No Access Point into ceiling void identified					
Eaves Linings	Flat AC Sheeting	40m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00J/R0003/Ceiling Structures/Linings/S26			Chrysotile (white asbestos) , Amosite (brown asbestos)		
Underfloor Voids	No Asbestos Found					
Ceiling Voids	Non Accessible Area - Height Restriction - Extreme Access Issue - No Access Point into ceiling void identified					

Interior

B00J - R0001 - Design L.S. (94.29 m2)

No Asbestos

B00J - R0002 - Darkroom Space (26.93 m2)

No Asbestos

B00J - R0003 - Movement (6.39 m2)

Ceiling Structures/Linings	Flat AC Sheeting	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00J/R0003/Ceiling Structures/Linings/S26			Chrysotile (white asbestos) , Amosite (brown asbestos)		

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00K - Technological & Applied Studies - 1966 - Timber (Timber)

Exterior

Eaves Linings	Flat AC Sheeting	80m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00K/Eaves Linings/S30				Chrysotile (white asbestos) , Amosite (brown asbestos) , Crocidolite (blue asbestos)	
Ceiling Voids	Non Accessible Area - Height Restriction					
Underfloor Voids	No Asbestos Found					

Interior

B00K - R0001 - Art Learning Space (63.05 m2)

No Asbestos

B00K - R0002 - Movement (5.64 m2)

Ceiling Structures/Linings	Flat AC Sheeting	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00K/Eaves Linings/S30				Chrysotile (white asbestos) , Amosite (brown asbestos) , Crocidolite (blue asbestos)	

B00K - R0003 - Workshop (49.87 m2)

No Asbestos

B00K - R0004 - Resources Store (11.44 m2)

No Asbestos

B00K - R0005 - Kiln Space (7.41 m2)

No Asbestos

B00K - R0006 - Art Learning Space (58.05 m2)

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)					No Asbestos Detected
	8114/B00K/R0006/Floor Coverings Res/Textile/S31					
Floor Coverings Res/Textile	Adhesive					No Asbestos Detected
	8114/B00K/R0006/Floor Coverings Res/Textile/S32					

B00K - R0007 - Food Technology L.S. (72.61 m2)

No Asbestos

B00K - R0011 - Laundry (8.33 m2)

Floor Coverings Res/Textile	Vinyl Tiles	9m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00A/R0013/Floor Coverings Res/Textile/S5				Chrysotile (white asbestos)	

B00K - R0012 - Staff Study (13.65 m2)

No Asbestos

B00K - R0013 - Resources (6.84 m2)

Ceiling Structures/Linings	Flat AC Sheeting	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00K/Eaves Linings/S30				Chrysotile (white asbestos) , Amosite (brown asbestos) , Crocidolite (blue asbestos)	

B00K - R0014 - Movement (78.64 m2)

Ceiling Structures/Linings	Flat AC Sheeting	79m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00G/R0002/Ceiling Structures/Linings/S12				Chrysotile (white asbestos)	

Electrical Mounting Board	Resinous Board	1Unit	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00K/R0014/Electrical Mounting Board/S16				Chrysotile (white asbestos)	

B00K - R0015 - Kitchen - Type 2 (83.26 m2)

No Asbestos

B00K - R0016 - Materials Store - Type 1 (9.62 m2)

No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00K - R0017 - Preparation - Materials (14.83 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00L - Technological & Applied Studies - 1955 - Brick/Block (Brick/Block)**Exterior**

Eaves Linings	Flat AC Sheeting 8114/B00L/Gable Ends/S13					No Asbestos Detected
Gable Ends	Flat AC Sheeting 8114/B00L/Gable Ends/S13					No Asbestos Detected
Ceiling Voids	Non Accessible Area - Height Restriction					
Underfloor Voids	No Asbestos Found					

Interior**B00L - R0001 - Resource/Project Store (79.05 m2)**

Wall cladding	Flat AC Sheeting 8114/B00L/R0004/Wall Linings Internal/S15					No Asbestos Detected
---------------	---	--	--	--	--	----------------------

B00L - R0005 - Movement (3.77 m2)

No Asbestos

B00L - R0007 - Distribution Board Cupboard (1.61 m2)

Note: No inspection of live electrical installation.

Ceiling Structures/Linings	Flat AC Sheeting 8114/B00L/R0004/Wall Linings Internal/S15					No Asbestos Detected
----------------------------	---	--	--	--	--	----------------------

B00L - R0008 - Welding Store (40.46 m2)

No Asbestos

B00L - R0009 - General Storeroom (4.8 m2)

Wall Linings Internal	Flat AC Sheeting 8114/B00L/R0004/Wall Linings Internal/S15					No Asbestos Detected
-----------------------	---	--	--	--	--	----------------------

B00L - R0010 - Materials Technology L.S. (107.47 m2)

Ceiling Structures/Linings	Flat AC Sheeting 8114/B00L/R0004/Wall Linings Internal/S15					No Asbestos Detected
----------------------------	---	--	--	--	--	----------------------

B00L - R0012 - General Storeroom (14.16 m2)

No Asbestos

B00L - R0013 - Movement (18.53 m2)

No Asbestos

B00L - R0014 - Store (4.74 m2)

No Asbestos

B00L - R0015 - Workshop Area (122.89 m2)

No Asbestos

B00L - R0016 - Materials Store (8.35 m2)

No Asbestos

B00L - R0017 - Metal Technology Bay (3.67 m2)

No Asbestos

B00L - R0018 - Metal Technology Bay (3.89 m2)

No Asbestos

B00L - R0019 - Welding Area (7.7 m2)

No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00M - Physical Education - 1975 - Brick/Block (Brick/Block)**Exterior**

Ceiling Voids - Raked Ceiling	Non Accessible Area - Extreme Access Issue - Height Restricted - Approx >6m
Ceiling Voids - Raked Ceiling	Non Accessible Area - Height Restriction - Extreme Access Issue - Height Restricted - Approx >6m
Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible

Interior**B00M - R0001 - Gymnasium (308.88 m2)**

Decorative Coating	Vermiculite 8114/B00M/R1011/Decorative Coating/S28	Limited Samples Taken
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works		

B00M - R0002 - Movement (75.52 m2)

Decorative Coating	Vermiculite 8114/B00M/R1011/Decorative Coating/S28	Limited Samples Taken
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works		

B00M - R0003 - Sport Equipment Store (34.03 m2)

No Asbestos

B00M - R0004 - No Access (10.31 m2)

Electrical Mounting Board	Resinous Board	1Unit	South	Good Condition (1)	Low (1)	Low Priority (2-3)
Assumed Asbestos - Electrical Hazard						

B00M - R0005 - General Storeroom (6.33 m2)

No Asbestos

B00M - R0006 - Student Canteen (52.5 m2)

No Asbestos

B00M - R0007 - Distribution Board Cupboard (0.84 m2)

Note: No inspection of live electrical installation.

Electrical Mounting Board	Resinous Board	1Unit	West	Good Condition (1)	Low (1)	Low Priority (2-3)
Assumed Asbestos - Electrical Hazard						

B00M - R0008 - Chair Store (15.9 m2)

No Asbestos

B00M - R0009 - Sport Equipment Store (19.51 m2)

No Asbestos

B00M - R0010 - Staff - Toilet (1.75 m2)

No Asbestos

B00M - R0011 - Staff - Toilet (1.73 m2)

Incinerette	Encapsulated Insulation material within unit	1Unit	West	Good Condition (1)	Low (1)	Low Priority (2-3)
Assumed Asbestos - Area inaccessible						

B00M - R0012 - Maintenance Bulk Store (5.8 m2)

No Asbestos

B00M - R0013 - Staff - Toilet (3.24 m2)

No Asbestos

B00M - R0014 - Cleaning Store - Distributed (1.08 m2)

No Asbestos

B00M - R0015 - General Storeroom (0.9 m2)

No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00M - R1001 - Cleaning Store - Distributed (3.42 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1006/Ceiling Structures/Linings/S34					Chrysotile (white asbestos)
B00M - R1002 - General Storeroom (9.17 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1006/Ceiling Structures/Linings/S34					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Vinyl Tiles	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00A/R0013/Floor Coverings Res/Textile/S5					Chrysotile (white asbestos)
B00M - R1003 - Staff - Toilet (4.05 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1006/Ceiling Structures/Linings/S34					Chrysotile (white asbestos)
B00M - R1004 - Toilets-Girls (21.89 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	20m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1007/Partition Walls (Cubicles)/S19					Chrysotile (white asbestos)
Ceiling Structures/Linings	Flat AC Sheeting	22m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1006/Ceiling Structures/Linings/S34					Chrysotile (white asbestos)
B00M - R1005 - Shower/Change (43.75 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	40m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1007/Partition Walls (Cubicles)/S19					Chrysotile (white asbestos)
Ceiling Structures/Linings	Flat AC Sheeting	44m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1006/Ceiling Structures/Linings/S34					Chrysotile (white asbestos)
B00M - R1006 - Shower/Change (43.9 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	44m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1006/Ceiling Structures/Linings/S34					Chrysotile (white asbestos)
B00M - R1007 - Toilets-Boys (20.86 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	16m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1007/Partition Walls (Cubicles)/S19					Chrysotile (white asbestos)
Ceiling Structures/Linings	Flat AC Sheeting	21m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1006/Ceiling Structures/Linings/S34					Chrysotile (white asbestos)
B00M - R1008 - Staff - Toilet (3.83 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1006/Ceiling Structures/Linings/S34					Chrysotile (white asbestos)
B00M - R1009 - General Storeroom (9.1 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1006/Ceiling Structures/Linings/S34					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Vinyl Tiles	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00A/R0013/Floor Coverings Res/Textile/S5					Chrysotile (white asbestos)
B00M - R1010 - Cleaning Store - Distributed (3.49 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1006/Ceiling Structures/Linings/S34					Chrysotile (white asbestos)
B00M - R1011 - Movement (66.82 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Flat AC Sheeting 8114/B00M/R1011/Decorative Coating/S28					No Asbestos Detected
B00M - Room+1 - Walkway (First floor) from Building M to Building						
Ceiling Structures/Linings	Flat AC Sheeting	20m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00M/R1006/Ceiling Structures/Linings/S34					Chrysotile (white asbestos)

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00N - Science Learning - 1966 - Brick/Block (Brick/Block)**Exterior**

Eaves Linings	Flat AC Sheeting	100m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
---------------	------------------	-------	--------------	--------------------	---------	--------------------

Assumed Asbestos - Height Restriction

Ceiling Voids - Raked Ceiling	Non Accessible Area - Area inaccessible					
Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible					

Interior**B00N - R0001 - Movement (3.37 m2)**

No Asbestos

B00N - R0002 - General Learning Space (52.85 m2)

Decorative Coating	Vermiculite 8114/B00N/R0007/Decorative Coating/S24					Limited Samples Taken
--------------------	---	--	--	--	--	-----------------------

Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works**B00N - R0003 - Preparation (28.89 m2)**

Decorative Coating	Vermiculite 8114/B00N/R0007/Decorative Coating/S24					Limited Samples Taken
--------------------	---	--	--	--	--	-----------------------

Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works**B00N - R0004 - Growing/Breeding (9.68 m2)**

Decorative Coating	Vermiculite 8114/B00N/R0007/Decorative Coating/S24					Limited Samples Taken
--------------------	---	--	--	--	--	-----------------------

Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works**B00N - R0005 - Laboratory L.S. (92.82 m2)**

Decorative Coating	Vermiculite 8114/B00N/R0007/Decorative Coating/S24					Limited Samples Taken
--------------------	---	--	--	--	--	-----------------------

Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works**B00N - R0006 - Movement (3.25 m2)**

Panels Above Windows	Flat AC Sheeting	2m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
----------------------	------------------	-----	-------	--------------------	---------	--------------------

8114/B00N/R0006/Panels Above Windows/S20
Chrysotile (white asbestos) , Amosite (brown Asbestos)**B00N - R0007 - Movement (12 m2)**

Decorative Coating	Vermiculite 8114/B00N/R0007/Decorative Coating/S24					Limited Samples Taken
--------------------	---	--	--	--	--	-----------------------

Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works**B00N - R0008 - Laboratory L.S. (85.85 m2)**

Fume Cupboard	Flat AC Sheeting	1Unit	West	Good Condition (1)	Low (1)	Low Priority (2-3)
---------------	------------------	-------	------	--------------------	---------	--------------------

8114/B00N/R0011/Fume Cupboard/S17
Chrysotile (white asbestos) , Amosite (brown Asbestos)

Decorative Coating	Vermiculite 8114/B00N/R0007/Decorative Coating/S24					Limited Samples Taken
--------------------	---	--	--	--	--	-----------------------

Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works**B00N - R0011 - Laboratory L.S. (92.13 m2)**

Decorative Coating	Vermiculite 8114/B00N/R0007/Decorative Coating/S24					Limited Samples Taken
--------------------	---	--	--	--	--	-----------------------

Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

Fume Cupboard	Flat AC Sheeting	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
---------------	------------------	-------	------	--------------------	---------	--------------------

8114/B00N/R0011/Fume Cupboard/S17
Chrysotile (white asbestos) , Amosite (brown Asbestos)**B00N - R0015 - Movement (117.71 m2)**

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R0016 - Stairs (1.34 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R0017 - Stairs (1.34 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R0018 - Movement (4.55 m2)						
No Asbestos						
B00N - R0019 - Lift (2.1 m2)						
No Asbestos						
B00N - R0020 - Movement (1.53 m2)						
No Asbestos						
B00N - R0021 - Laundry (10.56 m2)						
No Asbestos						
B00N - R0022 - Toilets-Disabled (7.86 m2)						
No Asbestos						
B00N - R0023 - External Movement (28.43 m2)						
No Asbestos						
B00N - R0024 - Preparation - Science (38.97 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1001 - Staff Study (25.62 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1002 - Seminar (12.39 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1003 - Seminar (13.06 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1004 - Senior Study (53.29 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1005 - Careers Advisers Office (25.69 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1006 - Computer Learning Space (52.78 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1007 - General Learning Space (52.64 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1008 - General Storeroom (6.19 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1009 - General Storeroom (6.16 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1010 - Interview/Office - Type 1 (12.64 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1011 - General Storeroom (6.12 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1012 - General Learning Space (44.14 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1013 - General Learning Space (67.34 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1014 - General Storeroom (32.56 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1015 - Movement (106.14 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Sheet	8114/B00N/R1015/Floor Coverings Res/Textile/S18				No Asbestos Detected
B00N - R1016 - Stairs (14.58 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1017 - Stairs (14.87 m2)						
Decorative Coating	Vermiculite	8114/B00N/R0007/Decorative Coating/S24				Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00N - R1018 - External Movement (12.03 m2)						
No Asbestos						
B00N - R1019 - Movement (1.53 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B000 - Library/Science Learning - 1972 - Brick/Block (Brick/Block)**Exterior**

Gable Verge Lining	Flat AC Sheeting	10m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
8114/B000/Gable Verge Lining/S35					Chrysotile (white asbestos)	

Interior**B000 - R0001 - General Learning Space (58.6 m2)**

Floor Coverings Res/Textile	Vinyl Tiles	59m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8114/B000/R0006/Floor Coverings Res/Textile/S21					Chrysotile (white asbestos)	

Decorative Coating	Vermiculite	8114/B000/R0003/Decorative Coating/S23			Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

Floor Coverings Res/Textile	Adhesive	8114/B000/R0001/Floor Coverings Res/Textile/S36			No Asbestos Detected	
-----------------------------	----------	---	--	--	-----------------------------	--

B000 - R0002 - Preparation (43.79 m2)

Floor Coverings Res/Textile	Vinyl Tiles	44m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8114/B000/R0006/Floor Coverings Res/Textile/S21					Chrysotile (white asbestos)	

Decorative Coating	Vermiculite	8114/B000/R0003/Decorative Coating/S23			Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

Floor Coverings Res/Textile	Adhesive	8114/B000/R0001/Floor Coverings Res/Textile/S36			No Asbestos Detected	
-----------------------------	----------	---	--	--	-----------------------------	--

B000 - R0003 - Main Switchroom (7.35 m2)

Floor Coverings Res/Textile	Vinyl Tiles	8m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8114/B000/R0006/Floor Coverings Res/Textile/S21					Chrysotile (white asbestos)	

Decorative Coating	Vermiculite	8114/B000/R0003/Decorative Coating/S23			Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

Floor Coverings Res/Textile	Adhesive	8114/B000/R0001/Floor Coverings Res/Textile/S36			No Asbestos Detected	
-----------------------------	----------	---	--	--	-----------------------------	--

B000 - R0004 - Distribution Board Cupboard (0.95 m2)

Note: No inspection of live electrical installation.

Floor Coverings Res/Textile	Vinyl Tiles	1m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8114/B000/R0006/Floor Coverings Res/Textile/S21					Chrysotile (white asbestos)	

Floor Coverings Res/Textile	Adhesive	8114/B000/R0001/Floor Coverings Res/Textile/S36			No Asbestos Detected	
-----------------------------	----------	---	--	--	-----------------------------	--

B000 - R0005 - Cleaning Store - Distributed (0.64 m2)

Floor Coverings Res/Textile	Vinyl Tiles	1m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8114/B000/R0006/Floor Coverings Res/Textile/S21					Chrysotile (white asbestos)	

Floor Coverings Res/Textile	Adhesive	8114/B000/R0001/Floor Coverings Res/Textile/S36			No Asbestos Detected	
-----------------------------	----------	---	--	--	-----------------------------	--

B000 - R0006 - Movement (3.81 m2)

Floor Coverings Res/Textile	Vinyl Tiles	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8114/B000/R0006/Floor Coverings Res/Textile/S21					Chrysotile (white asbestos)	

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Decorative Coating	Vermiculite 8114/B000/R0003/Decorative Coating/S23					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Adhesive 8114/B000/R0001/Floor Coverings Res/Textile/S36					No Asbestos Detected
B000 - R0007 - Staff - Toilet (3.02 m2)						
No Asbestos						
B000 - R0008 - Staff - Toilet (3.04 m2)						
No Asbestos						
B000 - R0009 - Chemical Store (22.88 m2)						
Floor Coverings Res/Textile	Vinyl Tiles 8114/B000/R0006/Floor Coverings Res/Textile/S21	23m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive 8114/B000/R0001/Floor Coverings Res/Textile/S36					No Asbestos Detected
B000 - R0010 - Laboratory L.S. (91.41 m2)						
Decorative Coating	Vermiculite 8114/B000/R0003/Decorative Coating/S23					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
B000 - R0011 - Laboratory L.S. (91.41 m2)						
Floor Coverings Res/Textile	Vinyl Tiles 8114/B000/R0006/Floor Coverings Res/Textile/S21	92m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Decorative Coating	Vermiculite 8114/B000/R0003/Decorative Coating/S23					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Adhesive 8114/B000/R0001/Floor Coverings Res/Textile/S36					No Asbestos Detected
B000 - R0012 - Movement (153.28 m2)						
No Asbestos						
B000 - R0013 - External Stairs (8.85 m2)						
No Asbestos						
B000 - R0014 - External Movement (10 m2)						
No Asbestos						
B000 - R1001 - Main Area (53.72 m2)						
No Asbestos						
B000 - R1002 - Workroom (11.27 m2)						
No Asbestos						
B000 - R1003 - General Storeroom (8.21 m2)						
No Asbestos						
B000 - R1004 - Librarian (5.82 m2)						
No Asbestos						
B000 - R1005 - Entry (29.05 m2)						
No Asbestos						
B000 - R1006 - Staff - Toilet (3.25 m2)						
No Asbestos						
B000 - R1007 - Distribution Board Cupboard (0.69 m2)						
Electrical Mounting Board	Resinous Board	2Unit	South	Good Condition (1)	Low (1)	Low Priority (2-3) Note: No inspection of live electrical installation. Assumed Asbestos - Electrical Hazard

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B000 - R1008 - Cleaning Store - Distributed (2.62 m2)						
No Asbestos						
B000 - R1009 - Staff - Toilet (3.26 m2)						
Incinerette	Encapsulated Insulation material within unit	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
Assumed Asbestos - Area inaccessible						
B000 - R1010 - General Storeroom (12.31 m2)						
No Asbestos						
B000 - R1011 - Audio Visual Workroom (12.75 m2)						
No Asbestos						
B000 - R1012 - Audio Visual Workroom (12.82 m2)						
No Asbestos						
B000 - R1013 - Workroom (12.85 m2)						
No Asbestos						
B000 - R1014 - Main Area (161.16 m2)						
No Asbestos						
B000 - R1015 - Movement (19 m2)						
No Asbestos						
B000 - R1016 - External Movement (10 m2)						
No Asbestos						
B000 - R1017 - External Stairs (8.85 m2)						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00P - Agricultural Science - 1884 - Brick/Block (Brick/Block)**Exterior**

Wall Cladding	Flat AC Sheeting	30m2	Throughout, Variable positions	Minimal Damage (2)	Low (1)	Low Priority (2-3)
	8114/B00P/Wall Cladding/S2					Chrysotile (white asbestos)
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	Non Accessible Area					
	- Area inaccessible					

Interior**B00P - R0001 - Plant Space (7.58 m2)**

Ceiling Structures/Linings	Flat AC Sheeting	8m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00P/R0002/Ceiling Structures/Linings/S3					Chrysotile (white asbestos)
Wall Linings Internal	Flat AC Sheeting	15m2	Throughout, Upper portion	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00P/R0002/Ceiling Structures/Linings/S3					Chrysotile (white asbestos)

B00P - R0002 - Movement (18.71 m2)

Ceiling Structures/Linings	Flat AC Sheeting	19m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00P/R0002/Ceiling Structures/Linings/S3					Chrysotile (white asbestos)

B00P - R0003 - Machine Storage (33.97 m2)

Ceiling Structures/Linings	Flat AC Sheeting	34m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00P/R0002/Ceiling Structures/Linings/S3					Chrysotile (white asbestos)

B00P - R0004 - Class Tools Storage (8.84 m2)

Ceiling Structures/Linings	Flat AC Sheeting	9m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8114/B00P/R0002/Ceiling Structures/Linings/S3					Chrysotile (white asbestos)

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00Q - Music - 1996 - Brick/Veneer (Brick/Veneer)**Exterior**

Ceiling Voids	No Asbestos Found
Underfloor Voids	No Asbestos Found

Interior**B00Q - R0001 - Music Learning Space (76.22 m2)**

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00Q - R0002 - Practice/Seminar (17.81 m2)

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00Q - R0003 - Music Store (17.56 m2)

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00Q - R0004 - Practice/Seminar (17.76 m2)

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00Q - R0005 - Movement (53.39 m2)

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00Q - R0006 - General Learning Space (43.22 m2)

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00Q - R0007 - General Learning Space (66.32 m2)

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00Q - R0008 - Staff Study (20.38 m2)

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00Q - R0009 - Movement (62.24 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00R - Physical Education - 2008 - Metal Shed (Metal Shed)

Exterior

Ceiling Voids	No Asbestos Found
Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible

Interior

B00R - R0001 - Gymnasium (70.06 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00S - Other - 2008 - Steel (Steel)

Exterior

Ceiling Voids	No Asbestos Found
Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible

Interior

B00S - R0001 - Store (83.66 m2)

No Asbestos

B00S - R0002 - Resource/Project Store (23.56 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00T - General Learning/Computer Learning - 2010 - Brick/Veneer (Brick/Veneer)

Exterior

Underfloor Voids - Slab on Ground Non Accessible Area
 - Area inaccessible

Ceiling Voids No Asbestos Found

Interior

B00T - R0001 - Computer Learning Space (91.72 m2)

No Asbestos

B00T - R0002 - Seminar - Type 1 (19.08 m2)

No Asbestos

B00T - R0003 - Computer Resource (9.72 m2)

No Asbestos

B00T - R0004 - Computer Store (9 m2)

No Asbestos

B00T - R0005 - External Movement (30.33 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Demountables

Demountable details as per the AMS records as of 15 Feb 2017.

NS 210 - D10949 - Home Science/Preparation Area/Laundry : Placement Date - 30/06/1995

Exterior

No Asbestos Found.

Interior

R1 - Food Technology L.S.

No Asbestos Found.

R2 - Laundry

No Asbestos Found.

R3 - Preparation-Materials

No Asbestos Found.

R4 - Entry

No Asbestos Found.

OS 601 - D10957 - Learning Unit - Standard/Withdrawal : Placement Date - 30/06/1995

Exterior

Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos	11.52 m2

Interior

R1 - Entry

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	8 m2

R2 - General Learning Space

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	55 m2

R3 - Store

Ceiling	Flat AC Sheet	Assumed Asbestos	10 m2
---------	---------------	------------------	-------

OS 601 - D11000 - Learning Unit - Standard/Withdrawal : Placement Date - 13/01/2015

Exterior

Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos	11.52 m2

Interior

R1 - Entry

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	8 m2

R2 - General Learning Space

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	55 m2

R3 - Store

Ceiling	Flat AC Sheet	Assumed Asbestos	10 m2
---------	---------------	------------------	-------

OS 601 - D14971 - Learning Unit - Standard/Withdrawal : Placement Date - 30/06/1995

Exterior

Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Eave Lining	Flat AC Sheet	Assumed Asbestos				11.52 m2
Interior						
R1 - Entry						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				8 m2
R2 - General Learning Space						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				55 m2
R3 - Store						
Ceiling	Flat AC Sheet	Assumed Asbestos				10 m2

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Listing of Electronic Attachments as of 22/03/2017

There are no asbestos related file attachment(s) for this school.

2017
