


Asbestos Register

(Hazardous Materials and Risk Assessment)

School : Gosford High School (8115)
Region : Hunter/Central Coast
State Electorate : Gosford
Local Government Area : Gosford

Initial Survey : Noel Arnold & Associates : 03 - Apr - 2008
Reviewed By : Grencap-NAA : 20 - Mar - 2015

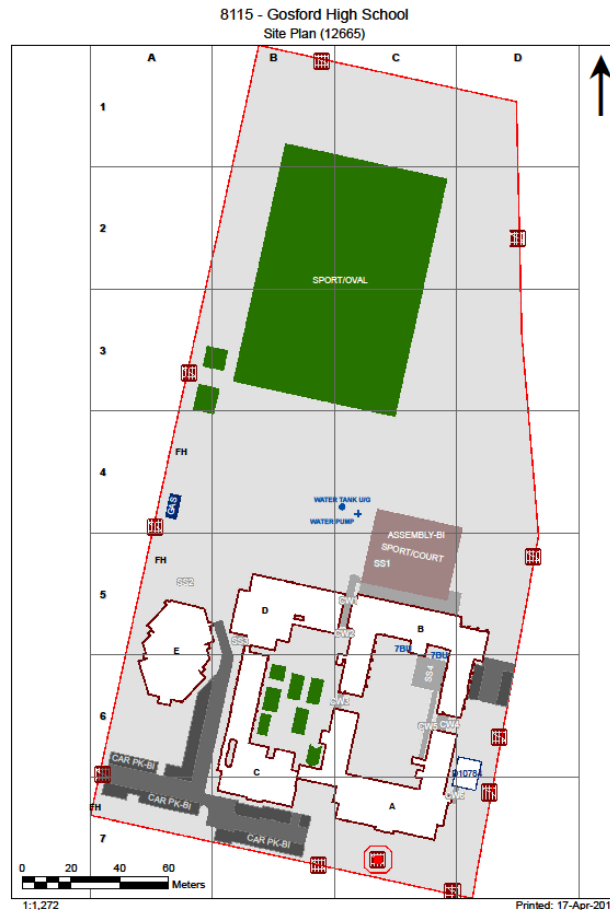

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00A - Administration/General Learning/Art - 1938 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids	Non Accessible Area - Extreme Access Issue - Obstructed Area - Access Hatch in middle of room and Hallway.					
Eaves Linings	Flat AC Sheeting	100m2	North facing, Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
Assumed Asbestos - Height Restriction - Height						
Ceiling Voids	Non Accessible Area - Height Restriction - Extreme Access Issue - Obstructed Area - Access Hatch in middle of room and Hallway.					
Underfloor Voids	Lagging	5m	Variable positions	Friable Asbestos (5)	Low (1)	Medium Priority (4-5)
Assumed Asbestos - Area inaccessible						

Interior

B00A - R0001 - Food Technology L.S. (95.89 m2)

No Asbestos

B00A - R0002 - Movement (2.11 m2)

Ceiling Structures/Linings	Flat AC Sheeting	3m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
8115/B00A/R2019/Ceiling Structures/Linings/S7				Chrysotile (white asbestos)		

B00A - R0004 - Preparation - Materials (10.2 m2)

Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected	

B00A - R0005 - Pantry (9.62 m2)

Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected	

B00A - R0006 - Computer Learning Space (82.96 m2)

No Asbestos

B00A - R0007 - Office/Store (3.99 m2)

No Asbestos

B00A - R0008 - Movement (42.46 m2)

No Asbestos

B00A - R0009 - Craft Store (10.41 m2)

No Asbestos

B00A - R0010 - Cleaning Store - Distributed (4.58 m2)

No Asbestos

B00A - R0011 - Art Learning Space (85.7 m2)

Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00A/R0016/Floor Coverings Res/Textile/S6					No Asbestos Detected	

B00A - R0012 - Project Store - Type 1 (11.99 m2)

Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00A/R0016/Floor Coverings Res/Textile/S6					No Asbestos Detected	

B00A - R0013 - Craft Store (11.82 m2)

Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00A/R0016/Floor Coverings Res/Textile/S6					No Asbestos Detected	

B00A - R0014 - Design/Technology L.S. (36.77 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R0016/Floor Coverings Res/Textile/S6					No Asbestos Detected
B00A - R0015 - Resources Store (8.49 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R0016/Floor Coverings Res/Textile/S6					No Asbestos Detected
B00A - R0016 - Art Learning Space (85.95 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R0016/Floor Coverings Res/Textile/S6					No Asbestos Detected
B00A - R0019 - Cleaning Store - Distributed (4.33 m2)						
No Asbestos						
B00A - R0020 - Art Learning Space (54.69 m2)						
No Asbestos						
B00A - R0021 - General Learning Space (54.48 m2)						
No Asbestos						
B00A - R0022 - General Learning Space (54.31 m2)						
No Asbestos						
B00A - R0023 - Staff - Toilet (11.09 m2)						
No Asbestos						
B00A - R0024 - External Movement (2.75 m2)						
No Asbestos						
B00A - R0026 - External Movement (2.63 m2)						
No Asbestos						
B00A - R0027 - External Movement (69.08 m2)						
No Asbestos						
B00A - R0028 - External Movement (92.67 m2)						
No Asbestos						
B00A - R0029 - Stairs (6.96 m2)						
No Asbestos						
B00A - R0030 - Stairs (7.32 m2)						
No Asbestos						
B00A - R0032 - Stairs (4.77 m2)						
No Asbestos						
B00A - R0033 - Laundry (13.56 m2)						
No Asbestos						
B00A - R0034 - Staff Study (27.17 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R0016/Floor Coverings Res/Textile/S6					No Asbestos Detected
B00A - R0035 - Tea Room (2.93 m2)						
No Asbestos						
B00A - R0036 - Staff Study (8.46 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R0016/Floor Coverings Res/Textile/S6					No Asbestos Detected
B00A - R0037 - Movement (90.1 m2)						
No Asbestos						
B00A - R0038 - Handwashing Facilities (0.36 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00A - R0039 - Kiln Space (6.88 m2)						
Ceiling Structures/Linings	Flat AC Sheeting					
		8115/B00A/R0039/Ceiling Structures/Linings/S41				No Asbestos Detected
B00A - R0040 - Interview/Office - Type 1 (4.01 m2)						
No Asbestos						
B00A - R0041 - Lift (2.24 m2)						
No Asbestos						
B00A - R1001 - General Learning Space (55.22 m2)						
No Asbestos						
B00A - R1002 - General Learning Space (54.35 m2)						
No Asbestos						
B00A - R1003 - General Learning Space (54.28 m2)						
No Asbestos						
B00A - R1004 - Leading Teacher (9.41 m2)						
No Asbestos						
B00A - R1005 - Leading Teacher (13.99 m2)						
No Asbestos						
B00A - R1006 - Interview/Office - Type 1 (13.74 m2)						
No Asbestos						
B00A - R1008 - Printing/Photocopying (26.51 m2)						
No Asbestos						
B00A - R1009 - Principal Office (26.27 m2)						
No Asbestos						
B00A - R1010 - Public Reception (49.49 m2)						
No Asbestos						
B00A - R1011 - External Movement (3.58 m2)						
No Asbestos						
B00A - R1013 - Resources Store (12.2 m2)						
No Asbestos						
B00A - R1014 - General Learning Space (58.39 m2)						
No Asbestos						
B00A - R1015 - General Learning Space (56.14 m2)						
No Asbestos						
B00A - R1016 - General Learning Space (57.28 m2)						
No Asbestos						
B00A - R1017 - Archive Store (8.6 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
		8115/B00A/R1019/Floor Coverings Res/Textile/S4				No Asbestos Detected
B00A - R1018 - Cleaning Store - Distributed (3.51 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
		8115/B00A/R1027/Floor Coverings Res/Textile/S3				No Asbestos Detected
B00A - R1019 - Staff - Toilet (7.37 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
		8115/B00A/R1019/Floor Coverings Res/Textile/S4				No Asbestos Detected
B00A - R1020 - Staff - Toilet (5.89 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
		8115/B00A/R1019/Floor Coverings Res/Textile/S4				No Asbestos Detected

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00A - R1021 - Deputy Principal Office (24.1 m2)						
No Asbestos						
B00A - R1022 - Deputy Principal Office (17.13 m2)						
No Asbestos						
B00A - R1023 - Administration - Clerical (30.28 m2)						
No Asbestos						
B00A - R1024 - Administration - Clerical (13.68 m2)						
No Asbestos						
B00A - R1025 - Administration - Clerical (14.58 m2)						
No Asbestos						
B00A - R1028 - Toilets-Unisex (3.91 m2)						
No Asbestos						
B00A - R1029 - General Storeroom (1.68 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00A/R1027/Floor Coverings Res/Textile/S3					No Asbestos Detected	
B00A - R1030 - Distribution Board Cupboard (0.7 m2)						
Note: No inspection of live electrical installation.						
Ceiling Structures/Linings	Flat AC Sheeting	1m2	All surfaces	Some Damage / Unsealed (3)	Low (1)	Low Priority (2-3)
8115/B00A/R1030/Ceiling Structures/Linings/S5					Chrysotile (white asbestos)	
Debris	Flat AC Sheeting	0.5m2	East facing	Some Damage - Unsealed (3)	Medium (2)	Medium Priority (4-5)
8115/B00A/R1030/Ceiling Structures/Linings/S5					Chrysotile (white asbestos)	
Wall Linings Internal	Flat AC Sheeting	3m2	Surrounding	Minimal Damage (2)	Low (1)	Low Priority (2-3)
8115/B00A/R1030/Ceiling Structures/Linings/S5					Chrysotile (white asbestos)	
B00A - R1031 - General Storeroom (9.43 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00A/R1027/Floor Coverings Res/Textile/S3					No Asbestos Detected	
B00A - R1032 - Music Store (3.5 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00A/R1027/Floor Coverings Res/Textile/S3					No Asbestos Detected	
B00A - R1034 - Movement (50.81 m2)						
No Asbestos						
B00A - R1036 - External Movement (3.26 m2)						
No Asbestos						
B00A - R1037 - External Movement (2.17 m2)						
No Asbestos						
B00A - R1038 - External Movement (2.16 m2)						
No Asbestos						
B00A - R1039 - External Movement (1.97 m2)						
No Asbestos						
B00A - R1040 - Stairs (12.03 m2)						
No Asbestos						
B00A - R1041 - Stairs (12.05 m2)						
No Asbestos						
B00A - R1045 - Movement (13.79 m2)						
No Asbestos						
B00A - R1046 - Student Waiting (16.25 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00A - R1047 - General Storeroom (7.71 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R0016/Floor Coverings Res/Textile/S6					No Asbestos Detected
B00A - R1048 - Clinic (15.62 m2)						
No Asbestos						
B00A - R1049 - Commonroom (94.08 m2)						
No Asbestos						
B00A - R1050 - Staff Kitchen (17.92 m2)						
No Asbestos						
B00A - R1051 - Movement (35.23 m2)						
No Asbestos						
B00A - R1052 - Movement (107.73 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	10m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/B00A/R1052/Ceiling Structures/Linings/S40					Chrysotile (white asbestos)
B00A - R1053 - Movement (112.86 m2)						
No Asbestos						
B00A - R1054 - Movement (4 m2)						
No Asbestos						
B00A - R2001 - Seminar (29.96 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2004 - General Learning Space (55.06 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2005 - Staff - Toilet (4.73 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2006 - Staff - Toilet (4.64 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2007 - Interview/Office - Type 1 (21.22 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2008 - General Learning Space (58.35 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2009 - General Learning Space (55.46 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2010 - General Learning Space (57.58 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2011 - General Learning Space (56.71 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2012 - General Learning Space (59.2 m2)						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2013 - Uniform Shop (20.65 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2014 - General Learning Space (53.73 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2015 - Resources Store (14.16 m2)						
No Asbestos						
B00A - R2016 - General Learning Space (28.26 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2017 - General Learning Space (55.09 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2019 - External Movement (1.97 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	2m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/B00A/R2019/Ceiling Structures/Linings/S7					Chrysotile (white asbestos)
B00A - R2020 - Stairs (11.64 m2)						
No Asbestos						
B00A - R2021 - Stairs (11.18 m2)						
No Asbestos						
B00A - R2023 - Resources Store (12.22 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2024 - Resources Store (11.42 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2025 - Staff Study (51.66 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2026 - Tea Room (4.62 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00A/R1019/Floor Coverings Res/Textile/S4					No Asbestos Detected
B00A - R2029 - Movement (173.25 m2)						
No Asbestos						
B00A - R2030 - Movement (3.98 m2)						
No Asbestos						
B00A - R9001 - Computer Store (25.56 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00B - Science Learning/Pupil Facilities/General Learning - 1970 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids	Non Accessible Area - Area inaccessible					
Ceiling Voids	Non Accessible Area - Height Restriction					
Window Frame	Mastic	10m	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/B00B/Window Frame/S38				Chrysotile (white asbestos)	
Window Beading	Mastic					No Asbestos Detected
	8115/B00B/Window Beading/S39					
Gable Verge Lining	Flat AC Sheeting	10m	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Height Restriction					
Gable Verge Lining	Non Accessible Area - Extreme Access Issue - Height Restricted - Approx >10m High					

Interior

B00B - R0002 - Office/Store (2.71 m2)

No Asbestos

B00B - R0003 - Pantry (7.87 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					

B00B - R0004 - Staff - Toilet (3.72 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					

B00B - R0006 - Main Switchroom (10.62 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					

B00B - R0009 - Change (52.09 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					

Partition Walls (Cubicles)	Compressed AC Sheet	20m2	West facing	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/B00B/R0009/Partition Walls (Cubicles)/S11					
	Chrysotile (white asbestos)					

B00B - R0014 - Staff - Toilet (5.23 m2)

No Asbestos

B00B - R0015 - Sport Equipment Store (18.09 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					

B00B - R0016 - Toilets-Boys (50.49 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					

B00B - R0017 - Change (52.3 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R0017/Ceiling Structures/Linings/S36					
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					

B00B - R0021 - External Movement (16.78 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
No Asbestos						
B00B - R0022 - External Stairs (9.7 m2)						
No Asbestos						
B00B - R0023 - External Stairs (15.37 m2)						
No Asbestos						
B00B - R0025 - Multi Media L.S. (70.58 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R0032/Ceiling Structures/Linings/S35			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0026 - Tea Room (5.64 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R0032/Ceiling Structures/Linings/S35			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0027 - Interview/Office - Type 1 (11.21 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R0032/Ceiling Structures/Linings/S35			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0028 - Student Canteen (51.82 m2)						
No Asbestos						
B00B - R0029 - Store - Coolroom (3.04 m2)						
No Asbestos						
B00B - R0030 - External Movement (5.7 m2)						
No Asbestos						
B00B - R0031 - Student Lounge (64.84 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R0032/Ceiling Structures/Linings/S35			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0032 - Careers Advisers Office (14.57 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R0032/Ceiling Structures/Linings/S35			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0033 - Tea Room (9.53 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R0032/Ceiling Structures/Linings/S35			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0034 - External Movement (15.37 m2)						
No Asbestos						
B00B - R0035 - Covered Area (218.33 m2)						
No Asbestos						
B00B - R0036 - External Movement (162.59 m2)						
No Asbestos						
B00B - R0037 - Toilets-Girls (68.19 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R0039/Ceiling Structures/Linings/S37			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0038 - Plant (3.74 m2)						
No Asbestos						
B00B - R0040 - Movement (4.18 m2)						
No Asbestos						
B00B - R0041 - Lift (2.24 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00B - R0042 - Plant (1.83 m2)						
No Asbestos						
B00B - R0043 - Sport Equipment Store (26.15 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R0044/Ceiling Structures/Linings/S43			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R0044/Ceiling Structures/Linings/S43			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R0044 - External Movement (136.87 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R0044/Ceiling Structures/Linings/S43			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R0044/Ceiling Structures/Linings/S43			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1001 - Preparation - Science (28.75 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R1021/Ceiling Structures/Linings/S9			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1002 - Resources Store (9.74 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R1021/Ceiling Structures/Linings/S9			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1003 - Laboratory L.S. (92.26 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R1021/Ceiling Structures/Linings/S9			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1004 - Apparatus Store (12.56 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R1021/Ceiling Structures/Linings/S9			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1005 - Distribution Board Cupboard (0.42 m2)						
						Note: No inspection of live electrical installation.
No Asbestos						
B00B - R1006 - Chemical Store (12.94 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R1021/Ceiling Structures/Linings/S9			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1007 - Staff - Toilet (3.19 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R1021/Ceiling Structures/Linings/S9			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1008 - Cleaning Store - Distributed (1.83 m2)						
No Asbestos						
B00B - R1009 - Laboratory L.S. (86.05 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R1021/Ceiling Structures/Linings/S9			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1010 - Preparation - Science (25.93 m2)						
Ceiling Structures/Linings	Vermiculite		8115/B00B/R1021/Ceiling Structures/Linings/S9			Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		
Heat-proof Mat	Flat AC Sheeting	2Unit	Variable positions	Good Condition (1)	Medium (2)	Low Priority (2-3)
	8115/B00B/R1010/Heat-proof Mat/S33			Chrysotile (white asbestos) , Amosite (brown asbestos)		
B00B - R1011 - Laboratory L.S. (79.76 m2)						
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R1012 - Laboratory L.S. (92.65 m2)						
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R1015 - Laboratory L.S. (85.81 m2)						
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R1016 - Staff - Toilet (4.92 m2)						
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R1018 - Laboratory L.S. (92.62 m2)						
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R1020 - Distribution Board Cupboard (0.36 m2)						
						Note: No inspection of live electrical installation.
No Asbestos						
B00B - R1022 - External Movement (10.98 m2)						
No Asbestos						
B00B - R1023 - External Stairs (21.31 m2)						
No Asbestos						
B00B - R1024 - External Stairs (19.81 m2)						
No Asbestos						
B00B - R1025 - External Stairs (15.39 m2)						
No Asbestos						
B00B - R1026 - Preparation - Science (39.12 m2)						
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R1027 - Staff Study (35.07 m2)						
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R1028 - Tea Room (3.96 m2)						
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R1029 - Staff Lounge (23.49 m2)						
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00B/R1021/Ceiling Structures/Linings/S9					<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00B - R1030 - Tea Room (2.17 m2)						
Recently Modified Space	Requires Inspection					
B00B - R1031 - External Movement (260.53 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite	8115/B00B/R1031/Ceiling Structures/Linings/S34			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R1032 - Movement (4.18 m2)						
No Asbestos						
B00B - R2002 - General Storeroom (6.09 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Sheet	8115/B00B/R2039/Floor Coverings Res/Textile/S31			No Asbestos Detected	
B00B - R2003 - Resources Store (6.16 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Sheet	8115/B00B/R2039/Floor Coverings Res/Textile/S31			No Asbestos Detected	
B00B - R2004 - General Learning Space (52.44 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R2006 - Distribution Board Cupboard (0.71 m2)					Note: No inspection of live electrical installation.	
No Asbestos						
B00B - R2007 - Staff - Toilet (3.38 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R2008 - Cleaning Store - Distributed (1.85 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R2009 - Music Learning Space (58.65 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Sheet	8115/B00B/R2039/Floor Coverings Res/Textile/S31			No Asbestos Detected	
B00B - R2010 - Staff Study (26.58 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Sheet	8115/B00B/R2039/Floor Coverings Res/Textile/S31			No Asbestos Detected	
B00B - R2011 - Music Learning Space (51.94 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Sheet	8115/B00B/R2039/Floor Coverings Res/Textile/S31			No Asbestos Detected	
B00B - R2014 - General Learning Space (51.5 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Sheet	8115/B00B/R2039/Floor Coverings Res/Textile/S31			No Asbestos Detected	
B00B - R2015 - General Learning Space (51.43 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Sheet	8115/B00B/R2039/Floor Coverings Res/Textile/S31			No Asbestos Detected	
B00B - R2016 - General Learning Space (58.63 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Sheet	8115/B00B/R2039/Floor Coverings Res/Textile/S31			No Asbestos Detected	
B00B - R2017 - Staff - Toilet (5.14 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R2018 - General Learning Space (52.09 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Sheet	8115/B00B/R2039/Floor Coverings Res/Textile/S31			No Asbestos Detected	
B00B - R2019 - Toilets-Disabled (11.84 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R2020 - Staff Study (12.14 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Sheet	8115/B00B/R2039/Floor Coverings Res/Textile/S31			No Asbestos Detected	
B00B - R2022 - Resources Store (6.23 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R2023 - Resources Store (6.23 m2)						
Ceiling Structures/Linings	Vermiculite	8115/B00B/R2036/Ceiling Structures/Linings/S32			Limited Samples Taken	
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R2025 - Distribution Board Cupboard (0.71 m2)					Note: No inspection of live electrical installation.	
No Asbestos						
B00B - R2027 - External Movement (10.98 m2)						
No Asbestos						
B00B - R2028 - External Stairs (10.08 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

No Asbestos

B00B - R2029 - Performance Workspace (105.62 m2)

Ceiling Structures/Linings Vermiculite
 8115/B00B/R2036/Ceiling Structures/Linings/S32 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

Floor Coverings Res/Textile Vinyl Sheet
 8115/B00B/R2039/Floor Coverings Res/Textile/S31 **No Asbestos Detected**

B00B - R2030 - External Stairs (19.81 m2)

No Asbestos

B00B - R2031 - External Stairs (20.51 m2)

No Asbestos

B00B - R2032 - Staff Lounge (23.31 m2)

Ceiling Structures/Linings Vermiculite
 8115/B00B/R2036/Ceiling Structures/Linings/S32 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

Floor Coverings Res/Textile Vinyl Sheet
 8115/B00B/R2039/Floor Coverings Res/Textile/S31 **No Asbestos Detected**

B00B - R2033 - Tea Room (1.97 m2)

Ceiling Structures/Linings Vermiculite
 8115/B00B/R2036/Ceiling Structures/Linings/S32 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

Floor Coverings Res/Textile Vinyl Sheet
 8115/B00B/R2039/Floor Coverings Res/Textile/S31 **No Asbestos Detected**

B00B - R2034 - Staff Study (36.21 m2)

Ceiling Structures/Linings Vermiculite
 8115/B00B/R2036/Ceiling Structures/Linings/S32 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

Floor Coverings Res/Textile Vinyl Sheet
 8115/B00B/R2039/Floor Coverings Res/Textile/S31 **No Asbestos Detected**

B00B - R2035 - Tea Room (1.96 m2)

Ceiling Structures/Linings Vermiculite
 8115/B00B/R2036/Ceiling Structures/Linings/S32 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

Floor Coverings Res/Textile Vinyl Sheet
 8115/B00B/R2039/Floor Coverings Res/Textile/S31 **No Asbestos Detected**

B00B - R2036 - Staff Study (20.21 m2)

Ceiling Structures/Linings Vermiculite
 8115/B00B/R2036/Ceiling Structures/Linings/S32 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

Floor Coverings Res/Textile Vinyl Sheet
 8115/B00B/R2039/Floor Coverings Res/Textile/S31 **No Asbestos Detected**

B00B - R2037 - Tea Room (6.3 m2)

Ceiling Structures/Linings Vermiculite
 8115/B00B/R2036/Ceiling Structures/Linings/S32 **Limited Samples Taken**
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

Floor Coverings Res/Textile Vinyl Sheet
 8115/B00B/R2039/Floor Coverings Res/Textile/S31 **No Asbestos Detected**

B00B - R2038 - General Learning Space (64.1 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00B/R2039/Floor Coverings Res/Textile/S31					No Asbestos Detected
Ceiling Structures/Linings	Vermiculite					
	8115/B00B/R2036/Ceiling Structures/Linings/S32					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00B - R2039 - Handwashing Facilities (1.79 m2)						
Floor Coverings Res/Textile	Millboard					
	8115/B00B/R2039/Floor Coverings Res/Textile/S30					No Asbestos Detected
Floor Coverings Res/Textile	Vinyl Sheet					
	8115/B00B/R2039/Floor Coverings Res/Textile/S31					No Asbestos Detected
B00B - R2040 - Movement (4.18 m2)						
No Asbestos						
B00B - R2041 - External Movement (255.49 m2)						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00C - Technological & Applied Studies - 1938 - Brick/Block (Brick/Block)**Exterior**

Gable Verge Lining	Flat AC Sheeting	20m	North facing, South facing	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/B00C/Gable Verge Lining/S43					Chrysotile (white asbestos)
Underfloor Voids	No Asbestos Found					
Ceiling Voids	Non Accessible Area - Height Restriction					
Debris to ground	AC Fragments/Debris	0.5m2	West	Poor Condition - Extensive Damage (4)	Medium (2)	Low Priority (2-3)

Interior**B00C - R0002 - Distribution Board Cupboard (0.73 m2)**

Note: No inspection of live electrical installation.

Ceiling Structures/Linings	Flat AC Sheeting	1m2	Throughout	Some Damage - Unsealed (3)	Low (1)	Low Priority (2-3)
	8115/B00C/R0002/Ceiling Structures/Linings/S27					Chrysotile (white asbestos)

B00C - R0004 - Design L.S. (70.55 m2)

No Asbestos

B00C - R0005 - Resources Store (24.08 m2)

No Asbestos

B00C - R0006 - Resources Store (8.38 m2)

Ceiling Structures/Linings	Flat AC Sheeting					No Asbestos Detected
	8115/B00C/R0010/Ceiling Structures/Linings/S24					

B00C - R0007 - Dust Extraction Space (5.55 m2)

Ceiling Structures/Linings	Flat AC Sheeting					No Asbestos Detected
	8115/B00C/R0010/Ceiling Structures/Linings/S24					

Air Conditioning Unit	Mastic	1Unit	Ductwork joints	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/B00C/R0007/Air Conditioning Unit/S25					Chrysotile (white asbestos)

Floor	Corrugated AC Sheeting					No Asbestos Detected
	8115/B00C/R0007/Floor/S26					

B00C - R0008 - Resources Store (8.95 m2)

Ceiling Structures/Linings	Flat AC Sheeting					No Asbestos Detected
	8115/B00C/R0010/Ceiling Structures/Linings/S24					

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)					No Asbestos Detected
	8115/B00A/R1027/Floor Coverings Res/Textile/S3					

B00C - R0009 - Wood Technology L.S. (98.24 m2)

No Asbestos

B00C - R0010 - Materials Store (21.61 m2)

Ceiling Structures/Linings	Flat AC Sheeting					No Asbestos Detected
	8115/B00C/R0010/Ceiling Structures/Linings/S24					

B00C - R0012 - Staff - Toilet (4.75 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00C/R0012/Ceiling Structures/Linings/S8					
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

B00C - R0013 - Staff - Toilet (4.83 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8115/B00C/R0012/Ceiling Structures/Linings/S8					
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

B00C - R0014 - Metal Technology L.S. (108.76 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite					
	8115/B00C/R0012/Ceiling Structures/Linings/S8					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
B00C - R0015 - Project Store - Type 1 (9.67 m2)						
Ceiling Structures/Linings	Vermiculite					
	8115/B00C/R0012/Ceiling Structures/Linings/S8					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Floor Coverings Res/Textile	Resinous Membrane					
	8115/B00C/R0015/Floor Coverings Res/Textile/S21					No Asbestos Detected
B00C - R0016 - Wood Technology L.S. (96.61 m2)						
Ceiling Structures/Linings	Vermiculite					
	8115/B00C/R0012/Ceiling Structures/Linings/S8					Limited Samples Taken
	<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>					
Adhesive to concrete floor	Bituminous material	97m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/B00C/R0016/Adhesive to concrete floor/S22					Chrysotile (white asbestos)
B00C - R0017 - General Storeroom (8.47 m2)						
Adhesive to concrete floor	Bituminous material	8m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/B00C/R0016/Adhesive to concrete floor/S22					Chrysotile (white asbestos)
B00C - R0018 - Materials Store (10.49 m2)						
No Asbestos						
B00C - R0019 - Distribution Board Cupboard (0.75 m2)						
				Note: No inspection of live electrical installation.		
Ceiling Structures/Linings	Flat AC Sheeting	1m2	All surfaces	Minimal Damage (2)	Low (1)	Low Priority (2-3)
	8115/B00A/R1030/Ceiling Structures/Linings/S5					Chrysotile (white asbestos)
B00C - R0022 - Movement (91.61 m2)						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)					
	8115/B00A/R1027/Floor Coverings Res/Textile/S3					No Asbestos Detected
B00C - R0024 - External Movement (17.25 m2)						
No Asbestos						
B00C - R0025 - Staff Study (18.67 m2)						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)					
	8115/B00A/R1027/Floor Coverings Res/Textile/S3					No Asbestos Detected
B00C - R0026 - Tea Room (4.68 m2)						
No Asbestos						
B00C - R0027 - Textiles Technology L.S. (52.78 m2)						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)					
	8115/B00A/R1027/Floor Coverings Res/Textile/S3					No Asbestos Detected
B00C - R0028 - Handwashing Facilities (3.91 m2)						
No Asbestos						
B00C - R0029 - Textiles Technology L.S. (53.61 m2)						
No Asbestos						
B00C - R0030 - Handwashing Facilities (3.96 m2)						
No Asbestos						
B00C - R0031 - Staff Study (18.71 m2)						
Cupboard	Vinyl Sheet					
	8115/B00C/R0031/Cupboard/S28					No Asbestos Detected
B00C - R0032 - Tea Room (3.55 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00C - R0033 - External Movement (33.96 m2)						
Infill panels	Flat AC Sheeting	3m2	Above window	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/B00C/R0033/Infill panels/S29					Chrysotile (white asbestos)
Awning	Flat AC Sheeting	3m2	Above window	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/B00C/R0033/Infill panels/S29					Chrysotile (white asbestos)
B00C - R0034 - Welding Area (4.49 m2)						
No Asbestos						
B00C - R0035 - Welding Area (4.74 m2)						
No Asbestos						
B00C - R0036 - External Movement (123.93 m2)						
No Asbestos						
B00C - R9001 - Tea Room (18.02 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R1027/Floor Coverings Res/Textile/S3					No Asbestos Detected
B00C - R9002 - Garden Store Room (18.49 m2)						
No Asbestos						
B00C - R9003 - Cleaning Supplies Store (19.49 m2)						
No Asbestos						
B00C - R9005 - General Assistants (29.52 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R1027/Floor Coverings Res/Textile/S3					No Asbestos Detected
B00C - R9008 - General Storeroom (94.88 m2)						
No Asbestos						
B00C - R9009 - Darkroom Space (12.7 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R1027/Floor Coverings Res/Textile/S3					No Asbestos Detected
B00C - R9010 - Dark Room (16.98 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R1027/Floor Coverings Res/Textile/S3					No Asbestos Detected
B00C - R9011 - Resources Store (1.32 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
	8115/B00A/R1027/Floor Coverings Res/Textile/S3					No Asbestos Detected
B00C - R9012 - General Storeroom (8.01 m2)						
Stored item	Flat AC Sheeting					
	8115/B00C/R9012/Stored item/S20					No Asbestos Detected
B00C - R9013 - General Storeroom (37.88 m2)						
No Asbestos						
B00C - R9014 - Dust Extraction Space (4.77 m2)						
No Asbestos						
B00C - R9015 - General Storeroom (16.58 m2)						
No Asbestos						
B00C - R9016 - Sport Equipment Store (35.01 m2)						
No Asbestos						
B00C - R9017 - General Storeroom (23.54 m2)						
No Asbestos						
B00C - R9018 - General Storeroom (17.12 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

No Asbestos

B00C - R9019 - General Storeroom (2.84 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00D - Library/General Learning - 1983 - Brick/Block (Brick/Block)

Exterior

Wall Cladding	Flat AC Sheeting 8115/B00D/Wall Cladding/S12					No Asbestos Detected
Eaves Linings	Flat AC Sheeting 8115/B00D/R1024/Eaves Lining/S16	70m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Underfloor Voids - Slab on Ground	No Asbestos Found					
Window Frame	Mastic 8115/B00D/Window Frame/S18	20m	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Ceiling Voids	No Asbestos Found					
Ceiling Voids	Non Accessible Area - Height Restriction					

Interior

B00D - R0001 - General Learning Space (47.55 m2)

No Asbestos

B00D - R0005 - General Learning Space (42.68 m2)

Floor Coverings Res/Textile	No Asbestos Found
Floor Coverings Res/Textile	No Asbestos Found
Floor Coverings Res/Textile	No Asbestos Found

B00D - R0006 - General Learning Space (47.13 m2)

No Asbestos

B00D - R0007 - Movement (16.22 m2)

Floor Coverings Res/Textile	No Asbestos Found
Floor Coverings Res/Textile	No Asbestos Found
Floor Coverings Res/Textile	No Asbestos Found

B00D - R0008 - Library Administration (43.77 m2)

Floor Coverings Res/Textile	No Asbestos Found
Floor Coverings Res/Textile	No Asbestos Found
Floor Coverings Res/Textile	No Asbestos Found

B00D - R0009 - Distribution Board Cupboard (0.98 m2)

Note: No inspection of live electrical installation.

No Asbestos

B00D - R0010 - Librarian (13.7 m2)

No Asbestos

B00D - R0011 - Audio Visual Workroom (39.45 m2)

Fire Door	Encapsulated Insulation material within unit	2Unit	East & West	Friable Asbestos (5)	Low (1)	Low Priority (2-3) Assumed Asbestos - Encased material
-----------	--	-------	-------------	----------------------	---------	--

B00D - R0012 - Staff - Toilet (4.14 m2)

No Asbestos

B00D - R0013 - Cleaning Store - Distributed (0.73 m2)

No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00D - R0014 - Staff - Toilet (4.31 m2)						
No Asbestos						
B00D - R0015 - Movement (8.51 m2)						
Floor Coverings Res/Textile	No Asbestos Found					
Floor Coverings Res/Textile	No Asbestos Found					
Floor Coverings Res/Textile	No Asbestos Found					
B00D - R0016 - Main Area (344.25 m2)						
No Asbestos						
B00D - R0017 - Office/Store (23.22 m2)						
No Asbestos						
B00D - R0018 - Seminar (28.41 m2)						
No Asbestos						
B00D - R0020 - Stairs (0.52 m2)						
No Asbestos						
B00D - R0021 - Resources Store (5.7 m2)						
Floor Coverings Res/Textile	No Asbestos Found					
Floor Coverings Res/Textile	No Asbestos Found					
Floor Coverings Res/Textile	No Asbestos Found					
B00D - R0022 - Staff Study (25.48 m2)						
No Asbestos						
B00D - R0023 - External Movement (12.95 m2)						
Infil Panels	Flat AC Sheeting	3m2	Above window	Minimal Damage (2)	Low (1)	Low Priority (2-3)
8115/B00D/R0023/Infil Panels/S19				Chrysotile (white asbestos) , Amosite (brown asbestos)		
B00D - R0024 - External Movement (9 m2)						
No Asbestos						
B00D - R0025 - External Movement (140.91 m2)						
No Asbestos						
B00D - R1001 - Computer Learning Space (57.31 m2)						
No Asbestos						
B00D - R1002 - Independent Learning Space (19.65 m2)						
Floor Coverings Res/Textile	No Asbestos Found					
Floor Coverings Res/Textile	No Asbestos Found					
Floor Coverings Res/Textile	No Asbestos Found					
B00D - R1004 - Computer Learning Space (74.3 m2)						
No Asbestos						
B00D - R1005 - Movement (7.57 m2)						
No Asbestos						
B00D - R1010 - Senior Study (60.1 m2)						
No Asbestos						
B00D - R1011 - Seminar (22.13 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00D - R1012 - General Learning Space (50.5 m2)						
No Asbestos						
B00D - R1013 - General Learning Space (47.56 m2)						
No Asbestos						
B00D - R1015 - General Learning Space (48.35 m2)						
No Asbestos						
B00D - R1016 - Resources Store (10.98 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00D/R1016/Floor Coverings Res/Textile/S15					No Asbestos Detected	
B00D - R1017 - General Learning Space (49.75 m2)						
No Asbestos						
B00D - R1018 - Movement (58.06 m2)						
Floor Coverings Res/Textile	No Asbestos Found					
Floor Coverings Res/Textile	No Asbestos Found					
Floor Coverings Res/Textile	No Asbestos Found					
B00D - R1020 - Stairs (6.21 m2)						
No Asbestos						
B00D - R1021 - External Movement (7.6 m2)						
No Asbestos						
B00D - R1022 - Museum (21.57 m2)						
No Asbestos						
B00D - R1023 - Tea Room (3.04 m2)						
No Asbestos						
B00D - R1024 - External Movement (54.49 m2)						
Eaves Lining	Flat AC Sheeting	10m2	West	Good Condition (1)	Low (1)	Low Priority (2-3)
8115/B00D/R1024/Eaves Lining/S16					Chrysotile (white asbestos)	
B00D - R1025 - Staff Study (24.17 m2)						
No Asbestos						
B00D - R1026 - Tea Room (2.05 m2)						
No Asbestos						
B00D - R1027 - Staff Study (23.28 m2)						
No Asbestos						
B00D - R1028 - Staff Study (58.06 m2)						
Floor Coverings Res/Textile	No Asbestos Found					
Floor Coverings Res/Textile	No Asbestos Found					
Floor Coverings Res/Textile	No Asbestos Found					
B00D - R1029 - Tea Room (6.3 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00E - Multi Purpose Facilities - 1983 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids	AC Fragments/Debris 8115/B00E/Underfloor Voids/S14					No Asbestos Detected
Ceiling Voids	Non Accessible Area - Height Restriction					

Interior

B00E - M0001 - Change (15.91 m2)						
No Asbestos						
B00E - M0002 - Toilets-Girls (1.73 m2)						
No Asbestos						
B00E - M0003 - Shower (1.68 m2)						
No Asbestos						
B00E - M0004 - Movement (4.19 m2)						
No Asbestos						
B00E - M0005 - Control Room (16.29 m2)						
No Asbestos						
B00E - M0006 - Movement (4.33 m2)						
No Asbestos						
B00E - M0008 - Change (15.85 m2)						
No Asbestos						
B00E - M0009 - Shower (1.72 m2)						
No Asbestos						
B00E - M0010 - Toilets-Boys (1.78 m2)						
No Asbestos						
B00E - M0011 - Stairs (2.03 m2)						
No Asbestos						
B00E - M0012 - Stairs (1.98 m2)						
No Asbestos						
B00E - R0003 - Staff - Toilet (1.78 m2)						
No Asbestos						
B00E - R0004 - Chair Store (18.99 m2)						
No Asbestos						
B00E - R0005 - Multi-Purpose Space (456.96 m2)						
No Asbestos						
B00E - R0007 - Cleaning Store - Distributed (2.87 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					No Asbestos Detected
	8115/B00E/R0009/Floor Coverings Res/Textile/S1					
B00E - R0008 - Distribution Board Cupboard (0.91 m2)						
					Note: No inspection of live electrical installation.	
Door Lining	Flat AC Sheeting					No Asbestos Detected
	8115/B00E/R0008/Door Lining/S2					
Ceiling Structures/Linings	Flat AC Sheeting					No Asbestos Detected
	8115/B00E/R0008/Door Lining/S2					
Electrical Mounting Board	Resinous Board	2m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/B00E/R0008/Electrical Mounting Board/S13					Chrysotile (white asbestos)
B00E - R0010 - Staff Kitchen (17.58 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00E/R0009/Floor Coverings Res/Textile/S1					No Asbestos Detected	
B00E - R0013 - Chair Store (21.22 m2)						
No Asbestos						
B00E - R0015 - External Movement (16.52 m2)						
No Asbestos						
B00E - R0020 - External Movement (3.54 m2)						
No Asbestos						
B00E - R0021 - External Movement (3.6 m2)						
No Asbestos						
B00E - R0022 - General Storeroom (9.62 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00E/R0009/Floor Coverings Res/Textile/S1					No Asbestos Detected	
B00E - R0023 - Chair Store (3.06 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00E/R0009/Floor Coverings Res/Textile/S1					No Asbestos Detected	
B00E - R0024 - Toilet - Lobby (11.91 m2)						
No Asbestos						
B00E - R0025 - Toilets-Girls (14.19 m2)						
Incinerator	Millboard	1Unit	In wall	Friable Asbestos (5)	Low (1)	Low Priority (2-3)
Assumed Asbestos - Electrical Hazard						
Incinerator Flue	Fibre Cement Pipe	5m	In wall	Minimal Damage (2)	Low (1)	Low Priority (2-3)
Assumed Asbestos - Area inaccessible						
B00E - R0026 - Toilet - Lobby (11.72 m2)						
No Asbestos						
B00E - R0027 - Toilets-Boys (14.54 m2)						
No Asbestos						
B00E - R0028 - Movement (74.99 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00E/R0009/Floor Coverings Res/Textile/S1					No Asbestos Detected	
B00E - R0029 - Public Reception (1.31 m2)						
Floor Coverings Res/Textile	Vinyl Tiles					
8115/B00E/R0009/Floor Coverings Res/Textile/S1					No Asbestos Detected	
B00E - R0030 - Movement (3.18 m2)						
No Asbestos						
B00E - R0031 - Stairs (4.1 m2)						
No Asbestos						
B00E - R0032 - Movement (3.13 m2)						
No Asbestos						
B00E - R0033 - Stairs (4.12 m2)						
No Asbestos						
B00E - R0034 - External Movement (2.32 m2)						
No Asbestos						
B00E - R0035 - Stage (114.06 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00E - R0036 - Music Store (2.87 m2)						
No Asbestos						
B00E - R0037 - External Movement (3.56 m2)						
No Asbestos						
B00E - R0038 - External Movement (3.52 m2)						
No Asbestos						
B00E - R9002 - Performance Store (5.7 m2)						
No Asbestos						
B00E - R9003 - Movement (1.05 m2)						
No Asbestos						
B00E - R9004 - External Movement (2.08 m2)						
No Asbestos						
B00E - R9005 - Music Store (4.61 m2)						
No Asbestos						
B00E - R9006 - Stairs (1.94 m2)						
No Asbestos						
B00E - R9007 - Practice/Seminar (62.84 m2)						
No Asbestos						
B00E - R9008 - Performance Store (8.87 m2)						
No Asbestos						
B00E - R9009 - Music Store (25.97 m2)						
No Asbestos						
B00E - R9010 - Movement (3.42 m2)						
No Asbestos						
B00E - R9011 - Stairs (2.67 m2)						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Build+1 - Farm Cottage

Exterior

Wall Cladding	Flat AC Sheeting	200m2	Throughout	Some Damage - Unsealed (3)	Medium (2)	Medium Priority (4-5)
	8115/Build+1/Wall Cladding/S42					Chrysotile (white asbestos)
Eaves Linings	Flat AC Sheeting	50m2	Perimeter	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/Build+1/Wall Cladding/S42					Chrysotile (white asbestos)
Roof	Corrugated AC Sheeting	2m2	South	Some Damage - Unsealed (3)	Low (1)	Low Priority (2-3)
	8115/Build+1/Roof/S43			Chrysotile (white asbestos) , Amosite (brown asbestos)		
Debris to ground surface	AC Fragments/Debris	0.5m2	Throughout	Poor Condition - Extensive Damage (4)	Low (1)	Medium Priority (4-5)
	8115/Build+1/Debris to ground surface/S44					Chrysotile (white asbestos)
Electrical Backing Board	Resinous Board	1Unit	South	Minimal Damage (2)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					
Underfloor Voids	AC Fragments/Debris	0.5m2	Throughout	Poor Condition - Extensive Damage (4)	Low (1)	Medium Priority (4-5)
	8115/Build+1/Debris to ground surface/S44					Chrysotile (white asbestos)
Ceiling Voids	Non Accessible Area - Height Restriction Area inaccessible					

Interior

Build+1 - R0001 - General L.S.

No Asbestos

Build+1 - R0002 - Kitchen

Wall Linings Internal	Flat AC Sheeting	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/Build+1/Wall Cladding/S42					Chrysotile (white asbestos)

Build+1 - R0003 - Kitchen Store Room

Wall Linings Internal	Flat AC Sheeting	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/Build+1/Wall Cladding/S42					Chrysotile (white asbestos)

Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Medium (2)	Low Priority (2-3)
	8115/Build+1/Wall Cladding/S42					Chrysotile (white asbestos)

Build+1 - R0004 - Bathroom

Wall Linings Internal	Flat AC Sheeting	10m2	Throughout	Minimal Damage (2)	Low (1)	Low Priority (2-3)
	8115/Build+1/Wall Cladding/S42					Chrysotile (white asbestos)

Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8115/Build+1/Wall Cladding/S42					Chrysotile (white asbestos)

Build+1 - R0005 - General Store Room

No Asbestos

Build+1 - R0006 - Movement (hall)

No Asbestos

Build+1 - R0007 - Toilet

Ceiling Structures/Linings	Flat AC Sheeting	2m2	Throughout	Minimal Damage (2)	Low (1)	Low Priority (2-3)
	8115/Build+1/Wall Cladding/S42					Chrysotile (white asbestos)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Wall Linings Internal	Flat AC Sheeting	5m2	Throughout	Minimal Damage (2)	Low (1)	Low Priority (2-3)
8115/Build+1/Wall Cladding/S42					Chrysotile (white asbestos)	
Build+1 - R0008 - Movement (verandah)						
Ceiling Structures/Linings	Flat AC Sheeting	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8115/Build+1/Wall Cladding/S42					Chrysotile (white asbestos)	
Build+1 - R0009 - Carport						
Ceiling Structures/Linings	Flat AC Sheeting	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8115/Build+1/Wall Cladding/S42					Chrysotile (white asbestos)	

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Demountables

Demountable details as per the AMS records as of 15 Feb 2017.

NS 210 - D10784 - Home Science/Preparation Area/Laundry : Placement Date - 11/03/2002

Exterior

No Asbestos Found.

Interior

R1 - Food Technology L.S.

No Asbestos Found.

R2 - Laundry

No Asbestos Found.

R3 - Preparation-Materials

No Asbestos Found.

R4 - Entry

No Asbestos Found.

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Listing of Electronic Attachments as of 22/03/2017

Available Asbestos Related Electronic Files

8115_ASB_231112_AMP.pdf

* Note : Refer to AMS for details of the attachment(s).

2017
