


Asbestos Register

(Hazardous Materials and Risk Assessment)

School : Liverpool Girls High School (8176)
Region : South Western Sydney
State Electorate : Liverpool
Local Government Area : Liverpool

Initial Survey : Noel Arnold & Associates : 31 - Mar - 2008
Reviewed By : Greencap-NAA : 26 - Aug - 2014

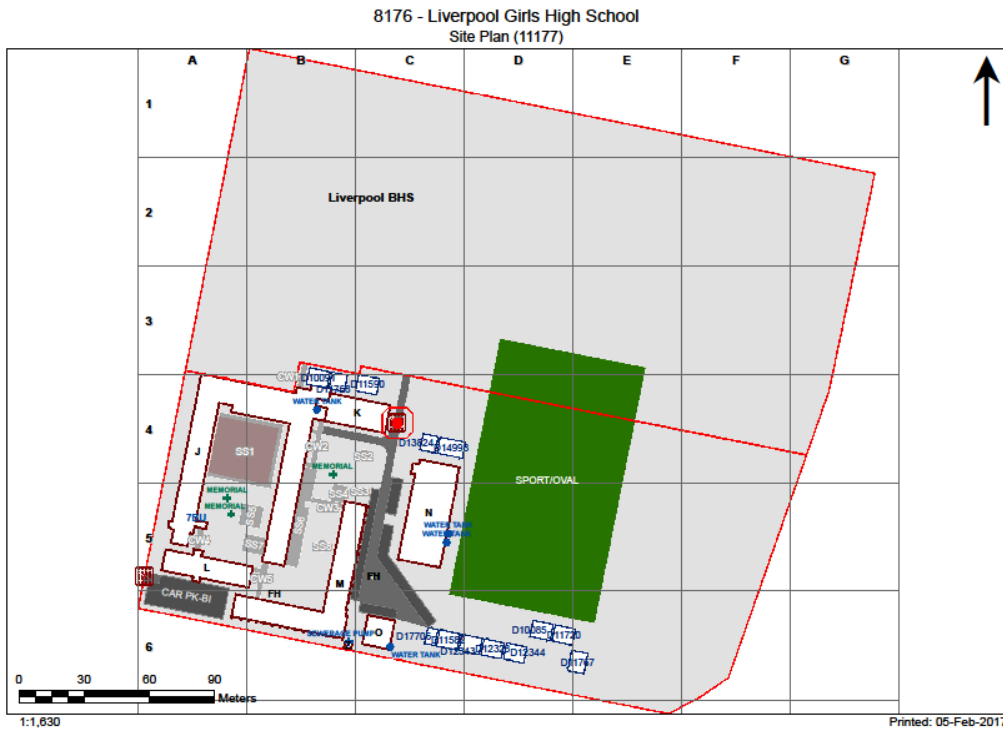

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00J - Various - 1955 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids	No Asbestos Found					
Ceiling Voids	No Asbestos Found					
Ceiling Voids	Non Accessible Area - Height Restriction					

Interior

B00J - R0001 - Laundry (12.57 m2)

Floor Coverings Res/Textile	Vinyl Tiles					No Asbestos Detected
8176/B00J/R0001/Floor Coverings Res/Textile/S3						
Ceiling Structures/Linings	Flat AC Sheeting	13m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00J/R0001/Ceiling Structures/Linings/S4						Chrysotile (white asbestos) , Amosite (brown asbestos)

B00J - R0002 - Materials Learning Space - Type 1 (72.57 m2)

No Asbestos

B00J - R0009 - General Storeroom (17.46 m2)

No Asbestos

B00J - R0010 - Computer Learning Space (49.76 m2)

No Asbestos

B00J - R0011 - General Learning Space (49.83 m2)

No Asbestos

B00J - R0012 - General Learning Space (49.83 m2)

No Asbestos

B00J - R0013 - General Learning Space (49.83 m2)

No Asbestos

B00J - R0014 - General Learning Space (50.01 m2)

No Asbestos

B00J - R0015 - General Learning Space (50.21 m2)

No Asbestos

B00J - R0016 - General Storeroom (6.7 m2)

No Asbestos

B00J - R0017 - Staff - Toilet (5.33 m2)

No Asbestos

B00J - R0019 - Cleaning Store - Distributed (3.66 m2)

No Asbestos

B00J - R0021 - General Assistants (25.2 m2)

No Asbestos

B00J - R0023 - Archive Store (21.31 m2)

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	21.31m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00J/R0023/Floor Coverings Res/Textile/S14						Chrysotile (white asbestos)

B00J - R0027 - Kiln Space (24.46 m2)

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	24.46m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00J/R0023/Floor Coverings Res/Textile/S14						Chrysotile (white asbestos)

B00J - R0028 - Resources Store (15.77 m2)

No Asbestos

B00J - R0029 - External Movement (85.17 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
No Asbestos						
B00J - R0033 - Student Canteen (60.07 m2)						
No Asbestos						
B00J - R0034 - Pantry (15.39 m2)						
No Asbestos						
B00J - R0035 - Staff - Toilet (5.12 m2)						
No Asbestos						
B00J - R0038 - Garden Store Room (10.8 m2)						
No Asbestos						
B00J - R0039 - General Storeroom (10 m2)						
No Asbestos						
B00J - R0040 - General Storeroom (1.9 m2)						
No Asbestos						
B00J - R0041 - General Storeroom (3.56 m2)						
No Asbestos						
B00J - R0042 - Movement (29.33 m2)						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet) 8176/B00J/R0023/Floor Coverings Res/Textile/S14	0.5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B00J - R0044 - Movement (121.89 m2)						
No Asbestos						
B00J - R0045 - Archive Store (25.26 m2)						
No Asbestos						
B00J - R0046 - Plant (7.99 m2)						
No Asbestos						
B00J - R0048 - External Movement (17.87 m2)						
No Asbestos						
B00J - R0049 - Resources Store (7.64 m2)						
No Asbestos						
B00J - R0050 - Wood Technology L.S. (58.27 m2)						
Floor Coverings Res/Textile	Vinyl Sheet 8176/B00J/R0050/Floor Coverings Res/Textile/S17					No Asbestos Detected
B00J - R0051 - Wood Technology Bay (43.28 m2)						
No Asbestos						
B00J - R0052 - General Storeroom (1.85 m2)						
No Asbestos						
B00J - R0053 - Stairs (6.29 m2)						
No Asbestos						
B00J - R0054 - Stairs (7.86 m2)						
No Asbestos						
B00J - R0055 - Movement (76.79 m2)						
No Asbestos						
B00J - R0056 - Student Lounge (18.92 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00J/R0001/Ceiling Structures/Linings/S4	18.92m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos) , Amosite (brown asbestos)
B00J - R0057 - Fitness Laboratory (116.45 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet) 8176/B00J/R0023/Floor Coverings Res/Textile/S14	116.45m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B00J - R0058 - Sport Equipment Store (32.37 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00J/R0059/Ceiling Structures/Linings/S15					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet) 8176/B00J/R0058/Floor Coverings Res/Textile/S16					No Asbestos Detected
B00J - R0059 - Student Lounge (60.56 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00J/R0059/Ceiling Structures/Linings/S15					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
B00J - R0060 - External Movement (1.87 m2)						
No Asbestos						
B00J - R0061 - Stairs (5.97 m2)						
No Asbestos						
B00J - R0062 - General Storeroom (25.45 m2)						
No Asbestos						
B00J - R0063 - External Stairs (19.71 m2)						
No Asbestos						
B00J - R0064 - External Movement (4.48 m2)						
No Asbestos						
B00J - R0065 - External Movement (18.93 m2)						
No Asbestos						
B00J - R0066 - General Storeroom (4.17 m2)						
No Asbestos						
B00J - R0067 - Stairs (3.77 m2)						
No Asbestos						
B00J - R0068 - Handwashing Facilities (0.78 m2)						
No Asbestos						
B00J - R0069 - Staff Study (23.46 m2)						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet) 8176/B00J/R0023/Floor Coverings Res/Textile/S14	23.46m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B00J - R0070 - Tea Room (2.65 m2)						
Floor Coverings Res/Textile	Vinyl Sheet Assumed Asbestos - Bone coloured vinyl sheet	3m2	North	Good Condition (1)	Low (1)	Low Priority (2-3)
B00J - R0071 - Distribution Board Cupboard (0.32 m2)						
					Note: No inspection of live electrical installation.	
No Asbestos						
B00J - R0072 - Movement (158.03 m2)						
No Asbestos						
B00J - R0073 - Movement (21.28 m2)						
No Asbestos						
B00J - R0074 - Stairs (3.26 m2)						
No Asbestos						
B00J - R0075 - External Movement (4.17 m2)						
No Asbestos						
B00J - R0076 - Movement (29.73 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
No Asbestos						
B00J - R1002 - Principal Office (21.32 m2)						
No Asbestos						
B00J - R1003 - Administration - Clerical (12.8 m2)						
No Asbestos						
B00J - R1004 - Deputy Principal Office (13.74 m2)						
No Asbestos						
B00J - R1005 - Ancillary Staff (9.78 m2)						
No Asbestos						
B00J - R1006 - Communications Cupboard (3.13 m2)						
No Asbestos						
B00J - R1007 - Deputy Principal Office (18.4 m2)						
No Asbestos						
B00J - R1008 - Computer Learning Space (42.34 m2)						
No Asbestos						
B00J - R1009 - Office/Store (14.86 m2)						
No Asbestos						
B00J - R1011 - Leading Teacher (17.63 m2)						
No Asbestos						
B00J - R1012 - System Administrators Office (17.84 m2)						
Panel to window	Flat AC Sheeting					
	8176/B00J/R1012/Panel to window/S2					No Asbestos Detected
B00J - R1013 - Seminar (106.98 m2)						
No Asbestos						
B00J - R1014 - Movement (219.43 m2)						
No Asbestos						
B00J - R1015 - Staff Study (20.22 m2)						
No Asbestos						
B00J - R1016 - Distribution Board Cupboard (0.8 m2)						
					Note: No inspection of live electrical installation.	
No Asbestos						
B00J - R1017 - Staff - Toilet (21.05 m2)						
No Asbestos						
B00J - R1018 - Interview/Meeting (21.01 m2)						
No Asbestos						
B00J - R1019 - Staff Study (36.69 m2)						
No Asbestos						
B00J - R1020 - Printing/Photocopying (37 m2)						
No Asbestos						
B00J - R1022 - Preparation - Materials (12.05 m2)						
No Asbestos						
B00J - R1023 - Resources Store (2.74 m2)						
No Asbestos						
B00J - R1024 - Pantry (2.76 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
	8176/B00J/R2024/Floor Coverings Res/Textile/S1					No Asbestos Detected
B00J - R1025 - Food Technology L.S. (71.12 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Floor Coverings Res/Textile Vinyl Sheet
 8176/B00J/R2024/Floor Coverings Res/Textile/S1 **No Asbestos Detected**

B00J - R1026 - Food Technology L.S. (73.16 m2)

No Asbestos

B00J - R1027 - Resources Store (18.79 m2)

Floor Coverings Res/Textile Vinyl Sheet
 8176/B00J/R2024/Floor Coverings Res/Textile/S1 **No Asbestos Detected**

B00J - R1029 - Uniform Shop (17.53 m2)

No Asbestos

B00J - R1030 - General Learning Space (52.54 m2)

No Asbestos

B00J - R1031 - General Learning Space (52.15 m2)

No Asbestos

B00J - R1032 - General Learning Space (52.3 m2)

No Asbestos

B00J - R1033 - General Learning Space (52.08 m2)

No Asbestos

B00J - R1034 - General Learning Space (52.67 m2)

No Asbestos

B00J - R1035 - General Learning Space (52.57 m2)

No Asbestos

B00J - R1036 - Resources Store (5.66 m2)

No Asbestos

B00J - R1037 - Resources Store (10.03 m2)

No Asbestos

B00J - R1038 - Staff - Toilet (5.35 m2)

No Asbestos

B00J - R1039 - Administration - Clerical (26.75 m2)

No Asbestos

B00J - R1040 - Cleaning Store - Distributed (3.84 m2)

No Asbestos

B00J - R1043 - External Movement (42.71 m2)

No Asbestos

B00J - R1044 - Movement (5.41 m2)

No Asbestos

B00J - R1045 - Student Waiting (83.2 m2)

No Asbestos

B00J - R1046 - Administration - Clerical (5.34 m2)

No Asbestos

B00J - R1047 - Administration - Clerical (7.84 m2)

No Asbestos

B00J - R1048 - Handwashing Facilities (0.8 m2)

No Asbestos

B00J - R1049 - Clinic - Girls (18.92 m2)

No Asbestos

B00J - R1050 - Movement (9.17 m2)

No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00J - R1051 - Food Technology L.S. (71.32 m2)						
No Asbestos						
B00J - R1052 - Stairs (7.86 m2)						
No Asbestos						
B00J - R1053 - Stairs (11.29 m2)						
No Asbestos						
B00J - R1054 - Handwashing Facilities (0.71 m2)						
No Asbestos						
B00J - R1055 - Stairs (11.18 m2)						
No Asbestos						
B00J - R1056 - Movement (0.48 m2)						
No Asbestos						
B00J - R1057 - Stairs (8.17 m2)						
No Asbestos						
B00J - R1058 - Handwashing Facilities (0.71 m2)						
No Asbestos						
B00J - R1059 - Stairs (11.51 m2)						
No Asbestos						
B00J - R1060 - Movement (144.4 m2)						
No Asbestos						
B00J - R1061 - Movement (21.07 m2)						
No Asbestos						
B00J - R1062 - External Movement (10.89 m2)						
No Asbestos						
B00J - R2002 - Resources Store (9.7 m2)						
No Asbestos						
B00J - R2003 - Resources Store (8.54 m2)						
No Asbestos						
B00J - R2004 - Textiles Technology L.S. (72.42 m2)						
No Asbestos						
B00J - R2005 - Office/Store (9.68 m2)						
No Asbestos						
B00J - R2006 - Resources Store (9.64 m2)						
No Asbestos						
B00J - R2007 - Computer Learning Space (54.83 m2)						
No Asbestos						
B00J - R2008 - Resources Store (21.58 m2)						
No Asbestos						
B00J - R2009 - Staff - Toilet (21.54 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	21.54m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00J/R2009/Ceiling Structures/Linings/S18				Chrysotile (white asbestos) , Amosite (brown asbestos)		
B00J - R2021 - Staff Study (31.75 m2)						
No Asbestos						
B00J - R2022 - Preparation - Science (35.3 m2)						
No Asbestos						
B00J - R2023 - Preparation - Science (33.35 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00J - R2024 - Study Space (11.62 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
8176/B00J/R2024/Floor Coverings Res/Textile/S1					No Asbestos Detected	
B00J - R2025 - Study Space (13.51 m2)						
No Asbestos						
B00J - R2026 - Movement (3.73 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
8176/B00J/R2024/Floor Coverings Res/Textile/S1					No Asbestos Detected	
B00J - R2028 - Movement (4.8 m2)						
No Asbestos						
B00J - R2029 - Staff Study (40.33 m2)						
No Asbestos						
B00J - R2030 - Independent Learning Space (14.08 m2)						
No Asbestos						
B00J - R2031 - Staff Kitchen (12.45 m2)						
Sink	Sink pad					
8176/B00J/R2031/Sink/S19					No Asbestos Detected	
B00J - R2032 - Handwashing Facilities (0.75 m2)						
No Asbestos						
B00J - R2033 - Stairs (11.04 m2)						
No Asbestos						
B00J - R2034 - Stairs (11.19 m2)						
No Asbestos						
B00J - R2035 - Handwashing Facilities (0.75 m2)						
No Asbestos						
B00J - R2036 - Movement (199.2 m2)						
No Asbestos						
B00J - R2037 - Laboratory L.S. (104.84 m2)						
No Asbestos						
B00J - R2038 - Laboratory L.S. (100.85 m2)						
No Asbestos						
B00J - R2039 - Commonroom (63.9 m2)						
No Asbestos						
B00J - R2040 - Tea Room (2.42 m2)						
No Asbestos						
B00J - R2041 - Movement (10.65 m2)						
No Asbestos						
B00J - R2042 - Stairs (6.96 m2)						
No Asbestos						



Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00K - Physical Education - 1955 - Brick/Block (Brick/Block)

Exterior

Gable verge linings	Flat AC Sheeting	30m	East facing, West facing	Good Condition (1)	Low (1)	Low Priority (2-3)
Assumed Asbestos - Height Restriction						
Ceiling Voids	Non Accessible Area - Area inaccessible					
Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible					

Interior

B00K - R0002 - Cleaning Store - Distributed (2.52 m2)

No Asbestos

B00K - R0003 - Cleaning Supplies Store (4.51 m2)

No Asbestos

B00K - R0004 - Change (60.36 m2)

No Asbestos

B00K - R0005 - Sport Equipment Store (17.52 m2)

No Asbestos

B00K - R0006 - Movement (25.32 m2)

No Asbestos

B00K - R0007 - General Storeroom (5.22 m2)

No Asbestos

B00K - R0008 - Change (56.67 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	20m2	North facing, South facing	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00K/R0008/Partition Walls (Cubicles)/S10					Chrysotile (white asbestos)	

B00K - R0009 - External Movement (21.35 m2)

No Asbestos

B00K - R0010 - Chair Store (4.16 m2)

No Asbestos

B00K - R0011 - General Storeroom (8.71 m2)

No Asbestos

B00K - R0012 - Handwashing Facilities (11.57 m2)

No Asbestos

B00K - R0014 - Cleaning Supplies Store (16.18 m2)

No Asbestos

B00K - R0015 - Toilets-Girls (71.1 m2)

No Asbestos

B00K - R0016 - Stairs (2.73 m2)

No Asbestos

B00K - R0017 - Plant (13.93 m2)

Stored Item	Flat AC Sheeting	8176/B00K/R0017/Stored Item/S25				No Asbestos Detected	
-------------	------------------	---------------------------------	--	--	--	-----------------------------	--

B00K - R1001 - Multi-Purpose Space (285.89 m2)

No Asbestos

B00K - R1002 - General Storeroom (14.5 m2)

No Asbestos

B00K - R1003 - General Storeroom (7.51 m2)

No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00K - R1004 - Toilets-Unisex (4.88 m2)						
No Asbestos						
B00K - R1005 - Sport Equipment Store (9.45 m2)						
No Asbestos						
B00K - R1007 - Stairs (9.92 m2)						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00L - General Learning/Art - 1955 - Brick/Block (Brick/Block)

Exterior

Eaves Linings	Non Accessible Area - Height Restriction					
Underfloor Voids	No Asbestos Found					
Ceiling Voids	Non Accessible Area - Height Restriction					

Interior

B00L - R0001 - Staff - Toilet (5.45 m2)

No Asbestos

B00L - R0002 - Staff Study (5.79 m2)

Ceiling Structures/Linings	Vermiculite	5.79m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	

B00L - R0004 - General Learning Space (53.29 m2)

Ceiling Structures/Linings	Vermiculite	53.29m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	

B00L - R0005 - Resources Store (6.15 m2)

No Asbestos

B00L - R0006 - Resources Store (5.97 m2)

No Asbestos

B00L - R0007 - General Learning Space (40 m2)

Ceiling Structures/Linings	Vermiculite	40m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	

B00L - R0008 - General Learning Space (53.22 m2)

Ceiling Structures/Linings	Vermiculite	53.22m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	

B00L - R0009 - Student Waiting (6.14 m2)

Floor Coverings Res/Textile	Vinyl Sheet					No Asbestos Detected
8176/B00L/R0009/Floor Coverings Res/Textile/S6						
Ceiling Structures/Linings	Vermiculite	6.14m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	

B00L - R0010 - Interview/Office - Type 1 (11.06 m2)

Ceiling Structures/Linings	Vermiculite	11.06m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	

B00L - R0011 - General Storeroom (8.2 m2)

Floor Coverings Res/Textile	Vinyl Sheet					No Asbestos Detected
8176/B00L/R0009/Floor Coverings Res/Textile/S6						
Ceiling Structures/Linings	Vermiculite	8.2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	

B00L - R0012 - General Learning Space (39.49 m2)

Ceiling Structures/Linings	Vermiculite	39.49m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	

B00L - R0013 - Staff Study (40.08 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite	40.08m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	
B00L - R0014 - Distribution Board Cupboard (0.1 m2)						
Note: No inspection of live electrical installation.						
No Asbestos						
B00L - R0016 - Cleaning Store - Distributed (2.75 m2)						
No Asbestos						
B00L - R0017 - Stairs (2.59 m2)						
No Asbestos						
B00L - R0018 - Movement (78.83 m2)						
Ceiling Structures/Linings	Vermiculite	78.83m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	
B00L - R0019 - External Movement (10.66 m2)						
No Asbestos						
B00L - R0020 - External Movement (6.07 m2)						
No Asbestos						
B00L - R1001 - Cleaning Store - Distributed (4.41 m2)						
No Asbestos						
B00L - R1004 - Staff Study (32.92 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	34m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R1004/Floor Coverings Res/Textile/S7					Chrysotile (white asbestos)	
B00L - R1006 - Art Learning Space (53.73 m2)						
No Asbestos						
B00L - R1007 - Art Learning Space (53.51 m2)						
No Asbestos						
B00L - R1008 - General Learning Space (53.14 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
8176/B00L/R1010/Floor Coverings Res/Textile/S21					No Asbestos Detected	
B00L - R1010 - General Learning Space (51.9 m2)						
Floor Coverings Res/Textile	Vinyl Sheet					
8176/B00L/R1010/Floor Coverings Res/Textile/S21					No Asbestos Detected	
B00L - R1011 - General Storeroom (1.16 m2)						
No Asbestos						
B00L - R1012 - Art Learning Space (14.4 m2)						
No Asbestos						
B00L - R1013 - Resources Store (10.82 m2)						
No Asbestos						
B00L - R1014 - Resources Store (6.85 m2)						
Ceiling Structures/Linings	Vermiculite	6.85m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	
B00L - R1015 - Office/Store (7.99 m2)						
Ceiling Structures/Linings	Vermiculite	7.99m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	
B00L - R1016 - Movement (59.12 m2)						
Ceiling Structures/Linings	Vermiculite	59.12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00L - R1017 - Stairs (11.01 m2)						
Ceiling Structures/Linings	Vermiculite	11.01m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00L/R0018/Ceiling Structures/Linings/S20					Chrysotile (white asbestos)	

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00M - Various - 1955 - Brick/Block (Brick/Block)

Exterior

No Asbestos

Interior

B00M - R0001 - Garden Store Room (5.65 m2)

No Asbestos

B00M - R0002 - Distribution Board Cupboard (0.65 m2)

Note: No inspection of live electrical installation.

Electrical Backing Board	Resinous Board	1m2	North	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00M/R0002/Electrical Backing Board/S24					Chrysotile (white asbestos)	

B00M - R0003 - Laboratory L.S. (92.89 m2)

Fume Cupboard	Flat AC Sheeting	2Unit	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00M/R0004/Fume Cupboard/S9					Chrysotile (white asbestos)	

Ceiling Structures/Linings	Vermiculite	8176/B00M/R0028/Ceiling Structures/Linings/S22			Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

B00M - R0006 - Laboratory L.S. (93.22 m2)

Ceiling Structures/Linings	Vermiculite	8176/B00M/R0028/Ceiling Structures/Linings/S22			Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

B00M - R0007 - Resources Store (25.88 m2)

Floor Coverings Res/Textile	Vinyl Tiles	27m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00M/R0020/Floor Coverings Res/Textile/S8					Chrysotile (white asbestos)	

Ceiling Structures/Linings	Vermiculite	8176/B00M/R0028/Ceiling Structures/Linings/S22			Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

B00M - R0008 - Staff Study (39.29 m2)

Floor Coverings Res/Textile	Vinyl Tiles	41m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00M/R0020/Floor Coverings Res/Textile/S8					Chrysotile (white asbestos)	

Ceiling Structures/Linings	Vermiculite	8176/B00M/R0028/Ceiling Structures/Linings/S22			Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						

B00M - R0009 - Distribution Board Cupboard (0.61 m2)

Note: No inspection of live electrical installation.

No Asbestos

B00M - R0010 - Staff - Toilet (5.64 m2)

Floor Coverings Res/Textile	Vinyl Tiles	6m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00M/R0020/Floor Coverings Res/Textile/S8					Chrysotile (white asbestos)	

B00M - R0011 - External Movement (211.04 m2)

No Asbestos

B00M - R0012 - Resources Store (8.13 m2)

No Asbestos

B00M - R0013 - Toilets-Girls (45.46 m2)

No Asbestos

B00M - R0014 - Laboratory L.S. (92.96 m2)

Floor Coverings Res/Textile	Vinyl Tiles	92m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00M/R0020/Floor Coverings Res/Textile/S8					Chrysotile (white asbestos)	

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Wall Linings Internal	Flat AC Sheeting 8176/B00M/R0016/Wall Linings Internal/S23					No Asbestos Detected
B00M - R0015 - Preparation - Science (29.21 m2)						
Floor Coverings Res/Textile	Vinyl Tiles 8176/B00M/R0020/Floor Coverings Res/Textile/S8	30m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3) <i>Chrysotile (white asbestos)</i>
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R0016 - Chemical Store (9.61 m2)						
Floor Coverings Res/Textile	Vinyl Tiles 8176/B00M/R0020/Floor Coverings Res/Textile/S8	11m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3) <i>Chrysotile (white asbestos)</i>
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Wall Linings Internal	Flat AC Sheeting 8176/B00M/R0016/Wall Linings Internal/S23					No Asbestos Detected
B00M - R0022 - Resources Store (11.05 m2)						
Floor Coverings Res/Textile	Vinyl Tiles 8176/B00M/R0020/Floor Coverings Res/Textile/S8	12m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3) <i>Chrysotile (white asbestos)</i>
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R0023 - Distribution Board Cupboard (0.71 m2)						
					Note: No inspection of live electrical installation.	
No Asbestos						
B00M - R0024 - Cleaning Store - Distributed (5.61 m2)						
No Asbestos						
B00M - R0025 - Cleaning Store - Distributed (6.34 m2)						
No Asbestos						
B00M - R0026 - Preparation - Science (39.62 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R0027 - Laboratory L.S. (65.95 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R0028 - Art Learning Space (59.8 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R0029 - Darkroom Space (0.64 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R0030 - Dark Room (19.69 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00M - R0031 - Movement (11.78 m2)						
No Asbestos						
B00M - R0032 - Stairs (9.8 m2)						
No Asbestos						
B00M - R0033 - Movement (11.56 m2)						
No Asbestos						
B00M - R0034 - Stairs (10.05 m2)						
No Asbestos						
B00M - R0035 - External Movement (8.14 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	8.14m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00M/R0020/Floor Coverings Res/Textile/S8					Chrysotile (white asbestos)	
B00M - R0036 - Movement (11.45 m2)						
No Asbestos						
B00M - R0037 - Stairs (10.11 m2)						
No Asbestos						
B00M - R1001 - Distribution Board Cupboard (0.69 m2)						
No Asbestos						
						Note: No inspection of live electrical installation.
B00M - R1002 - Music Store (6.19 m2)						
Ceiling Structures/Linings	Vermiculite					
8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00M - R1003 - Music Store (6.19 m2)						
Ceiling Structures/Linings	Vermiculite					
8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00M - R1004 - Music Learning Space (52.63 m2)						
Ceiling Structures/Linings	Vermiculite					
8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00M - R1007 - Performance Workshop (52.42 m2)						
Ceiling Structures/Linings	Vermiculite					
8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00M - R1009 - Staff - Toilet (3.78 m2)						
No Asbestos						
B00M - R1010 - Staff Lounge (14.5 m2)						
Ceiling Structures/Linings	Vermiculite					
8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00M - R1011 - Resources Store (8.63 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	9m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)
8176/B00M/R0020/Floor Coverings Res/Textile/S8					Chrysotile (white asbestos)	
Ceiling Structures/Linings	Vermiculite					
8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00M - R1012 - Staff Study (16.85 m2)						
Ceiling Structures/Linings	Vermiculite					
8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken	
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00M - R1013 - Office/Store (8.61 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R1014 - Distribution Board Cupboard (0.68 m2)					Note: No inspection of live electrical installation.	
No Asbestos						
B00M - R1015 - Staff Study (26.86 m2)						
Floor Coverings Res/Textile	Vinyl Tiles 8176/B00M/R0020/Floor Coverings Res/Textile/S8	28m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R1017 - Staff - Toilet (2.09 m2)						
No Asbestos						
B00M - R1018 - Office/Store (26.02 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R1019 - Computer Learning Space (65.92 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R1020 - Staff Study (26.06 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R1021 - General Learning Space (52.49 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R1022 - Resources Store (6.55 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R1023 - Resources Store (19.1 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R1024 - General Learning Space (66.17 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R1025 - Resources Store (7.93 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
B00M - R1026 - Resources Store (8.33 m2)						
Floor Coverings Res/Textile	Vinyl Tiles 8176/B00M/R0020/Floor Coverings Res/Textile/S8	10m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B00M - R1027 - Music Learning Space (52.56 m2)						
Ceiling Structures/Linings	Vermiculite 8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00M - R1028 - Music Store (7.91 m2)						
Ceiling Structures/Linings	Vermiculite					
	8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00M - R1029 - External Movement (243.99 m2)						
Thermacon Heater	Encapsulated Insulation material within unit	1Unit	South West	Good Condition (1)	Low (1)	Low Priority (2-3)
<i>Assumed Asbestos - Area inaccessible</i>						
B00M - R1030 - Distribution Board Cupboard (0.65 m2)					Note: No inspection of live electrical installation.	
No Asbestos						
B00M - R1031 - Resources Store (3.67 m2)						
Ceiling Structures/Linings	Vermiculite					
	8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00M - R1032 - General Storeroom (4.56 m2)						
Ceiling Structures/Linings	Vermiculite					
	8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00M - R1033 - Resources Store (5.58 m2)						
Ceiling Structures/Linings	Vermiculite					
	8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00M - R1034 - Performing Arts Store (6.17 m2)						
Ceiling Structures/Linings	Vermiculite					
	8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00M - R1035 - Movement Studio (106.29 m2)						
Ceiling Structures/Linings	Vermiculite					
	8176/B00M/R0028/Ceiling Structures/Linings/S22					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00M - R1036 - Stairs (17.94 m2)						
No Asbestos						
B00M - R1037 - Stairs (17.91 m2)						
No Asbestos						
B00M - R1038 - Handwashing Facilities (0.46 m2)						
No Asbestos						
B00M - R1039 - Stairs (18.02 m2)						
No Asbestos						
B00M - R1040 - Handwashing Facilities (0.46 m2)						
No Asbestos						



Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00N - Multi Purpose Facilities - 2009 - Brick/Veneer (Brick/Veneer)**Exterior**

Ceiling Voids Non Accessible Area
 - Area inaccessible

Interior**B00N - R0001 - Change (29.04 m2)**

No Asbestos

B00N - R0002 - Change (29.38 m2)

No Asbestos

B00N - R0003 - Access Student Shower/Toilet/Change (7.81 m2)

No Asbestos

B00N - R0004 - Distribution Board Cupboard (1.6 m2)

Note: No inspection of live electrical installation.

No Asbestos

B00N - R0005 - Gymnasium (620.8 m2)

No Asbestos

B00N - R0006 - Chair Store (32.82 m2)

No Asbestos

B00N - R0007 - Staff Study (24.63 m2)

No Asbestos

B00N - R0008 - First Aid (12.73 m2)

No Asbestos

B00N - R0009 - External Movement (62.85 m2)

No Asbestos

B00N - R0010 - External Movement (69.64 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B000 - Language Centre - 2010 - Brick/Veneer (Brick/Veneer)**Exterior**

Ceiling Voids	Non Accessible Area - Area inaccessible
Underfloor Voids	Non Accessible Area - Area inaccessible

Interior**B000 - R0001 - Computer Learning Space (91.89 m2)**

No Asbestos

B000 - R0002 - Seminar - Type 2 (18.76 m2)

No Asbestos

B000 - R0003 - Resources Store (10.08 m2)

No Asbestos

B000 - R0004 - Computer Store (9 m2)

No Asbestos

B000 - R0005 - External Movement (27.44 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00Z - Building Services - 1955 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids	No Asbestos Found
Underfloor Voids	No Asbestos Found

Interior

B00Z - R0001 - Plant (6.13 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Demountables

Demountable details as per the AMS records as of 15 Feb 2017.

OS 601 - D10085 - Learning Unit - Standard/Withdrawal : Placement Date - 28/11/2012

Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.

Exterior

No Asbestos Found.

Interior

R1 - Entry

No Asbestos Found.

R2 - General Learning Space

No Asbestos Found.

R3 - Store

No Asbestos Found.

OS 601 - D10091 - Learning Unit - Standard/Withdrawal : Placement Date - 27/03/1996

Exterior

Eave Lining	Flat AC Sheet	Assumed Asbestos	11.52 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2

Interior

R1 - Entry

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	8 m2

R2 - General Learning Space

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	55 m2

R3 - Store

Ceiling	Flat AC Sheet	Assumed Asbestos	10 m2
---------	---------------	------------------	-------

OS 601 - D11582 - Learning Unit - Standard/Withdrawal : Placement Date - 5/02/1997

Exterior

Eave Lining	Flat AC Sheet	Assumed Asbestos	11.52 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2

Interior

R1 - Entry

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	8 m2

R2 - General Learning Space

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	55 m2

R3 - Store

Ceiling	Flat AC Sheet	Assumed Asbestos	10 m2
---------	---------------	------------------	-------

OS 601 - D11590 - Learning Unit - Standard/Withdrawal : Placement Date - 30/06/1995

Exterior

Eave Lining	Flat AC Sheet	Assumed Asbestos	11.52 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Interior						
R1 - Entry						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				8 m2
R2 - General Learning Space						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				55 m2
R3 - Store						
Ceiling	Flat AC Sheet	Assumed Asbestos				10 m2
OS 601 - D11720 - Learning Unit - Standard/Withdrawal : Placement Date - 28/11/2012						
Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.						
Exterior						
No Asbestos Found.						
Interior						
R1 - Entry						
No Asbestos Found.						
R2 - General Learning Space						
No Asbestos Found.						
R3 - Store						
No Asbestos Found.						
OS 601 - D11767 - Learning Unit - Standard/Withdrawal : Placement Date - 30/06/1995						
Exterior						
Eave Lining	Flat AC Sheet	Assumed Asbestos				11.52 m2
Landing	Compressed AC Sheet	Assumed Asbestos				1.2 m2
Step Treads	Compressed AC Sheet	Assumed Asbestos				1.08 m2
Interior						
R1 - Entry						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				8 m2
R2 - General Learning Space						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				55 m2
R3 - Store						
Ceiling	Flat AC Sheet	Assumed Asbestos				10 m2
OS 600 - D11768 - Learning Unit - Small : Placement Date - 30/06/1995						
Exterior						
Step Treads	Compressed AC Sheet	Assumed Asbestos				1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos				1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos				8.64 m2
Interior						
R1 - General Learning Space						
End wall panel	Flat AC Sheet	Assumed Asbestos				50 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				55 m2
OS 601 - D12328 - Learning Unit - Standard/Withdrawal : Placement Date - 15/01/1999						
Exterior						
Eave Lining	Flat AC Sheet	Assumed Asbestos				11.52 m2
Landing	Compressed AC Sheet	Assumed Asbestos				1.2 m2

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Step Treads	Compressed AC Sheet	Assumed Asbestos				1.08 m2
Interior						
R1 - Entry						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				8 m2
R2 - General Learning Space						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				55 m2
R3 - Store						
Ceiling	Flat AC Sheet	Assumed Asbestos				10 m2
OS 601 - D12343 - Learning Unit - Standard/Withdrawal : Placement Date - 5/01/1999						
Exterior						
Step Treads	Compressed AC Sheet	Assumed Asbestos				1.08 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos				11.52 m2
Landing	Compressed AC Sheet	Assumed Asbestos				1.2 m2
Interior						
R1 - Entry						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				8 m2
R2 - General Learning Space						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				55 m2
R3 - Store						
Ceiling	Flat AC Sheet	Assumed Asbestos				10 m2
OS 601 - D12344 - Learning Unit - Standard/Withdrawal : Placement Date - 17/03/1999						
Exterior						
Step Treads	Compressed AC Sheet	Assumed Asbestos				1.08 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos				11.52 m2
Landing	Compressed AC Sheet	Assumed Asbestos				1.2 m2
Interior						
R1 - Entry						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				8 m2
R2 - General Learning Space						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				55 m2
R3 - Store						
Ceiling	Flat AC Sheet	Assumed Asbestos				10 m2
OS 600 - D13824 - Learning Unit - Small : Placement Date - 28/11/2012						
Exterior						
Eave Lining	Flat AC Sheet	Assumed Asbestos				8.64 m2
Landing	Compressed AC Sheet	Assumed Asbestos				1.2 m2
Step Treads	Compressed AC Sheet	Assumed Asbestos				1.08 m2
Interior						
R1 - General Learning Space						
End wall panel	Flat AC Sheet	Assumed Asbestos				50 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				55 m2

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
OS 701 - D14998 - Art Learning Space/Workshop/Store : Placement Date - 13/01/2011						
Exterior						
No Asbestos Found.						
Interior						
R1 - Entry						
No Asbestos Found.						
R2 - Art Learning Space						
No Asbestos Found.						
R3 - Store						
No Asbestos Found.						
OS 750 - D17706 - Learning Unit - ESL : Placement Date - 12/02/2010						
Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.						
Exterior						
No Asbestos Found.						
Interior						
R1 - Esl						
No Asbestos Found.						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Listing of Electronic Attachments as of 22/03/2017

There are no asbestos related file attachment(s) for this school.

2017
