

Asbestos Register


(Hazardous Materials and Risk Assessment)



School : Wollongong High School of the Performing Arts (8143)
Region : Illawarra and South East
State Electorate : Keira
Local Government Area : Wollongong

Initial Survey : Noel Arnold & Associates : 12 - May - 2008
Reviewed By : AECOM : 18 - Jun - 2015

8143 - Wollongong High School of the Performing Arts
Site Plan (All Sites)

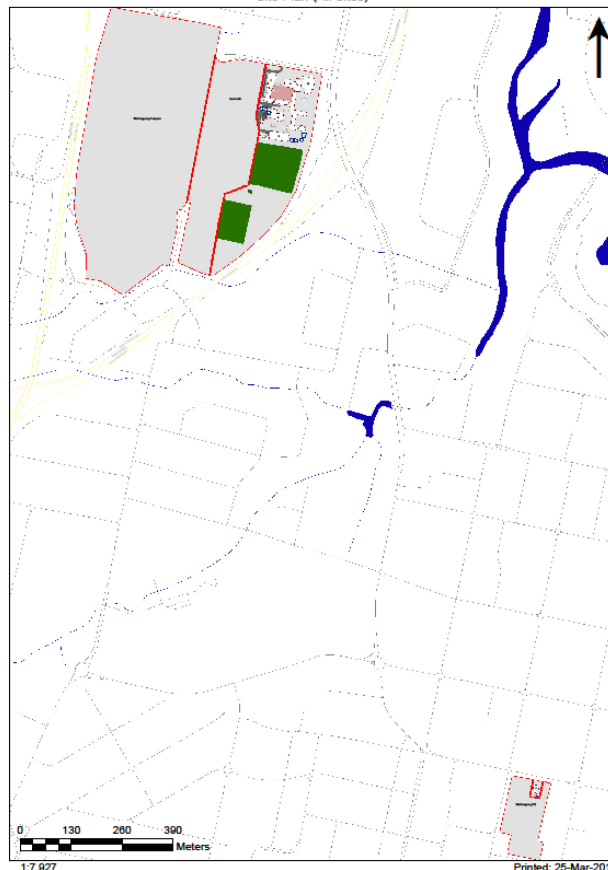

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00A - Physical Education - 1953 - Brick/Block (Brick/Block)**Exterior**

Ceiling Voids - Flat Roof	No Asbestos Found
Underfloor Voids - Slab on Ground	No Asbestos Found

Interior**B00A - R0001 - Gymnasium (288.91 m2)**

No Asbestos

B00A - R0002 - Shower/Change (38.04 m2)

No Asbestos

B00A - R0003 - General Storeroom (5.3 m2)

Non Accessible

B00A - R0006 - Sport Equipment Store (4.94 m2)

Ceiling Structures/Linings	Flat AC Sheeting 8143/B00A/R0006/Ceiling Structures/Linings/S6					No Asbestos Detected
Wall Linings Internal	Flat AC Sheeting 8143/B00A/R0006/Ceiling Structures/Linings/S6					No Asbestos Detected

B00A - R0008 - Toilets-Boys (13.73 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	4m2	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00B/R0023/Partition Walls (Cubicles)/S1					Chrysotile (white asbestos)

B00A - R0009 - Toilets-Girls (14.84 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	4m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00B/R0023/Partition Walls (Cubicles)/S1					Chrysotile (white asbestos)

B00A - R0010 - Shower/Change (30.7 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	14m2	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00B/R0023/Partition Walls (Cubicles)/S1					Chrysotile (white asbestos)

B00A - R0011 - Toilets-Girls (8.52 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	4m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00B/R0023/Partition Walls (Cubicles)/S1					Chrysotile (white asbestos)

B00A - R0012 - Toilets-Boys (5.48 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	4m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00B/R0023/Partition Walls (Cubicles)/S1					Chrysotile (white asbestos)

B00A - R0013 - Staff Study (24.36 m2)

No Asbestos

B00A - R0014 - Sport Equipment Store (13.96 m2)

Ceiling Structures/Linings	Flat AC Sheeting	14m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00B/R1013/Ceiling Structures/Linings/S4					Chrysotile (white asbestos) , Amosite (brown asbestos)

B00A - R0015 - Stairs (1.4 m2)

No Asbestos

B00A - R0016 - Movement (81.26 m2)

No Asbestos

B00A - R1002 - Sport Equipment Store (26.44 m2)

Floor Coverings Res/Textile	Vinyl Tiles 8143/B00A/R1002/Floor Coverings Res/Textile/S7					No Asbestos Detected
-----------------------------	---	--	--	--	--	-----------------------------

B00A - R1003 - Stairs (1.89 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00B - Administration/General Learning - 1953 - Brick/Block (Brick/Block)

Exterior

Eaves Linings	Flat AC Sheeting	200m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
Assumed Asbestos - Height Restriction						
Ceiling Voids	No Asbestos Found					
Underfloor Voids	Non Accessible Area - Area inaccessible - access could not be found.					

Interior

B00B - R0001 - Staff Study (13.17 m2)						
No Asbestos						
B00B - R0002 - Staff Study (10.97 m2)						
No Asbestos						
B00B - R0003 - Principal Office (22.62 m2)						
No Asbestos						
B00B - R0004 - Administration - Clerical (12.74 m2)						
No Asbestos						
B00B - R0005 - Staff - Toilet (2.75 m2)						
No Asbestos						
B00B - R0006 - Clinic-Toilets (2.74 m2)						
No Asbestos						
B00B - R0007 - Clinic-Waiting (14.42 m2)						
No Asbestos						
B00B - R0009 - General Storeroom (2.7 m2)						
No Asbestos						
B00B - R0010 - Ancillary Staff (29.43 m2)						
No Asbestos						
B00B - R0011 - Staff - Toilet (7.25 m2)						
No Asbestos						
B00B - R0012 - Security Store (12.32 m2)						
No Asbestos						
B00B - R0013 - General Storeroom (6.45 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1005/Floor Coverings Res/Textile/S5					Chrysotile (white asbestos)	
B00B - R0014 - Cleaning Store - Distributed (4.84 m2)						
No Asbestos						
B00B - R0015 - Duplicating Workroom (40.15 m2)						
No Asbestos						
B00B - R0016 - Administration - Clerical (36.96 m2)						
No Asbestos						
B00B - R0018 - General Storeroom (0.83 m2)						
No Asbestos						
B00B - R0019 - Multi-Purpose Space (9.38 m2)						
No Asbestos						
B00B - R0020 - Deputy Principal Office (16.6 m2)						
No Asbestos						
B00B - R0021 - Movement (12.61 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00B - R0022 - Toilets-Girls (21.48 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	10m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R0023/Partition Walls (Cubicles)/S1					Chrysotile (white asbestos)	
B00B - R0023 - Toilets-Boys (26.77 m2)						
Partition Walls (Cubicles)	Compressed AC Sheet	6m2	North	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R0023/Partition Walls (Cubicles)/S1					Chrysotile (white asbestos)	
B00B - R0024 - General Learning Space (52.46 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	53m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1005/Floor Coverings Res/Textile/S5					Chrysotile (white asbestos)	
B00B - R0025 - General Learning Space (52.46 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	53m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1005/Floor Coverings Res/Textile/S5					Chrysotile (white asbestos)	
B00B - R0026 - General Learning Space (52.46 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	53m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1005/Floor Coverings Res/Textile/S5					Chrysotile (white asbestos)	
B00B - R0027 - General Learning Space (52.52 m2)						
No Asbestos						
B00B - R0028 - General Storeroom (8.47 m2)						
No Asbestos						
B00B - R0029 - Main Switchroom (3.97 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	4m2	Throughout	Minimal Damage (2)	Low (1)	Low Priority (2-3)
8143/B00B/R0029/Floor Coverings Res/Textile/S2					Chrysotile (white asbestos)	
Wall Linings Internal	Flat AC Sheeting	7m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R0029/Wall Linings Internal/S3					Chrysotile (white asbestos)	
B00B - R0030 - Cleaning Supplies Store (2.94 m2)						
No Asbestos						
B00B - R0031 - General Learning Space (53.06 m2)						
No Asbestos						
B00B - R0032 - General Learning Space (52.8 m2)						
No Asbestos						
B00B - R0033 - General Learning Space (52.8 m2)						
No Asbestos						
B00B - R0034 - General Learning Space (65.37 m2)						
No Asbestos						
B00B - R0035 - General Learning Space (51.85 m2)						
No Asbestos						
B00B - R0036 - Chemical Store (15.78 m2)						
No Asbestos						
B00B - R0037 - Laboratory L.S. (89.81 m2)						
No Asbestos						
B00B - R0038 - Movement (51.88 m2)						
No Asbestos						
B00B - R0039 - Movement (249.13 m2)						
No Asbestos						
B00B - R0040 - General Storeroom (0.83 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
No Asbestos						
B00B - R0041 - Pupil Entry (6.07 m2)						
No Asbestos						
B00B - R0042 - Pupil Entry (2.73 m2)						
No Asbestos						
B00B - R0043 - Pupil Entry (3.15 m2)						
No Asbestos						
B00B - R0044 - Stairs (6.37 m2)						
No Asbestos						
B00B - R0045 - Stairs (7.3 m2)						
No Asbestos						
B00B - R0046 - Movement (89.67 m2)						
No Asbestos						
B00B - R0047 - Movement (42.73 m2)						
No Asbestos						
B00B - R0048 - Toilet - Lobby (3.98 m2)						
No Asbestos						
B00B - R0049 - Toilet - Lobby (2.94 m2)						
No Asbestos						
B00B - R0050 - Staff - Toilet (1.19 m2)						
No Asbestos						
B00B - R1001 - Staff Study (38.72 m2)						
No Asbestos						
B00B - R1002 - Staff - Toilet (7.45 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	8m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1013/Ceiling Structures/Linings/S4				Chrysotile (white asbestos) , Amosite (brown asbestos)		
B00B - R1003 - Staff - Toilet (2.76 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1013/Ceiling Structures/Linings/S4				Chrysotile (white asbestos) , Amosite (brown asbestos)		
B00B - R1004 - Cleaning Store - Distributed (3.8 m2)						
No Asbestos						
B00B - R1005 - General Storeroom (15.72 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	16m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1013/Ceiling Structures/Linings/S4				Chrysotile (white asbestos) , Amosite (brown asbestos)		
Floor Coverings Res/Textile	Vinyl Tiles	16m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1005/Floor Coverings Res/Textile/S5				Chrysotile (white asbestos)		
B00B - R1006 - General Learning Space (52.72 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	53m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1005/Floor Coverings Res/Textile/S5				Chrysotile (white asbestos)		
B00B - R1007 - Computer Learning Space (52.72 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	53m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1005/Floor Coverings Res/Textile/S5				Chrysotile (white asbestos)		
B00B - R1008 - General Assistants (1 m2)						
Non Accessible						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00B - R1009 - General Learning Space (52.72 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	53m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1005/Floor Coverings Res/Textile/S5					Chrysotile (white asbestos)	
B00B - R1010 - General Learning Space (52.72 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	53m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1005/Floor Coverings Res/Textile/S5					Chrysotile (white asbestos)	
B00B - R1011 - General Learning Space (52.71 m2)						
No Asbestos						
B00B - R1012 - General Learning Space (52.71 m2)						
No Asbestos						
B00B - R1013 - General Storeroom (15.89 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	16m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1013/Ceiling Structures/Linings/S4					Chrysotile (white asbestos) , Amosite (brown asbestos)	
B00B - R1014 - Movement (175.51 m2)						
No Asbestos						
B00B - R1015 - Staff Study (14.59 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R1013/Ceiling Structures/Linings/S4					Chrysotile (white asbestos) , Amosite (brown asbestos)	
B00B - R1019 - General Storeroom (16.84 m2)						
No Asbestos						
B00B - R1020 - General Learning Space (52.72 m2)						
No Asbestos						
B00B - R1021 - Preparation (15.76 m2)						
No Asbestos						
B00B - R1022 - Laboratory L.S. (89.67 m2)						
No Asbestos						
B00B - R1023 - Movement (50.9 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	51m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R0029/Floor Coverings Res/Textile/S2					Chrysotile (white asbestos)	
B00B - R1024 - General Storeroom (3.25 m2)						
No Asbestos						
B00B - R1025 - Stairs (16.42 m2)						
No Asbestos						
B00B - R1026 - Stairs (18.62 m2)						
No Asbestos						
B00B - R1030 - Commonroom (137.41 m2)						
No Asbestos						
B00B - R1031 - Staff Kitchen (8.08 m2)						
No Asbestos						
B00B - R1032 - Staff Study (52.59 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00C - Art - 1953 - Brick/Block (Brick/Block)**Exterior**

Eaves Linings	Flat AC Sheeting	46m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00C/R0016/Ceiling Structures/Linings/S9				Chrysotile (white asbestos) , Amosite (brown asbestos)	
Ceiling Voids - Flat Roof	No Asbestos Found					
Underfloor Voids	No Asbestos Found					

Interior**B00C - R0001 - Resources Store (15.5 m2)**

No Asbestos

B00C - R0002 - Resources Store (15.5 m2)

No Asbestos

B00C - R0003 - Movement (100.73 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	
Floor Coverings Res/Textile	Vinyl Tiles	101m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00B/R1005/Floor Coverings Res/Textile/S5				Chrysotile (white asbestos)	

B00C - R0004 - Staff Study (23.04 m2)

No Asbestos

B00C - R0005 - Resources Space (5.82 m2)

No Asbestos

B00C - R0006 - Movement (23.33 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	

B00C - R0007 - Art Learning Space (52.64 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	

B00C - R0008 - Art Learning Space (52.78 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	

B00C - R0009 - Resources Store (43.41 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	

B00C - R0010 - Art Learning Space (52.79 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	

B00C - R0011 - Resources Store (25.37 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	
Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	

B00C - R0012 - Kiln Space (8.62 m2)

Ceiling Structures/Linings	Vermiculite					Limited Samples Taken
	8143/B00C/R0013/Ceiling Structures/Linings/S8				Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works	

B00C - R0013 - Staff - Toilet (6.12 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		
Ceiling Structures/Linings	Vermiculite					
	8143/B00C/R0013/Ceiling Structures/Linings/S8					Limited Samples Taken
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00C - R0014 - Distribution Board Cupboard (2 m2)				Note: No inspection of live electrical installation.		
No Asbestos						
B00C - R0015 - Pupil Entry (15.4 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	16m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00C/R0016/Ceiling Structures/Linings/S9					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00C - R0016 - Movement (4.07 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00C/R0016/Ceiling Structures/Linings/S9					Chrysotile (white asbestos) , Amosite (brown asbestos)
Wall Linings Internal	Flat AC Sheeting	6m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00C/R0016/Ceiling Structures/Linings/S9					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00C - R0017 - Stairs (4.16 m2)						
No Asbestos						
B00C - R0018 - General Storeroom (5.58 m2)						
Non Accessible						
B00C - R0019 - Stairs (4.22 m2)						
No Asbestos						
B00C - R0020 - Movement (16.05 m2)						
No Asbestos						
B00C - R1001 - General Storeroom (2.81 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	2.8m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00C/R0016/Ceiling Structures/Linings/S9					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00C - R1002 - Cleaning Store - Distributed (2.81 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	2.8m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00C/R0016/Ceiling Structures/Linings/S9					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00C - R1003 - Staff Study (26.17 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	2m2	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00B/R0029/Floor Coverings Res/Textile/S2					Chrysotile (white asbestos)
B00C - R1005 - Music Learning Space (58.77 m2)						
No Asbestos						
B00C - R1006 - Computer Learning Space (39.43 m2)						
No Asbestos						
B00C - R1009 - Music Learning Space (78.85 m2)						
No Asbestos						
B00C - R1010 - Staff - Toilet (6.23 m2)						
No Asbestos						
B00C - R1011 - Movement (17.55 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	18m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00B/R0029/Floor Coverings Res/Textile/S2					Chrysotile (white asbestos)
B00C - R1012 - Stairs (15.32 m2)						
No Asbestos						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00C - R1013 - Stairs (14.65 m2)						
No Asbestos						
B00C - R1014 - Movement (22.52 m2)						
Floor Coverings Res/Textile	Vinyl Tiles	23m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00B/R0029/Floor Coverings Res/Textile/S2					Chrysotile (white asbestos)	
B00C - R1015 - Movement (70.11 m2)						
No Asbestos						
B00C - R1030 - Music Learning Space (12.53 m2)						
No Asbestos						
B00C - R1031 - Music Store (12.82 m2)						
No Asbestos						
B00C - R1032 - Music Store (16.43 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	16m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00C/R0016/Ceiling Structures/Linings/S9					Chrysotile (white asbestos) , Amosite (brown asbestos)	
B00C - R1033 - Music Learning Space (15.61 m2)						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00D - Library/Technological & Applied Studies - 1992 - Brick/Block (Brick/Block)**Exterior**

Ceiling Voids	No Asbestos Found
Underfloor Voids	No Asbestos Found

Interior**B00D - R0001 - General Storeroom (11.3 m2)**

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00D - R0002 - Design L.S. (70.1 m2)

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00D - R0003 - Design L.S. (70.28 m2)

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00D - R0004 - Food Technology L.S. (105.07 m2)

No Asbestos

B00D - R0005 - Food/Research Space (17.14 m2)

No Asbestos

B00D - R0006 - General Storeroom (12.35 m2)

No Asbestos

B00D - R0007 - Food Technology L.S. (104.37 m2)

No Asbestos

B00D - R0009 - Staff Study (23.9 m2)

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00D - R0010 - Staff - Toilet (10.96 m2)

No Asbestos

B00D - R0011 - Cleaning Store - Distributed (1.23 m2)

No Asbestos

B00D - R0012 - Toilets-Disabled (3.4 m2)

No Asbestos

B00D - R0013 - Distribution Board Cupboard (0.96 m2)

Note: No inspection of live electrical installation.

No Asbestos

B00D - R0014 - General Storeroom (2.93 m2)

No Asbestos

B00D - R0016 - Movement (69.89 m2)

No Asbestos

B00D - R0017 - Stairs (8.15 m2)

No Asbestos

B00D - R0018 - Movement (3.75 m2)

No Asbestos

B00D - R0019 - Movement (81.15 m2)

No Asbestos

B00D - R0020 - Staff Study (31.54 m2)

No Asbestos

B00D - R1001 - Main Area (340.95 m2)

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found
---	-------------------

B00D - R1002 - Workroom (28.04 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

B00D - R1003 - Audio Visual Workroom (28.55 m2)

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

B00D - R1004 - Librarian (12.85 m2)

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

B00D - R1005 - General Storeroom (4.23 m2)

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

B00D - R1006 - Seminar (10.87 m2)

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

B00D - R1007 - Seminar (10.79 m2)

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

B00D - R1008 - Office/Store (11.09 m2)

Vinyl Tiles (Under Floor Covering/Carpet) No Asbestos Found

B00D - R1009 - Toilets-Boys (13.04 m2)

No Asbestos

B00D - R1010 - Toilets-Girls (12.61 m2)

No Asbestos

B00D - R1011 - Cleaning Store - Distributed (1.08 m2)

No Asbestos

B00D - R1012 - General Storeroom (4.5 m2)

No Asbestos

B00D - R1013 - Main Switchroom (0.74 m2)

No Asbestos

B00D - R1014 - Movement (11.82 m2)

No Asbestos

B00D - R1015 - Movement (44.43 m2)

No Asbestos

B00D - R1016 - Stairs (11.34 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00E - Technological & Applied Studies - 1969 - Brick/Block (Brick/Block)**Exterior**

Ceiling Voids	Non Accessible Area - Height Restriction					
Underfloor Voids	AC Fragments/Debris 8143/B00E/Underfloor Voids/S24	NA	Throughout	Some Damage - Unsealed (3)	Low (1)	Medium Priority (4-5) Chrysotile (white asbestos)

Interior**B00E - R0001 - Toilets-Boys (17.52 m2)**

Partition Walls (Cubicles)	Compressed AC Sheet	4m2	South	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
8143/B00E/R0002/Partition Walls (Cubicles)/S17						

B00E - R0002 - Toilets-Girls (16.16 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	6m2	North	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
8143/B00E/R0002/Partition Walls (Cubicles)/S17						

B00E - R0003 - Staff - Toilet (4.4 m2)

Partition Walls (Cubicles)	Compressed AC Sheet	3m2	East	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
8143/B00E/R0002/Partition Walls (Cubicles)/S17						

B00E - R0004 - Cleaning Store - Distributed (6.05 m2)

Hotwater Unit	Fibre Cement Pipe	4m	East	Minimal Damage (2)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
8143/B00E/R0004/Hotwater Unit/S23						

B00E - R0005 - Main Switchroom (1.82 m2)

Wall Linings Internal	Flat AC Sheeting					No Asbestos Detected
8143/B00E/R0005/Wall Linings Internal/S18						

B00E - R0012 - Staff Study (36.49 m2)

No Asbestos

B00E - R0013 - Study Space (25.22 m2)

Floor Coverings Res/Textile	Vinyl Tiles					No Asbestos Detected
8143/B00E/R0023/Floor Coverings Res/Textile/S19						

B00E - R0014 - Design L.S. (56.29 m2)

Floor Coverings Res/Textile	Vinyl Tiles					No Asbestos Detected
8143/B00E/R0023/Floor Coverings Res/Textile/S19						

B00E - R0015 - Materials Store (4.5 m2)

Floor Coverings Res/Textile	Vinyl Tiles					No Asbestos Detected
8143/B00E/R0023/Floor Coverings Res/Textile/S19						

B00E - R0016 - Darkroom Space (7.87 m2)

No Asbestos

B00E - R0017 - Secure Storeroom (26.52 m2)

Floor Coverings Res/Textile	Vinyl Tiles					No Asbestos Detected
8143/B00E/R0023/Floor Coverings Res/Textile/S19						

B00E - R0018 - Design L.S. (67.49 m2)

No Asbestos

B00E - R0019 - Materials Technology L.S. (106.11 m2)

No Asbestos

B00E - R0020 - Wood Technology Bay (19.65 m2)

No Asbestos

B00E - R0021 - Materials Technology L.S. (103.9 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

No Asbestos

B00E - R0022 - Dust Extraction Space (5.02 m2)

No Asbestos

B00E - R0023 - Movement (86.63 m2)

Floor Coverings Vinyl Tiles
Res/Textile

8143/B00E/R0023/Floor Coverings Res/Textile/S19

No Asbestos Detected

B00E - R0024 - Movement (46.02 m2)

No Asbestos

B00E - R0025 - Performance Workspace (105.46 m2)

No Asbestos

B00E - R0026 - Control Room (2.77 m2)

No Asbestos

B00E - R0027 - Performing Arts Store (28.77 m2)

No Asbestos

B00E - R0028 - Materials Technology L.S. (87.62 m2)

No Asbestos

B00E - R0029 - Metal Technology Bay (38.18 m2)

No Asbestos

B00E - R0030 - Movement (2.61 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		

B00F - Performing Arts - 1983 - Brick/Block (Brick/Block)**Exterior**

Eaves Linings	Flat AC Sheeting	14m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00F/R0006/Ceiling Structures/Linings/S15			Chrysotile (white asbestos) , Amosite (brown asbestos)		
Underfloor Voids - Slab on Ground	No Asbestos Found					
Ceiling Voids - Raked Ceiling	Non Accessible Area - Area inaccessible					

Interior**B00F - M0001 - Performing Arts Store (19.71 m2)**

No Asbestos

B00F - M0002 - Control Room (19.7 m2)

No Asbestos

B00F - R0001 - Multi-Purpose Space (388.85 m2)

No Asbestos

B00F - R0002 - Student Drinking Facilities (10.93 m2)

Floor Coverings Res/Textile	Vinyl Tiles	11m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00F/R0002/Floor Coverings Res/Textile/S14			Chrysotile (white asbestos)		

B00F - R0003 - Performing Arts Chair Store (10.93 m2)

No Asbestos

B00F - R0004 - Performing Arts Store (5.73 m2)

Ceiling Structures/Linings	Flat AC Sheeting	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00F/R0006/Ceiling Structures/Linings/S15			Chrysotile (white asbestos) , Amosite (brown asbestos)		
Wall Linings Internal	Flat AC Sheeting	5m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00F/R0006/Ceiling Structures/Linings/S15			Chrysotile (white asbestos) , Amosite (brown asbestos)		

B00F - R0005 - Stage (92.12 m2)

No Asbestos

B00F - R0006 - Performing Arts Changeroom (15.9 m2)

Ceiling Structures/Linings	Flat AC Sheeting	16m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00F/R0006/Ceiling Structures/Linings/S15			Chrysotile (white asbestos) , Amosite (brown asbestos)		

B00F - R0007 - Performing Arts Changeroom (9.9 m2)

Ceiling Structures/Linings	Flat AC Sheeting	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00F/R0006/Ceiling Structures/Linings/S15			Chrysotile (white asbestos) , Amosite (brown asbestos)		
Wall Linings Internal	Flat AC Sheeting	5m2	North	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00F/R0006/Ceiling Structures/Linings/S15			Chrysotile (white asbestos) , Amosite (brown asbestos)		

B00F - R0008 - Movement (78.27 m2)

No Asbestos

B00F - R0009 - Movement (12.69 m2)

No Asbestos

B00F - R0010 - Movement (2.65 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00F/R0006/Ceiling Structures/Linings/S15				Chrysotile (white asbestos) , Amosite (brown asbestos)		
B00F - R0011 - Movement (2.66 m2)						
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00F/R0006/Ceiling Structures/Linings/S15				Chrysotile (white asbestos) , Amosite (brown asbestos)		
B00F - R9001 - General Storeroom (87.85 m2)						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00G - General Learning/Science - 1972 - Brick/Block (Brick/Block)**Exterior**

Wall Cladding	Compressed AC Sheet 8143/B00G/Wall Cladding/S13					No Asbestos Detected
Ceiling Voids - Flat Roof	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior**B00G - R0001 - Movement (10.94 m2)**

Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Vinyl Tiles 8143/B00G/R0009/Floor Coverings Res/Textile/S11	11m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Wall Linings Internal	Flat AC Sheeting 8143/B00G/R0001/Wall Linings Internal/S27					No Asbestos Detected

B00G - R0002 - General Learning Space (70.45 m2)

Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Vinyl Tiles 8143/B00G/R0009/Floor Coverings Res/Textile/S11	71m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)

B00G - R0003 - Student Canteen (44.45 m2)

Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Wall Linings Internal	Flat AC Sheeting 8143/B00G/R1023/Ceiling Structures/Linings/S12	6m2	North, Upper portion	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)

B00G - R0004 - Student Canteen (5.13 m2)

Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
----------------------------	---	--	--	--	--	--

B00G - R0005 - Staff - Toilet (3.5 m2)

Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
----------------------------	---	--	--	--	--	--

B00G - R0006 - Movement (259.99 m2)

No Asbestos

B00G - R0007 - Movement (83.73 m2)

Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
Floor Coverings Res/Textile	Vinyl Tiles 8143/B00G/R0009/Floor Coverings Res/Textile/S11	84m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)

B00G - R0008 - Staff Study (26.27 m2)

Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken <i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>
----------------------------	---	--	--	--	--	--

B00G - R0009 - General Storeroom (4.96 m2)

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Vinyl Tiles 8143/B00G/R0009/Floor Coverings Res/Textile/S11	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B00G - R0010 - General Storeroom (6.02 m2)						
Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Vinyl Tiles 8143/B00G/R0012/Ceiling Structures/Linings/S10					No Asbestos Detected
B00G - R0011 - General Learning Space (54.02 m2)						
Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
B00G - R0012 - General Learning Space (54.32 m2)						
Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
B00G - R0013 - Cleaning Store - Distributed (1.13 m2)						
Electrical Mounting Board	Resinous Board 8143/B00G/R0013/Electrical Mounting Board/S28	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B00G - R0014 - Performing Arts Store (24.85 m2)						
No Asbestos						
B00G - R0015 - General Storeroom (11.32 m2)						
Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Vinyl Tiles 8143/B00G/R0009/Floor Coverings Res/Textile/S11	12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B00G - R0016 - General Storeroom (2.6 m2)						
Non Accessible						
B00G - R0017 - Distribution Board Cupboard (0.86 m2)						
No Asbestos Note: No inspection of live electrical installation.						
B00G - R0018 - General Learning Space (54.39 m2)						
Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
B00G - R0019 - General Storeroom (7.62 m2)						
Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
Floor Coverings Res/Textile	Vinyl Tiles 8143/B00G/R0009/Floor Coverings Res/Textile/S11	7.5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
B00G - R0020 - General Storeroom (11.27 m2)						
Ceiling Structures/Linings	Vermiculite 8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works
B00G - R0021 - Movement (31.32 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
No Asbestos						
B00G - R0022 - Stairs (4.11 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R0023 - Stairs (6.69 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R0024 - Stairs (11.19 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R0025 - Lift (1.68 m2)						
Recently Modified Space	Requires Inspection					
B00G - R1001 - General Storeroom (27.75 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Tiles	28m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00G/R0009/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00G - R1002 - Staff Study (27.38 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Tiles	28m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00G/R0009/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00G - R1004 - Distribution Board Cupboard (1.13 m2)						
					Note: No inspection of live electrical installation.	
No Asbestos						
B00G - R1005 - Staff - Toilet (7.76 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1006 - Movement (3.53 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Tiles	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00G/R0009/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00G - R1011 - Movement (96.88 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Tiles	97m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00G/R0009/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00G - R1012 - Staff Study (13.4 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1013 - Staff Study (20.06 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1014 - General Learning Space (41.35 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1015 - Distribution Board Cupboard (1.28 m2)					Note: No inspection of live electrical installation.	
No Asbestos						
B00G - R1016 - General Learning Space (40.44 m2)						
No Asbestos						
B00G - R1017 - General Storeroom (11.91 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
Floor Coverings Res/Textile	Vinyl Tiles	12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00G/R0009/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00G - R1018 - General Storeroom (12.6 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1019 - Withdrawal Space - 1hb (26.34 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1020 - General Storeroom (27.23 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1021 - Stairs (15.36 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1022 - Movement (65.52 m2)						
No Asbestos						
B00G - R1024 - Stairs (13.99 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1025 - Stairs (14.08 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
<i>Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works</i>						
B00G - R1026 - General Learning Space - Type 10 (48.17 m2)						
No Asbestos						
B00G - R1027 - Science Laboratory (42.08 m2)						
No Asbestos						
B00G - R1028 - Preparation - Science (35 m2)						
No Asbestos						
B00G - R1029 - Science Laboratory (38.93 m2)						
No Asbestos						
B00G - R1030 - General Learning Space - Type 10 (49.15 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
No Asbestos						
B00G - R1031 - Movement (55.77 m2)						
Recently Modified Space	Requires Inspection					
B00G - R1032 - Lift (2.39 m2)						
Recently Modified Space	Requires Inspection					
B00G - R1033 - Movement (2.26 m2)						
Recently Modified Space	Requires Inspection					
B00G - R2001 - Performance Workspace (70.79 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					
B00G - R2002 - Movement (14.72 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					
Floor Coverings Res/Textile	Vinyl Tiles	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00G/R0009/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00G - R2003 - Distribution Board Cupboard (1.12 m2)						
					Note: No inspection of live electrical installation.	
No Asbestos						
B00G - R2004 - Staff - Toilet (7.7 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					
B00G - R2005 - Movement (3.57 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					
B00G - R2006 - Laboratory L.S. (93.98 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					
Floor Coverings Res/Textile	Vinyl Tiles	94m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00G/R0009/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00G - R2007 - General Storeroom (9.63 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					
Floor Coverings Res/Textile	Vinyl Tiles	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00G/R0009/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00G - R2008 - Preparation (27.67 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					
Floor Coverings Res/Textile	Vinyl Tiles	28m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00G/R0009/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00G - R2009 - Laboratory L.S. (93.52 m2)						
Ceiling Structures/Linings	Vermiculite					
	8143/B00G/R0012/Ceiling Structures/Linings/S10					Limited Samples Taken
	Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works					

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No				Test Result		
Floor Coverings Res/Textile	Vinyl Tiles	94m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00G/R0009/Floor Coverings Res/Textile/S11				Chrysotile (white asbestos)		
B00G - R2010 - Movement (79.14 m2)						
Ceiling Structures/Linings	Vermiculite					
8143/B00G/R0012/Ceiling Structures/Linings/S10				Limited Samples Taken		
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
Floor Coverings Res/Textile	Vinyl Tiles	80m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00G/R0009/Floor Coverings Res/Textile/S11				Chrysotile (white asbestos)		
B00G - R2011 - General Learning Space (56.32 m2)						
Ceiling Structures/Linings	Vermiculite					
8143/B00G/R0012/Ceiling Structures/Linings/S10				Limited Samples Taken		
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00G - R2012 - Staff Study (25.45 m2)						
No Asbestos						
B00G - R2013 - Distribution Board Cupboard (0.85 m2)				Note: No inspection of live electrical installation.		
No Asbestos						
B00G - R2014 - Commonroom (8.86 m2)						
Ceiling Structures/Linings	Vermiculite					
8143/B00G/R0012/Ceiling Structures/Linings/S10				Limited Samples Taken		
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
Floor Coverings Res/Textile	Vinyl Tiles	9m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00G/R0009/Floor Coverings Res/Textile/S11				Chrysotile (white asbestos)		
B00G - R2015 - Chemical Store (26.06 m2)						
Ceiling Structures/Linings	Vermiculite					
8143/B00G/R0012/Ceiling Structures/Linings/S10				Limited Samples Taken		
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
Floor Coverings Res/Textile	Vinyl Tiles	27m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00G/R0009/Floor Coverings Res/Textile/S11				Chrysotile (white asbestos)		
B00G - R2016 - General Storeroom (26.67 m2)						
Ceiling Structures/Linings	Vermiculite					
8143/B00G/R0012/Ceiling Structures/Linings/S10				Limited Samples Taken		
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
Floor Coverings Res/Textile	Vinyl Tiles	27m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
8143/B00G/R0009/Floor Coverings Res/Textile/S11				Chrysotile (white asbestos)		
B00G - R2017 - General Learning Space (68.5 m2)						
Ceiling Structures/Linings	Vermiculite					
8143/B00G/R0012/Ceiling Structures/Linings/S10				Limited Samples Taken		
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00G - R2018 - Movement (65.51 m2)						
No Asbestos						
B00G - R2019 - Stairs (15.49 m2)						
Ceiling Structures/Linings	Vermiculite					
8143/B00G/R0012/Ceiling Structures/Linings/S10				Limited Samples Taken		
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00G - R2020 - Stairs (14.17 m2)						
Ceiling Structures/Linings	Vermiculite					
8143/B00G/R0012/Ceiling Structures/Linings/S10				Limited Samples Taken		
Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works						
B00G - R2021 - Stairs (14.17 m2)						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Ceiling Structures/Linings

Vermiculite

8143/B00G/R0012/Ceiling Structures/Linings/S10

Limited Samples Taken

Vermiculite Ceilings may contain asbestos. Asbestos testing MUST be conducted prior to any disturbance works

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00H - Pupil Facilities - 1983 - Brick/Block (Brick/Block)**Exterior**

Eaves Linings	Flat AC Sheeting	20m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00H/R0001/Ceiling Structures/Linings/S26				Chrysotile (white asbestos) , Amosite (brown asbestos) , Crocidolite (blue asbestos)	
Ceiling Voids - Flat Roof	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior**B00H - R0001 - Shower/Change (26.79 m2)**

Wall Linings Internal	Flat AC Sheeting	4m2	East, Upper portion	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00H/R0001/Wall Linings Internal/S25				Chrysotile (white asbestos)	
Ceiling Structures/Linings	Flat AC Sheeting	27m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00H/R0001/Ceiling Structures/Linings/S26				Chrysotile (white asbestos) , Amosite (brown asbestos) , Crocidolite (blue asbestos)	
Flue	Fibre Cement Pipe	6m2	Upper portion	Minimal Damage (2)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Unable to sample.					

B00H - R0002 - Shower/Change (26.79 m2)

Wall Linings Internal	Flat AC Sheeting	4m2	West, Upper portion	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00H/R0001/Wall Linings Internal/S25				Chrysotile (white asbestos)	
Ceiling Structures/Linings	Flat AC Sheeting	27m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8143/B00H/R0001/Ceiling Structures/Linings/S26				Chrysotile (white asbestos) , Amosite (brown asbestos) , Crocidolite (blue asbestos)	
Flue	Fibre Cement Pipe	6m	Upper portion	Minimal Damage (2)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Unable to sample.					

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B001 - Building Services - 2002 - Brick/Veneer (Brick/Veneer)

Exterior

Ceiling Voids - Flat Roof	No Asbestos Found
Underfloor Voids - Slab on Ground	No Asbestos Found

Interior

B001 - R0001 - Maintenance Bulk Store (27.04 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00J - General Learning - 1884 - Brick/Block (Brick/Block)

Exterior

Eaves Linings	Flat AC Sheeting 8143/B00J/Eaves Linings/S22	13m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Wall Cladding	Flat AC Sheeting 8143/B00J/Eaves Linings/S22	8m2	West	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Gable Verge Lining	Flat AC Sheeting 8143/B00J/Eaves Linings/S22	22m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3) Chrysotile (white asbestos)
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00J - R0001 - Movement (16.6 m2)

No Asbestos

B00J - R0002 - Administration - Clerical (18.23 m2)

No Asbestos

B00J - R0003 - Interview (20.54 m2)

No Asbestos

B00J - R0004 - Staff Kitchen (13.67 m2)

No Asbestos

B00J - R0005 - Staff - Toilet (6.59 m2)

No Asbestos

B00J - R0006 - Toilets-Unisex (2.07 m2)

Floor Coverings Res/Textile	Vinyl Tiles 8143/B00J/R0014/Floor Coverings Res/Textile/S21	No Asbestos Detected				
-----------------------------	--	-----------------------------	--	--	--	--

B00J - R0007 - General Storeroom (10.11 m2)

No Asbestos

B00J - R0008 - Movement (6.57 m2)

No Asbestos

B00J - R0009 - Staff Kitchen (15.46 m2)

No Asbestos

B00J - R0010 - Staff Study (29.28 m2)

No Asbestos

B00J - R0011 - Movement (13.59 m2)

No Asbestos

B00J - R0012 - Public Reception (16.46 m2)

No Asbestos

B00J - R0013 - Withdrawal Space - 1hb (24.58 m2)

Floor Coverings Res/Textile	Vinyl Tiles 8143/B00J/R0014/Floor Coverings Res/Textile/S21	No Asbestos Detected				
-----------------------------	--	-----------------------------	--	--	--	--

B00J - R0014 - Performing Arts Store (4.53 m2)

Floor Coverings Res/Textile	Vinyl Tiles 8143/B00J/R0014/Floor Coverings Res/Textile/S21	No Asbestos Detected				
-----------------------------	--	-----------------------------	--	--	--	--

B00J - R0015 - General Storeroom (7.3 m2)

No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00K - Building Services - 2002 - Brick/Veneer (Brick/Veneer)

Exterior

Ceiling Voids - Flat Roof	No Asbestos Found
Underfloor Voids - Slab on Ground	No Asbestos Found

Interior

B00K - R0001 - Maintenance Bulk Store (14.54 m2)

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

B00L - Building Services - 2002 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids - Slab on Ground No Asbestos Found

Ceiling Voids No Asbestos Found

Interior

B00L - R0001 - Maintenance Bulk Store (100.52 m2)

Electrical Mounting Board	Resinous Board	1Unit	North	Good Condition (1)	Low (1)	Low Priority (2-3)
---------------------------	----------------	-------	-------	--------------------	---------	--------------------

Assumed Asbestos - Electrical Hazard

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

B00M - Performing Arts - 2011 - Brick/Veneer (Brick/Veneer)**Exterior**

No Asbestos

Interior**B00M - M0001 - Control Room (5.21 m2)**

No Asbestos

B00M - R0001 - Movement Studio (325.15 m2)

No Asbestos

B00M - R0002 - Toilet - Lobby (3.24 m2)

No Asbestos

B00M - R0003 - Toilets - Boys (13.26 m2)

No Asbestos

B00M - R0004 - Access Student Shower/Toilet/Change (5.43 m2)

No Asbestos

B00M - R0005 - Toilet - Lobby (3.19 m2)

No Asbestos

B00M - R0006 - Toilets - Girls (14.83 m2)

No Asbestos

B00M - R0007 - Control Room (12.23 m2)

No Asbestos

B00M - R0008 - Store (37.06 m2)

No Asbestos

B00M - R0009 - Main Switch Board Cupboard (6.66 m2)

No Asbestos

B00M - R0010 - Movement (9.29 m2)

No Asbestos

B00M - R0011 - Change (29.08 m2)

No Asbestos

B00M - R0012 - Toilets - Boys (3.66 m2)

No Asbestos

B00M - R0013 - Change (30.01 m2)

No Asbestos

B00M - R0014 - Toilets - Girls (2.43 m2)

No Asbestos

B00M - R0015 - Movement (7.87 m2)

No Asbestos

B00M - R0016 - Chair Store (24.65 m2)

No Asbestos

B00M - R0017 - Other (25.45 m2)

No Asbestos

B00M - R0018 - Cleaning Store - Distributed (5.51 m2)

No Asbestos

B00M - R0019 - Store (1.11 m2)

No Asbestos

B00M - R0020 - Store (0.26 m2)

No Asbestos

B00M - R0021 - Store (0.26 m2)

No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
B00M - R0022 - Plant (41.5 m2)						
No Asbestos						
B00M - R0023 - Performance Workshop (132.22 m2)						
No Asbestos						
B00M - R0024 - External Movement (176.95 m2)						
No Asbestos						
B00M - R0025 - External Movement (121.16 m2)						
No Asbestos						
B00M - R0026 - Movement (3.47 m2)						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Demountables

Demountable details as per the AMS records as of 15 Feb 2017.

OS 601 - D10144 - Learning Unit - Standard/Withdrawal : Placement Date - 5/11/2015

Exterior

No Asbestos Found.

Interior

R1 - Entry

No Asbestos Found.

R2 - General Learning Space

No Asbestos Found.

R3 - Store

No Asbestos Found.

OS 601 - D10302 - Learning Unit - Standard/Withdrawal : Placement Date - 16/01/2014

Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.

Exterior

No Asbestos Found.

Interior

R1 - Entry

No Asbestos Found.

R2 - General Learning Space

No Asbestos Found.

R3 - Store

No Asbestos Found.

OS 600 - D10530 - Learning Unit - Small : Placement Date - 25/01/2012

Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.

Exterior

No Asbestos Found.

Interior

R1 - General Learning Space

No Asbestos Found.

OS 601 - D11926 - Learning Unit - Standard/Withdrawal : Placement Date - 8/01/2015

Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.

Exterior

No Asbestos Found.

Interior

R1 - Entry

No Asbestos Found.

R2 - General Learning Space

No Asbestos Found.

R3 - Store

No Asbestos Found.

NS 200 - D11955 - Art Learning Space/Workshop/Bulk Store : Placement Date - 11/01/2012

Exterior

No Asbestos Found.



Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Interior**R1 - Art Learning Space**

No Asbestos Found.

R2 - Workshop

No Asbestos Found.

R3 - Bulk Store

No Asbestos Found.

OS 601 - D12641 - Learning Unit - Standard/Withdrawal : Placement Date - 8/01/2015**Exterior**

Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos	11.52 m2

Interior**R1 - Entry**

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	8 m2

R2 - General Learning Space

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	55 m2

R3 - Store

Ceiling	Flat AC Sheet	Assumed Asbestos	10 m2
---------	---------------	------------------	-------

OS 600 - D14448 - Learning Unit - Small : Placement Date - 9/12/2015

Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.

Exterior

No Asbestos Found.

Interior**R1 - General Learning Space**

No Asbestos Found.

OS 904 - D14504 - Dormitory (Toilet/Shower) : Placement Date - 12/03/2007**Exterior**

No Asbestos Found.

Interior**R1 - Toilets**

No Asbestos Found.

R2 - Change Room

No Asbestos Found.

R3 - Toilets

No Asbestos Found.

R4 - Change Room

No Asbestos Found.

R5 - Store

No Asbestos Found.

R6 - Performance Workshop

No Asbestos Found.

OS 600 - D15922 - Learning Unit - Small : Placement Date - 23/11/2011**Exterior**

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	
No Asbestos Found.						
Interior						
R1 - General Learning Space						
No Asbestos Found.						
OS 837 - D17085 - Hcap Shower/Change/Toilet : Placement Date - 19/05/2016						
Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.						
Exterior						
No Asbestos Found.						
Interior						
R1 - Disabled Shower/Toilet						
No Asbestos Found.						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
Sample No					Test Result	

Listing of Electronic Attachments as of 22/03/2017

Available Asbestos Related Electronic Files

8143_ASB_050813_AMP.pdf

* Note : Refer to AMS for details of the attachment(s).

2017
