Asbestos Register

(Hazardous Materials and Risk Assessment)

School :	**Figtree Heights Public School (4462)**
Region :	**Illawarra and South East**
State Electorate :	**Keira**
Local Government Area :	**Wollongong**

Initial Survey :	**Noel Arnold & Associates : 21 - Apr - 2008**
Reviewed By :	**Greencap-NAA : 02 - Aug - 2016**

4462 - Figtree Heights Public School
Site Plan (10378)

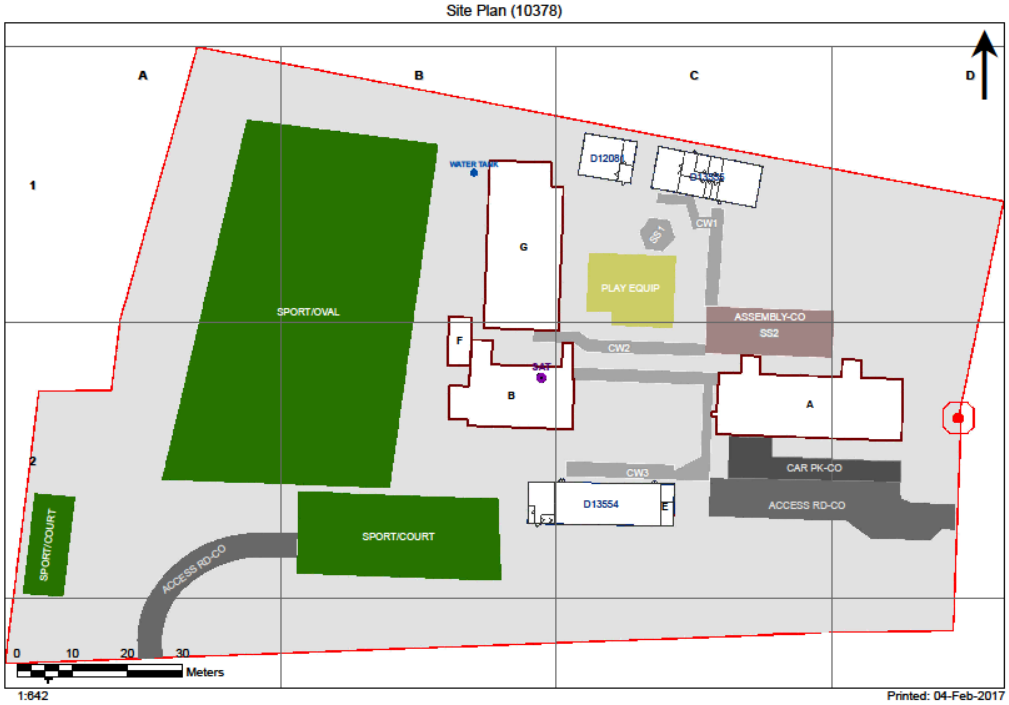

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00A - General Learning/Administration - 1971 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids - Packing to Floor Joists	No Asbestos Found					
Ceiling Voids - Flat Roof	No Asbestos Found					
Gable Verge Lining	Flat AC Sheeting	20m2	East, West	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Height Restriction					
In-fill-panel	Flat AC Sheeting	28m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0023/In-fill-panel/S3					**Chrysotile (white asbestos)**
Eaves Linings	Flat AC Sheeting	40m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Height Restriction					

Interior

B00A - R0002 - General Storeroom

No Asbestos

B00A - R0003 - Cleaning Distributed Store

No Asbestos

B00A - R0004 - Home Base

Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	59.59m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00A - R0005 - Home Base Store

Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00A - R0006 - Personal Effects Storage

Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	8m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00A - R0007 - Deputy Principal

Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	14.44m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00A - R0008 - Main Switch Board

Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Electrical Backing Board	Resinous Board	0.5m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					

B00A - R0009 - General Storeroom

Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Electrical Backing Board	Resinous Board	1m2	North	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0009/Electrical Backing Board/S11					**Chrysotile (white asbestos)**
B00A - R0010 - Principal						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	17.66m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R0011 - Entry Vestibule						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	9.44m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R0012 - Clerical Office						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	11.68m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R0013 - Sick Bay						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	9.27m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R0014 - Cleaning Distributed Store						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
B00A - R0015 - Duplicating Workroom						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R0016 - Staff Toilet						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
B00A - R0017 - Staff Toilet						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
B00A - R0018 - Staff Room						
Floor Coverings Res/Textile	Vinyl Tiles	33.48m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R0019 - Movement						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	21.48m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R0020 - Uniform Shop						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Floor Coverings Res/Textile	Vinyl Tiles	20.39m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R0021 - Clerical Office/Workroom						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
B00A - R0022 - General Storeroom						
Ceiling Structures/Linings	Vermiculite					
	4462/B00A/R0007/Ceiling Structures/Linings/S1					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R0023 - Movement						
In-fill-panel	Flat AC Sheeting	14m	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0023/In-fill-panel/S3					**Chrysotile (white asbestos)**
Wall Linings Internal	Flat AC Sheeting					
	4462/B00A/R0023/Wall Linings Internal/S4					**No Asbestos Detected**
B00A - R1002 - Home Base						
Floor Coverings Res/Textile	Vinyl Tiles	59.98m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R1003 - Home Base Store						
Floor Coverings Res/Textile	Vinyl Tiles	8m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R1004 - Personal Effects Storage						
Floor Coverings Res/Textile	Vinyl Tiles	14m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R1005 - Distribution Board					Note: No inspection of live electrical installation.	
No Asbestos						
B00A - R1006 - Home Base						
Floor Coverings Res/Textile	Vinyl Tiles	59.42m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R1007 - Home Base Store						
Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R1008 - Home Base						
Floor Coverings Res/Textile	Vinyl Tiles	59.41m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R1009 - Home Base Store						
Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R1010 - Personal Effects Storage						
Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0006/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00A - R1011 - Toilets - Girls						
No Asbestos						
B00A - R1012 - Cleaning Distributed Store						
No Asbestos						
B00A - R1013 - Toilets - Boys						

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
No Asbestos						
B00A - R1014 - Movement						
In-fill-panel	Flat AC Sheeting	14m	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00A/R0023/In-fill-panel/S3					**Chrysotile (white asbestos)**
Ceiling Structures/Linings	Flat AC Sheeting					
	4462/B00A/R1014/Ceiling Structures/Linings/S5					**No Asbestos Detected**
B00A - R9001 - General Storeroom						
No Asbestos						
B00A - R9002 - General Storeroom						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00B - General Learning - 1975 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids - Flat Roof	No Asbestos Found					
Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible					
Gable Verge Lining	Flat AC Sheeting 4462/B00B/Gable Verge Lining/S14					**No Asbestos Detected**
In-fill-panel	Flat AC Sheeting 4462/B00B/R0013/In-fill-panel/S6	16m2	South	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**
Eaves Linings	Flat AC Sheeting **Assumed Asbestos - Height Restriction**	20m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)

Interior

B00B - R0002 - Cleaning Supplies

No Asbestos

B00B - R0003 - Cleaning Distributed Store

No Asbestos

B00B - R0004 - Distribution Board

Note: No inspection of live electrical installation.

No Asbestos

B00B - R0005 - Special Programs Room

Ceiling Structures/Linings	Vermiculite 4462/B00B/R0005/Ceiling Structures/Linings/S7					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet) 4462/B00B/R0005/Floor Coverings Res/Textile/S12	74.58m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive 4462/B00B/R0005/Floor Coverings Res/Textile/S13	74.58m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**

B00B - R0010 - Home Base

Ceiling Structures/Linings	Vermiculite 4462/B00B/R0005/Ceiling Structures/Linings/S7					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive 4462/B00B/R0005/Floor Coverings Res/Textile/S13	74.82m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet) 4462/B00B/R0005/Floor Coverings Res/Textile/S12	74.82m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**

B00B - R0011 - Movement

No Asbestos

B00B - R0012 - Stairs

No Asbestos

B00B - R0013 - Movement

In-fill-panel	Flat AC Sheeting 4462/B00B/R0013/In-fill-panel/S6	6m	South	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**

B00B - R0014 - Stairs

No Asbestos

B00B - R0015 - Sports Store

No Asbestos

B00B - R0016 - Sports Store

No Asbestos

B00B - R1001 - Movement

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Ceiling Structures/Linings	Flat AC Sheeting	34m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00B/R1001/Ceiling Structures/Linings/S8					**Chrysotile (white asbestos)**
B00B - R1010 - Home Base						
No Asbestos						
B00B - R1011 - Home Base						
No Asbestos						
B00B - R1012 - Stairs						
Ceiling Structures/Linings	Flat AC Sheeting	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00B/R1001/Ceiling Structures/Linings/S8					**Chrysotile (white asbestos)**
B00B - R1013 - Stairs						
Ceiling Structures/Linings	Flat AC Sheeting	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00B/R1001/Ceiling Structures/Linings/S8					**Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00E - Building Services - 1972 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids - Flat Roof	Non Accessible Area - Area inaccessible					
Underfloor Voids - Packing to Floor Joists	No Asbestos Found					

Interior

B00E - R0001 - General Assistant/Bulk Store

Ceiling Structures/Linings	Flat AC Sheeting	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00E/R0001/Ceiling Structures/Linings/S9					**Chrysotile (white asbestos)**
Floor	Compressed AC Sheet	9.3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4462/B00E/R0001/Floor/S16					**Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00F - Pupil Facilities - 1977 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids - Packing to Floor Joists	Non Accessible Area - Area inaccessible door secured by coach bolts					
Ceiling Voids - Raked Ceiling	Non Accessible Area - Area inaccessible					
Gable Verge Lining	Flat AC Sheeting 4462/B00F/Gable Verge Lining/S15					**No Asbestos Detected**

Interior

B00F - R0001 - Toilets - Girls

Ceiling Structures/Linings	Flat AC Sheeting 4462/B00F/R0001/Ceiling Structures/Linings/S10	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**

B00F - R0002 - Toilets - Boys

Ceiling Structures/Linings	Flat AC Sheeting 4462/B00F/R0001/Ceiling Structures/Linings/S10	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00G - General Learning/Library - 2010 - Brick/Veneer (Brick/Veneer)

Exterior

Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible
Ceiling Voids	No Asbestos Found

Interior

B00G - R0001 - External Movement

No Asbestos

B00G - R0002 - General Storeroom

No Asbestos

B00G - R0003 - Practical Activities - 1hb

No Asbestos

B00G - R0004 - Withdrawal Space - 1hb

No Asbestos

B00G - R0005 - Home Base Store

No Asbestos

B00G - R0006 - Home Base

No Asbestos

B00G - R0007 - Reading Area

No Asbestos

B00G - R0008 - Communications Room

No Asbestos

B00G - R0009 - K.L.A. Store

No Asbestos

B00G - R0010 - Library Office/Workroom

No Asbestos

B00G - R0011 - General Storeroom

No Asbestos

B00G - R0012 - General Storeroom

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

Demountables

Demountable details as per the AMS records as of 15 Feb 2017.

OS 601 - D12081 - Learning Unit - Standard/Withdrawal : Placement Date - 4/02/2006

Exterior

Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos	11.52 m2

Interior

R1 - Entry

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	8 m2

R2 - General Learning Space

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	55 m2

R3 - Store

Ceiling	Flat AC Sheet	Assumed Asbestos	10 m2

OS 811 - D13554 - FSU/Shelter/Stores : Placement Date - 30/06/1995

Exterior

Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos	31.68 m2

Interior

R1 - Canteen

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	28 m2

R2 - Covered Area

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	145 m2

R3 - Store

Ceiling	Flat AC Sheet	Assumed Asbestos	4 m2

R4 - Sports Store

Ceiling	Flat AC Sheet	Assumed Asbestos	10 m2

R5 - Garden Store

Ceiling	Flat AC Sheet	Assumed Asbestos	8 m2

R6 - Change Room

Ceiling	Flat AC Sheet	Assumed Asbestos	3 m2

R7 - Store

Ceiling	Flat AC Sheet	Assumed Asbestos	2 m2

OS 534 - D13555 - Library/Group Study/Office/A V Store : Placement Date - 30/06/1995

Exterior

Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos	23.04 m2

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Interior						
R1 - Clerical Office						
End wall panel	Flat AC Sheet	Assumed Asbestos				18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				8 m2
R2 - Staff Room						
Ceiling	Flat AC Sheet	Assumed Asbestos				36 m2
R3 - Security Store						
Ceiling	Flat AC Sheet	Assumed Asbestos				8 m2
R4 - Principal						
Ceiling	Flat AC Sheet	Assumed Asbestos				16 m2
R5 - Staff Toilet						
Toilet partitions	Compressed AC Sheet	Assumed Asbestos				4 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				5 m2
R6 - Staff Toilet						
Toilet partitions	Compressed AC Sheet	Assumed Asbestos				4 m2
Ceiling	Flat AC Sheet	Assumed Asbestos				5 m2
R7 - Reading Area						
Ceiling	Flat AC Sheet	Assumed Asbestos				54 m2
R8 - Entry						
Ceiling	Flat AC Sheet	Assumed Asbestos				14 m2

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

Listing of Electronic Attachments as of 22/03/2017

Available Asbestos Related Electronic Files

4462_ASB_050813_AMP.pdf

* Note : Refer to AMS for details of the attachment(s).

2017
