Asbestos Register

(Hazardous Materials and Risk Assessment)

School :	**Irrawang Public School (4372)**
Region :	**Hunter/Central Coast**
State Electorate :	**Port Stephens**
Local Government Area :	**Port Stephens**

Initial Survey :	**Noel Arnold & Associates : 24 - Apr - 2008**
Reviewed By :	**Greencap-NAA : 10 - Feb - 2015**

4372 - Irrawang Public School
Site Plan (10439)

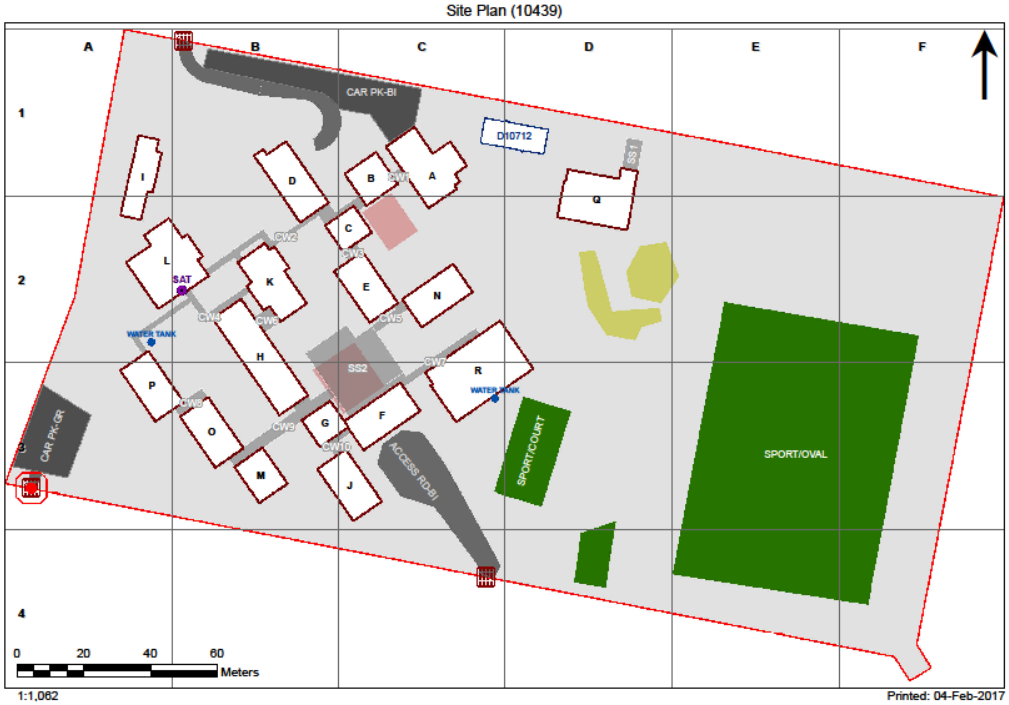

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00A - General Learning/Pupil Facilities - 1969 - Brick/Block (Brick/Block)

Exterior

In-fill-panel	Flat AC Sheeting	30m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00A - R0001 - Home Base Store

Floor Coverings Res/Textile	Vinyl Tiles	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00A - R0002 - Distribution Board

Note: No inspection of live electrical installation.

Electrical Backing Board	Resinous Board	1m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					

B00A - R0003 - Movement

Floor Coverings Res/Textile	Vinyl Tiles	10m2	North	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00A - R0004 - Home Base

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	56m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	8m2	Lower portion	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00A - R0005 - Home Base

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	87m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	12m2	Lower portion	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00A - R0006 - Toilets - Boys/Girls

No Asbestos

B00A - R0007 - Home Base Store

Floor Coverings Res/Textile	Vinyl Tiles	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00A - R0008 - Movement

Floor Coverings Res/Textile	Vinyl Tiles	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00A - R0009 - Movement

No Asbestos

B00A - R0010 - Movement

No Asbestos

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00B - Pupil Facilities/Communal Facilities - 1976 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids	No Asbestos Found
Underfloor Voids - Slab on Ground	No Asbestos Found

Interior

B00B - R0001 - Toilets - Boys

No Asbestos

B00B - R0002 - Cleaning Distributed Store

No Asbestos

B00B - R0003 - P.E. Store

Ceiling Structures/Linings	Flat AC Sheeting	50m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00H/R0006/Ceiling Structures/Linings/S5					**Chrysotile (white asbestos)**

B00B - R0004 - Toilets - Girls

No Asbestos

B00B - R0005 - Movement

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00C - General Learning - 1969 - Brick/Block (Brick/Block)

Exterior

In-fill-panel	Flat AC Sheeting	8m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids	No Asbestos Found					

Interior

B00C - R0001 - Home Base

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	57m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	6m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Thermacon Heater	Encapsulated Insulation material within unit	1Unit	North	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Sealed Unit					

B00C - R0002 - Home Base Store

Floor Coverings Res/Textile	Vinyl Tiles	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Thermacon Heater	Encapsulated Insulation material within unit	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Sealed unit					

B00C - R0003 - Movement

Floor Coverings Res/Textile	Vinyl Tiles	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00C - R0004 - Movement

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00D - General Learning/Administration - 1969 - Brick/Block (Brick/Block)

Exterior

In-fill-panel	Flat AC Sheeting	25m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00D - R0001 - General Storeroom

Floor Coverings Res/Textile	Vinyl Tiles	21m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00D - R0002 - Craft Store

Floor Coverings Res/Textile	Vinyl Tiles	8m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00D - R0003 - Cleaning Supplies

Floor Coverings Res/Textile	Vinyl Tiles	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00D - R0004 - General Assistant/Bulk Store

Floor Coverings Res/Textile	Vinyl Tiles	12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00D - R0005 - Movement

Floor Coverings Res/Textile	Vinyl Tiles	19m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00D - R0006 - General Storeroom

Floor Coverings Res/Textile	Vinyl Tiles	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00D - R0007 - Main Switch Board

Electrical Backing Board	Resinous Board	2Unit	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Thermacon Heater	Encapsulated Insulation material within unit	2Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Sealed Unit					

B00D - R0008 - Movement

No Asbestos

B00D - R0009 - Toilets - Boys/Girls

No Asbestos

B00D - R0010 - Practical Activities - 1hb

Floor Coverings Res/Textile	Vinyl Tiles	18m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00D - R0011 - Home Base

Infil panels	Flat AC Sheeting	11m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	73m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00E - General Learning - 1969 - Brick/Veneer (Brick/Veneer)

Exterior

In-fill-panel	Flat AC Sheeting	18m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00E - R0001 - Movement

No Asbestos

B00E - R0002 - Movement

Floor Coverings Res/Textile	Vinyl Tiles	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00E - R0003 - Distribution Board

Note: No inspection of live electrical installation.

Electrical Backing Board	Resinous Board	1m2	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					

B00E - R0004 - Home Base Store

Floor Coverings Res/Textile	Vinyl Tiles	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00E - R0005 - Home Base

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	56m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	8m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Thermacon Heater	Encapsulated Insulation material within unit	2Unit	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - sealed unit					

B00E - R0006 - Home Base

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	58m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	58m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Thermacon Heater	Encapsulated Insulation material within unit	2Unit	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Sealed unit					

B00E - R0007 - Home Base Store

Floor Coverings Res/Textile	Vinyl Tiles	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00E - R0008 - Movement

Floor Coverings Res/Textile	Vinyl Tiles	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00F - Pupil Facilities - 1969 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00F - R0001 - Movement

No Asbestos

B00F - R0002 - Toilets - Boys

Ceiling Structures/Linings	Flat AC Sheeting	24m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00F/R0002/Ceiling Structures/Linings/S4					**Chrysotile (white asbestos)**

B00F - R0003 - Toilets - Girls

Ceiling Structures/Linings	Flat AC Sheeting	3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00F/R0002/Ceiling Structures/Linings/S4					**Chrysotile (white asbestos)**

B00F - R0004 - Toilets - Girls

Ceiling Structures/Linings	Flat AC Sheeting	25m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00F/R0002/Ceiling Structures/Linings/S4					**Chrysotile (white asbestos)**

B00F - R0005 - Movement

Ceiling Structures/Linings	Flat AC Sheeting	42m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00F/R0002/Ceiling Structures/Linings/S4					**Chrysotile (white asbestos)**

B00F - R0006 - Canteen

Ceiling Structures/Linings	Flat AC Sheeting	44m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00F/R0002/Ceiling Structures/Linings/S4					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Vinyl Sheet					
	4372/B00F/R0006/Floor Coverings Res/Textile/S3					**No Asbestos Detected**
Electrical Backing Board	Resinous Board	1Unit	North	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					

B00F - R0007 - Staff Toilet

Floor Coverings Res/Textile	Vinyl Tiles	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Ceiling Structures/Linings	Flat AC Sheeting	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00F/R0002/Ceiling Structures/Linings/S4					**Chrysotile (white asbestos)**

B00F - R0008 - Canteen Office/Store

Floor Coverings Res/Textile	Vinyl Tiles	3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00F/R0002/Ceiling Structures/Linings/S4					**Chrysotile (white asbestos)**

B00F - R0009 - Uniform Shop

Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00F/R0002/Ceiling Structures/Linings/S4					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Vinyl Sheet					
	4372/B00F/R0006/Floor Coverings Res/Textile/S3					**No Asbestos Detected**

B00F - R0010 - Drinking Facilities

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00G - General Learning - 1969 - Brick/Block (Brick/Block)

Exterior

In-fill-panel	Flat AC Sheeting	12m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00G - R0001 - Home Base

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	57m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00G - R0002 - Home Base Store

Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00G - R0003 - Kiln Room

Floor Coverings Res/Textile	Vinyl Tiles	8m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	8m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Thermacon Heater	Encapsulated Insulation material within unit	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Sealed unit					

B00G - R0004 - Movement

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00H - Administration/General Learning - 1974 - Brick/Block (Brick/Block)

Exterior

In-fill-panel	Flat AC Sheeting	80m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00H - R0001 - Movement

No Asbestos

B00H - R0002 - Duplicating Workroom

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	2m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00H - R0003 - General Storeroom

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00H - R0004 - Clerical Office

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	16m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	2m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00H - R0005 - Movement

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	17m2	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00H - R0006 - General Storeroom

Floor Coverings Res/Textile	Vinyl Tiles	12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Ceiling Structures/Linings	Flat AC Sheeting	12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00H/R0006/Ceiling Structures/Linings/S5					**Chrysotile (white asbestos)**

B00H - R0007 - Staff Toilet

No Asbestos

B00H - R0008 - Staff Toilet

Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00H/R0006/Ceiling Structures/Linings/S5					**Chrysotile (white asbestos)**

B00H - R0009 - Staff Toilet

Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00H/R0006/Ceiling Structures/Linings/S5					**Chrysotile (white asbestos)**

B00H - R0010 - Principal

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	22m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Infil panels	Flat AC Sheeting	2m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
B00H - R0011 - Interview						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	2m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00H - R0012 - Distribution Board						Note: No inspection of live electrical installation.
Electrical Backing Board	Resinous Board	1Unit	North	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					
B00H - R0013 - Entry Vestibule						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00H - R0014 - Home Base						
Floor Coverings Res/Textile	Vinyl Tiles	57m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	4m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
B00H - R0015 - Home Base Store						
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Ceiling Structures/Linings	Flat AC Sheeting	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00F/R0002/Ceiling Structures/Linings/S4					**Chrysotile (white asbestos)**
B00H - R0016 - Movement						
Floor Coverings Res/Textile	Vinyl Tiles	16m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00H - R0017 - Home Base						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	57m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	4m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
B00H - R0018 - Home Base Store						
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00H - R0019 - General Storeroom						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00I - General Learning/Music - 1969 - Timber (Timber)

Exterior

Ceiling Voids	No Asbestos Found					
Underfloor Voids	Packing	2m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Area inaccessible					

Interior

B00I - R0001 - Movement

No Asbestos

B00I - R0002 - Uniform Shop

Electrical Backing Board	Resinous Board	1Unit	South	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					

B00I - R0003 - Special Programs Room

No Asbestos

B00I - R0004 - Special Programs Room

No Asbestos

B00I - R0005 - Music Store

No Asbestos

B00I - R0006 - Security Store

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00J - General Learning - 1969 - Brick/Veneer (Brick/Veneer)

Exterior

In-fill-panel	Flat AC Sheeting	20m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00J - R0001 - Movement

No Asbestos

B00J - R0002 - Home Base

Thermacon Heater	Encapsulated Insulation material within unit	1Unit	Throughout	Friable Asbestos (5)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Sealed unit					
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	59m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00J - R0003 - Home Base Store

Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00J - R0004 - Movement

No Asbestos

B00J - R0005 - Home Base

Thermacon Heater	Encapsulated Insulation material within unit	1Unit	Throughout	Friable Asbestos (5)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Sealed unit					
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	59m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00J - R0006 - Home Base Store

Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00K - Staff Facilities/Administration - 1976 - Brick/Block (Brick/Block)

Exterior

In-fill-panel	Flat AC Sheeting	20m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00K - R0001 - Movement

No Asbestos

B00K - R0002 - Duplicating Workroom

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	17m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	2m2	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00K - R0003 - Movement

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	27m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00K - R0004 - Staff Room Annexe

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	13m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	2m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00K - R0005 - Staff Toilet

Partition Walls (Cubicles)	Compressed AC Sheet	2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00K/R0005/Partition Walls (Cubicles)/S7					**Chrysotile (white asbestos)**

B00K - R0006 - Cleaning Distributed Store

Floor Coverings Res/Textile	Vinyl Tiles	2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00K - R0007 - Staff Toilet

Partition Walls (Cubicles)	Compressed AC Sheet	2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00K/R0005/Partition Walls (Cubicles)/S7					**Chrysotile (white asbestos)**

B00K - R0008 - Deputy Principal

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	13m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	2m2	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00K - R0009 - Staff Room Annexe

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	13m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Infil panels	Flat AC Sheeting	2m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
B00K - R0010 - General Storeroom						
Floor Coverings Res/Textile	Vinyl Tiles	13m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00K - R0011 - Distribution Board						Note: No inspection of live electrical installation.
Electrical Backing Board	Resinous Board	2Unit	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00K/R0011/Electrical Backing Board/S6					**Chrysotile (white asbestos)**
B00K - R0012 - Staff Room						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	70m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	8m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
B00K - R0013 - Movement						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00L - Library - 1976 - Brick/Block (Brick/Block)

Exterior

In-fill-panel	Flat AC Sheeting	20m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids - Raked Ceiling	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00L - R0001 - Reading Area

Infil panels	Flat AC Sheeting	8m2	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00L - R0002 - Seminar/Study

Infil panels	Flat AC Sheeting	2m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00L - R0003 - Seminar/Study

Infil panels	Flat AC Sheeting	2m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00L - R0004 - Toilets - Boys

Partition Walls (Cubicles)	Compressed AC Sheet	2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00K/R0005/Partition Walls (Cubicles)/S7					**Chrysotile (white asbestos)**

B00L - R0005 - Cleaning Distributed Store

No Asbestos

B00L - R0006 - Toilets - Girls

Partition Walls (Cubicles)	Compressed AC Sheet	2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00K/R0005/Partition Walls (Cubicles)/S7					**Chrysotile (white asbestos)**

B00L - R0007 - Movement

No Asbestos

B00L - R0008 - Movement

No Asbestos

B00L - R0009 - Distribution Board

Note: No inspection of live electrical installation.

Electrical Backing Board	Resinous Board	2Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00K/R0011/Electrical Backing Board/S6					**Chrysotile (white asbestos)**

B00L - R0010 - Library Office/Workroom

No Asbestos

B00L - R0011 - Library Office/Workroom

No Asbestos

B00L - R0012 - Communications Room

No Asbestos

B00L - R0013 - Movement

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00M - General Learning/Communal Facilities - 1943 - Brick/Block (Brick/Block)

Exterior

In-fill-panel	Flat AC Sheeting	8m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00M - R0001 - Movement

No Asbestos

B00M - R0002 - Craft Store

Floor Coverings Res/Textile	Vinyl Tiles	13m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00M - R0003 - Sports Store

Floor Coverings Res/Textile	Vinyl Tiles	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00M - R0004 - No Access

Floor Coverings Res/Textile	Vinyl Tiles	20m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00M - R0005 - Home Base

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	51m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	7m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Thermacon Heater	Encapsulated Insulation material within unit	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Sealed unit					

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00N - General Learning - 1969 - Brick/Veneer (Brick/Veneer)

Exterior

In-fill-panel	Flat AC Sheeting	15m2	East, West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					

Interior

B00N - R0001 - Practical Activities - 1hb

Floor Coverings Res/Textile	Vinyl Tiles	19m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

B00N - R0002 - Home Base

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	51m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	7m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00N - R0003 - Movement

Electrical Backing Board	Resinous Board	1Unit	North	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					

B00N - R0004 - Home Base

Floor Coverings Res/Textile	Vinyl Tiles	51m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Infil panels	Flat AC Sheeting	7m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00N - R0005 - Practical Activities - 1hb

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
B00O - General Learning - 1969 - Brick/Veneer (Brick/Veneer)						
Exterior						
In-fill-panel	Flat AC Sheeting	25m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					
Electrical Backing Board	Resinous Board	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					
Interior						
B00O - R0001 - Movement						
No Asbestos						
B00O - R0002 - Practical Activities - 1hb						
Floor Coverings Res/Textile	Vinyl Tiles	19m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00O - R0003 - Home Base						
Infil panels	Flat AC Sheeting	7m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Thermacon Heater	Encapsulated Insulation material within unit	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Sealed unit					
B00O - R0004 - Home Base						
Infil panels	Flat AC Sheeting	7m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Thermacon Heater	Encapsulated Insulation material within unit	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Seale unit					
B00O - R0005 - Practical Activities - 1hb						
Floor Coverings Res/Textile	Vinyl Tiles	20m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
B00P - General Learning - 1969 - Brick/Veneer (Brick/Veneer)						
Exterior						
In-fill-panel	Flat AC Sheeting	12m2	North, South	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00A/In-fill-panel/S1					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids	No Asbestos Found					
Underfloor Voids - Slab on Ground	No Asbestos Found					
Electrical Backing Board	Resinous Board	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					
Interior						
B00P - R0001 - Movement						
No Asbestos						
B00P - R0002 - Practical Activities - 1hb						
Floor Coverings Res/Textile	Vinyl Tiles	19m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
B00P - R0003 - Home Base						
Infil panels	Flat AC Sheeting	7m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Thermacon Heater	Encapsulated Insulation material within unit	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Sealed unit					
B00P - R0004 - Home Base						
Infil panels	Flat AC Sheeting	7m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**
Thermacon Heater	Encapsulated Insulation material within unit	1Unit	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Sealed unit					
B00P - R0005 - Practical Activities - 1hb						
Floor Coverings Res/Textile	Vinyl Tiles	19m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	4372/B00C/R0003/Floor Coverings Res/Textile/S2					**Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00Q - Pre-School Facilities - 2004 - Brick/Veneer (Brick/Veneer)

Exterior

Ceiling Voids	No Asbestos Found
Underfloor Voids	No Asbestos Found

Interior

B00Q - R0001 - Movement

No Asbestos

B00Q - R0002 - Entry Vestibule

No Asbestos

B00Q - R0003 - Security Store

No Asbestos

B00Q - R0004 - General Storeroom - Pre

No Asbestos

B00Q - R0005 - Home Base - Pre

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found

B00Q - R0006 - Practical Activities - Pre

No Asbestos

B00Q - R0007 - Toilets - Boys/Girls - Pre

No Asbestos

B00Q - R0008 - Laundry - Pre

No Asbestos

B00Q - R0009 - Access Shower/Toilet - Type 2

No Asbestos

B00Q - R0010 - Cleaning Distributed Store

No Asbestos

B00Q - R0011 - Kitchen - Pre

No Asbestos

B00Q - R0012 - Clerical Office - Pre

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found

B00Q - R0013 - Clerical Office - Pre

Vinyl Tiles (Under Floor Covering/Carpet)	No Asbestos Found

B00Q - R0014 - General Storeroom - Pre

No Asbestos

B00Q - R0015 - Movement

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00R - Multi Purpose Facilities - 2010 - Brick/Veneer (Brick/Veneer)

Exterior

Ceiling Voids - Raked Ceiling	No Asbestos Found
Underfloor Voids - Slab on Ground	

Interior

B00R - R0001 - Covered Outdoor Learning Area

No Asbestos

B00R - R0002 - Communal Space

No Asbestos

B00R - R0003 - Movement

No Asbestos

B00R - R0004 - Raised Platform

No Asbestos

B00R - R0005 - Hall Chair Store

No Asbestos

B00R - R0006 - Communal/Performance Store

No Asbestos

B00R - R0007 - P.E. Store

No Asbestos

B00R - R0008 - Movement

No Asbestos

B00R - R0009 - Toilets - Girls

No Asbestos

B00R - R0010 - Sound Cupboard

No Asbestos

B00R - R0011 - Movement

No Asbestos

B00R - R0012 - Toilets - Boys

No Asbestos

B00R - R0013 - Cleaning Supplies

No Asbestos

B00R - R0014 - Plant

No Asbestos

B00R - R0015 - Distribution Board Note: No inspection of live electrical installation.

No Asbestos

B00R - R0016 - Toilet - P

No Asbestos

B00R - R0017 - Movement

No Asbestos

B00R - R0018 - Movement

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

Demountables

Demountable details as per the AMS records as of 15 Feb 2017.

OS 534 - D10712 - Library/Group Study/Office/A V Store : Placement Date - 17/03/2003

Exterior

Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos	23.04 m2

Interior

R1 - Clerical Office

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	8 m2

R2 - Staff Room

Ceiling	Flat AC Sheet	Assumed Asbestos	36 m2

R3 - Security Store

Ceiling	Flat AC Sheet	Assumed Asbestos	8 m2

R4 - Principal

Ceiling	Flat AC Sheet	Assumed Asbestos	16 m2

R5 - Staff Toilet

Toilet partitions	Compressed AC Sheet	Assumed Asbestos	4 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	5 m2

R6 - Staff Toilet

Toilet partitions	Compressed AC Sheet	Assumed Asbestos	4 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	5 m2

R7 - Reading Area

Ceiling	Flat AC Sheet	Assumed Asbestos	54 m2

R8 - Entry

Ceiling	Flat AC Sheet	Assumed Asbestos	14 m2

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

Listing of Electronic Attachments as of 22/03/2017

There are no asbestos related file attachment(s) for this school.

2017
