Asbestos Register

(Hazardous Materials and Risk Assessment)

School :	**Tharbogang Public School (3195)**
Region :	**Riverina**
State Electorate :	**Murray**
Local Government Area :	**Griffith**

Initial Survey :	**Noel Arnold & Associates : 14 - May - 2008**
Reviewed By :	**Greencap-NAA : 15 - Jun - 2016**

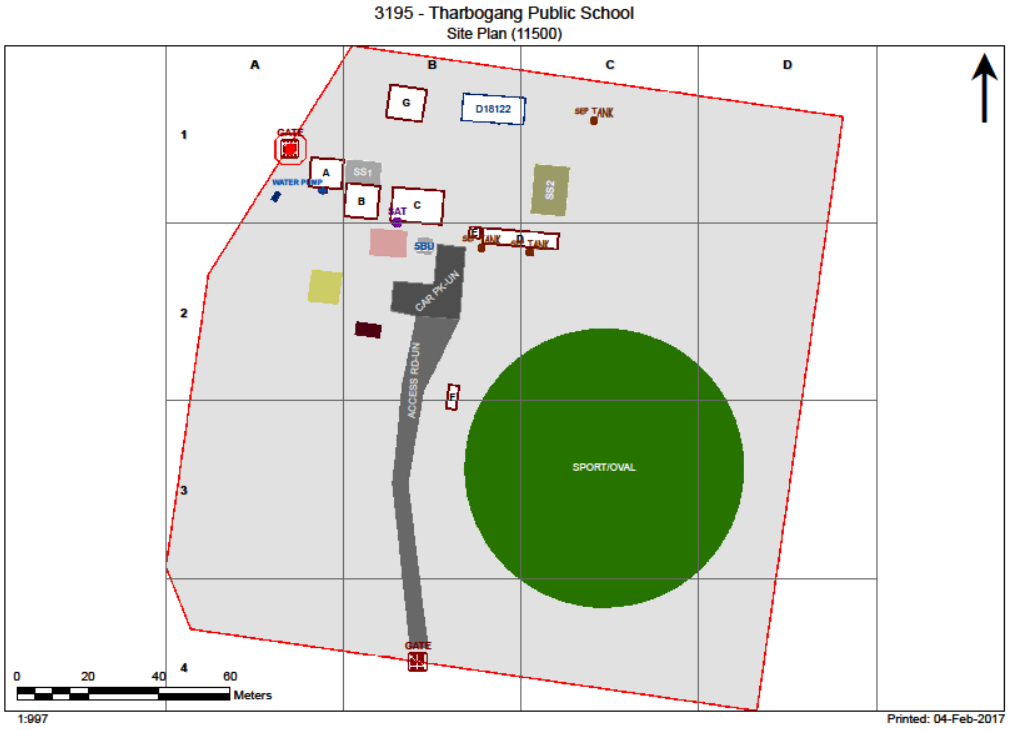

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00A - Library - 1960 - Timber (Timber)

Exterior

Ceiling Voids	Non Accessible Area - Height Restriction 4m height	
Underfloor Voids	No Asbestos Found	

Interior

B00A - R0001 - Movement

Flooring	Compressed AC Sheet	
	3195/B00C/R0005/Floor Coverings Res/Textile/S4	**No Asbestos Detected**

B00A - R0005 - Home Base

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00B - General Learning - 1960 - Timber (Timber)

Exterior

Ceiling Void	Non Accessible Area - Height Restriction 4m height					
Underfloor Void	No Asbestos Found					
Eaves Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	3195/B00B/R0007/Ceiling Structures/Linings/S2					**Chrysotile (white asbestos)**

Interior

B00B - R0001 - Movement

Flooring	Compressed AC Sheet					
	3195/B00C/R0005/Floor Coverings Res/Textile/S4					**No Asbestos Detected**

B00B - R0004 - Cleaning Supplies

Ceiling Structures/Linings	Flat AC Sheeting	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	3195/B00B/R0007/Ceiling Structures/Linings/S2					**Chrysotile (white asbestos)**

B00B - R0005 - General Storeroom

Wall Linings Internal	Flat AC Sheeting					
	3195/B00B/R0006/Wall Linings Internal/S3					**No Asbestos Detected**
Ceiling Structures/Linings	Flat AC Sheeting	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	3195/B00B/R0007/Ceiling Structures/Linings/S2					**Chrysotile (white asbestos)**

B00B - R0006 - Movement

Wall Linings Internal	Flat AC Sheeting					
	3195/B00B/R0006/Wall Linings Internal/S3					**No Asbestos Detected**
Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	3195/B00B/R0007/Ceiling Structures/Linings/S2					**Chrysotile (white asbestos)**

B00B - R0007 - Home Base

Ceiling Structures/Linings	Flat AC Sheeting	10m2	South facing	Good Condition (1)	Low (1)	Low Priority (2-3)
	3195/B00B/R0007/Ceiling Structures/Linings/S2					**Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00C - Administration/General Learning - 1946 - Timber (Timber)

Exterior

Ceiling Voids	Non Accessible Area - Height Restriction 4m height	
Underfloor Voids	No Asbestos Found	

Interior

B00C - R0001 - Practical Activities - 1hb

No Asbestos

B00C - R0002 - Home Base Store

No Asbestos

B00C - R0005 - Movement

Flooring	Compressed AC Sheet 3195/B00C/R0005/Floor Coverings Res/Textile/S4	**No Asbestos Detected**

B00C - R0006 - Home Base

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00D - Pupil Facilities - 1946 - Brick/Block (Brick/Block)

Exterior

Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible
Ceiling Voids - Flat Roof	Non Accessible Area - Area inaccessible

Interior

B00D - R0001 - Toilets - Girls

No Asbestos

B00D - R0002 - Movement

No Asbestos

B00D - R0003 - Toilets - Boys

No Asbestos

B00D - R0004 - Home Base Store

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00G - Library - 2010 - Fibre Cement Clad (Fibre Cement Clad)

Exterior

Ceiling Voids	No Asbestos Found
Underfloor Voids	No Asbestos Found

Interior

B00G - R0001 - Reading Area

No Asbestos

B00G - R0002 - K.L.A. Store

No Asbestos

B00G - R0003 - Practical Activities

No Asbestos

B00G - R0004 - External Movement

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

Build+1 - Pupil Facilities

Exterior

Gable Ends	Flat AC Sheeting	4m2	North & South	Good Condition (1)	Low (1)	Low Priority (2-3)
	3195/Build+1/Exterior/Gable Ends/S5					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

Interior

Build+1 - Room+1 - Added Room

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

Demountables

Demountable details as per the AMS records as of 15 Feb 2017.

OS 500 - D18122 - Admin - Library : Placement Date - 21/11/2001

Exterior

Step Treads	Compressed AC Sheet	Assumed Asbestos	1.08 m2
Landing	Compressed AC Sheet	Assumed Asbestos	1.2 m2
Eave Lining	Flat AC Sheet	Assumed Asbestos	20.16 m2

Interior

R1 - Entry

End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	13 m2

R2 - Principal

Ceiling	Flat AC Sheet	Assumed Asbestos	18 m2

R3 - Staff Room/Kitchen

Ceiling	Flat AC Sheet	Assumed Asbestos	19 m2

R4 - Clerical Office

Ceiling	Flat AC Sheet	Assumed Asbestos	18 m2

R5 - Library

Ceiling	Flat AC Sheet	Assumed Asbestos	54 m2

R6 - Storeroom

Ceiling	Flat AC Sheet	Assumed Asbestos	0 m2

R7 - Staff Toilet

Toilet partitions	Compressed AC Sheet	Assumed Asbestos	6 m2
End wall panel	Flat AC Sheet	Assumed Asbestos	18 m2
Ceiling	Flat AC Sheet	Assumed Asbestos	4 m2

R8 - Entry to toilet

Ceiling	Flat AC Sheet	Assumed Asbestos	0 m2

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

Listing of Electronic Attachments as of 22/03/2017

There are no asbestos related file attachment(s) for this school.

2017
