Asbestos Register

(Hazardous Materials and Risk Assessment)

School :	**Blacktown Boys High School (8244)**
Region :	**Western Sydney**
State Electorate :	**Blacktown**
Local Government Area :	**Blacktown**

Initial Survey :	**Noel Arnold & Associates : 21 - Apr - 2008**
Reviewed By :	**Greencap-NAA : 10 - Jun - 2015**

8244 - Blacktown Boys High School
Site Plan (10885)

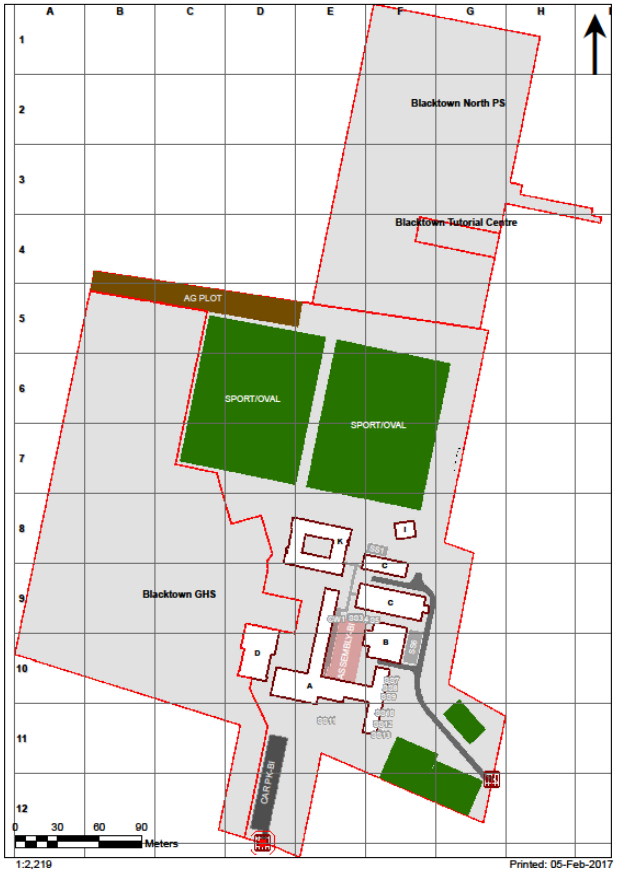

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

B00A - Various - 1956 - Brick/Block (Brick/Block)

Exterior

Eaves Linings	Flat AC Sheeting	30m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Height Restriction					
Ceiling Voids - Raked Ceiling	Non Accessible Area					
	- Area inaccessible					
Underfloor Voids	No Asbestos Found					

Interior

B00A - R0001 - Laboratory L.S.

Flue Pipe	Fibre Cement Pipe	6m	South East Corner	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R0001/Flue Pipe/S32			**Chrysotile (white asbestos) , Amosite (brown asbestos)**		

B00A - R0002 - Preparation

No Asbestos

B00A - R0003 - General Storeroom

No Asbestos

B00A - R0004 - General Learning Space

Flue Pipe	Fibre Cement Pipe	6m	North East Corner	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R0001/Flue Pipe/S32			**Chrysotile (white asbestos) , Amosite (brown asbestos)**		

B00A - R0005 - Distribution Board Cupboard

Note: No inspection of live electrical installation.

No Asbestos

B00A - R0006 - General Storeroom

No Asbestos

B00A - R0007 - Movement

Floor Coverings Res/Textile	Vinyl Tiles					
	8244/B00A/R0007/Floor Coverings Res/Textile/S2				**No Asbestos Detected**	

B00A - R0008 - Tiered Learning Area

Flue Pipe	Fibre Cement Pipe	2m	South East Corner	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R0001/Flue Pipe/S32			**Chrysotile (white asbestos) , Amosite (brown asbestos)**		

B00A - R0009 - Preparation

Flue Pipe	Fibre Cement Pipe	6m	Middle portion	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R0001/Flue Pipe/S32			**Chrysotile (white asbestos) , Amosite (brown asbestos)**		

B00A - R0010 - Staff Study

No Asbestos

B00A - R0011 - Laboratory L.S.

Flue Pipe	Fibre Cement Pipe	1m	North East Corner	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R0001/Flue Pipe/S32			**Chrysotile (white asbestos) , Amosite (brown asbestos)**		

B00A - R0012 - Commonroom

No Asbestos

B00A - R0013 - Administration - Clerical

No Asbestos

B00A - R0014 - Staff Kitchen

No Asbestos

B00A - R0015 - Staff - Toilet

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority

	Sample No	Test Result

No Asbestos

B00A - R0016 - Staff - Toilet

No Asbestos

B00A - R0017 - Duplicating Workroom

No Asbestos

B00A - R0018 - Security Store

No Asbestos

B00A - R0019 - Administration - Clerical

No Asbestos

B00A - R0020 - Principal Office

No Asbestos

B00A - R0021 - Movement

No Asbestos

B00A - R0022 - Movement

No Asbestos

B00A - R0023 - Interview/Office - Type 1

No Asbestos

B00A - R0024 - Staff - Toilet

No Asbestos

B00A - R0025 - Distribution Board Cupboard Note: No inspection of live electrical installation.

No Asbestos

B00A - R0026 - Ancillary Staff

No Asbestos

B00A - R0027 - Entry

No Asbestos

B00A - R0028 - Librarian

No Asbestos

B00A - R0029 - Audio Visual Workroom

No Asbestos

B00A - R0030 - Workroom

No Asbestos

B00A - R0031 - Main Area

No Asbestos

B00A - R0032 - Main Switchroom

Flooring	Compressed AC Sheet 8244/B00A/R0032/Flooring/S31	**No Asbestos Detected**

B00A - R0033 - Seminar

No Asbestos

B00A - R0034 - Seminar

No Asbestos

B00A - R0035 - Seminar

No Asbestos

B00A - R0036 - Movement

No Asbestos

B00A - R0037 - Administration - Clerical

No Asbestos

B00A - R0038 - Clinic-Toilets

No Asbestos

B00A - R0039 - Clinic - Boys

No Asbestos

B00A - R0040 - Deputy Principal Office

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority

	Sample No	Test Result

No Asbestos

B00A - R0041 - Administration - Clerical

No Asbestos

B00A - R0042 - General Storeroom

No Asbestos

B00A - R0043 - Movement

No Asbestos

B00A - R0044 - General Learning Space

Floor Coverings Res/Textile	Vinyl Sheet	
	8244/B00A/R0052/Floor Coverings Res/Textile/S29	**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive	
	8244/B00A/R0052/Floor Coverings Res/Textile/S30	**No Asbestos Detected**

B00A - R0045 - Distribution Board Cupboard Note: No inspection of live electrical installation.

No Asbestos

B00A - R0046 - General Storeroom

No Asbestos

B00A - R0047 - General Storeroom

No Asbestos

B00A - R0048 - General Storeroom

No Asbestos

B00A - R0049 - Staff Study

Floor Coverings Res/Textile	Adhesive	
	8244/B00A/R0052/Floor Coverings Res/Textile/S30	**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Sheet	
	8244/B00A/R0052/Floor Coverings Res/Textile/S29	**No Asbestos Detected**

B00A - R0050 - General Learning Space

Floor Coverings Res/Textile	Adhesive	
	8244/B00A/R0052/Floor Coverings Res/Textile/S30	**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Sheet	
	8244/B00A/R0052/Floor Coverings Res/Textile/S29	**No Asbestos Detected**

B00A - R0051 - General Learning Space

Floor Coverings Res/Textile	Adhesive	
	8244/B00A/R0052/Floor Coverings Res/Textile/S30	**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Sheet	
	8244/B00A/R0052/Floor Coverings Res/Textile/S29	**No Asbestos Detected**

B00A - R0052 - Computer Learning Space

Floor Coverings Res/Textile	Vinyl Sheet	
	8244/B00A/R0052/Floor Coverings Res/Textile/S29	**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive	
	8244/B00A/R0052/Floor Coverings Res/Textile/S30	**No Asbestos Detected**

B00A - R0053 - General Storeroom

No Asbestos

B00A - R0054 - Cleaning Store - Distributed

No Asbestos

B00A - R0055 - Computer Resource

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**

B00A - R0056 - Computer Store

No Asbestos

B00A - R0057 - Computer Learning Space

No Asbestos

B00A - R0058 - Movement

No Asbestos

B00A - R0059 - General Storeroom

No Asbestos

B00A - R0060 - Stairs

No Asbestos

B00A - R0061 - Stairs

No Asbestos

B00A - R0062 - Stairs

No Asbestos

B00A - R1001 - General Learning Space

No Asbestos

B00A - R1002 - General Learning Space

No Asbestos

B00A - R1004 - General Storeroom

No Asbestos

B00A - R1005 - Staff Study

No Asbestos

B00A - R1006 - General Storeroom

No Asbestos

B00A - R1007 - Distribution Board Cupboard Note: No inspection of live electrical installation.

No Asbestos

B00A - R1008 - General Storeroom

Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1015/Floor Coverings Res/Textile/S34					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1015/Floor Coverings Res/Textile/S33					**Chrysotile (white asbestos)**

B00A - R1009 - General Learning Space

No Asbestos

B00A - R1010 - General Learning Space

No Asbestos

B00A - R1011 - General Learning Space

No Asbestos

B00A - R1012 - Movement

Floor Coverings Res/Textile	Vinyl Tiles					
	8244/B00A/R1012/Floor Coverings Res/Textile/S1					**No Asbestos Detected**

B00A - R1013 - General Learning Space

Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	70m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1013/Floor Coverings Res/Textile/S35					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1013/Floor Coverings Res/Textile/S36					**No Asbestos Detected**

B00A - R1014 - Interview/Office - Type 1

Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1013/Floor Coverings Res/Textile/S36					**No Asbestos Detected**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	19m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1013/Floor Coverings Res/Textile/S35					Chrysotile (white asbestos)
B00A - R1015 - General Storeroom						
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1015/Floor Coverings Res/Textile/S34					No Asbestos Detected
Floor Coverings Res/Textile	Vinyl Tiles	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1015/Floor Coverings Res/Textile/S33					Chrysotile (white asbestos)
B00A - R1016 - Cleaning Store - Distributed						
No Asbestos						
B00A - R1017 - Movement						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	62m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1015/Floor Coverings Res/Textile/S33					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1015/Floor Coverings Res/Textile/S34					No Asbestos Detected
B00A - R1018 - General Learning Space						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	53m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1013/Floor Coverings Res/Textile/S35					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1015/Floor Coverings Res/Textile/S34					No Asbestos Detected
B00A - R1019 - General Learning Space						
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1015/Floor Coverings Res/Textile/S34					No Asbestos Detected
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	53m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1013/Floor Coverings Res/Textile/S35					Chrysotile (white asbestos)
B00A - R1020 - Staff Study						
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1013/Floor Coverings Res/Textile/S36					No Asbestos Detected
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	70m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1013/Floor Coverings Res/Textile/S35					Chrysotile (white asbestos)
B00A - R1021 - General Learning Space						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	70m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1015/Floor Coverings Res/Textile/S33					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1015/Floor Coverings Res/Textile/S34					No Asbestos Detected
B00A - R1022 - Music Learning Space						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	53m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1015/Floor Coverings Res/Textile/S33					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1015/Floor Coverings Res/Textile/S34					No Asbestos Detected
B00A - R1023 - Movement						
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1015/Floor Coverings Res/Textile/S34					No Asbestos Detected

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	45m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1015/Floor Coverings Res/Textile/S33					**Chrysotile (white asbestos)**
B00A - R1024 - Cleaning Store - Distributed						
No Asbestos						
B00A - R1025 - General Storeroom						
Floor Coverings Res/Textile	Vinyl Tiles	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1015/Floor Coverings Res/Textile/S33					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1015/Floor Coverings Res/Textile/S34					**No Asbestos Detected**
B00A - R1026 - Staff Study						
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1015/Floor Coverings Res/Textile/S34					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	19m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1015/Floor Coverings Res/Textile/S33					**Chrysotile (white asbestos)**
B00A - R1027 - Music Learning Space						
Floor Coverings Res/Textile	Adhesive					
	8244/B00A/R1015/Floor Coverings Res/Textile/S34					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	71m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00A/R1015/Floor Coverings Res/Textile/S33					**Chrysotile (white asbestos)**
B00A - R1028 - Stairs						
No Asbestos						
B00A - R1029 - Stairs						
No Asbestos						
B00A - R1030 - Stairs						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

B00B - Pupil Facilities - 1956 - Concrete (Concrete)

Exterior

Eaves Linings	Flat AC Sheeting	30m2	North, South, East, West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Ceiling Voids - Raked Ceiling	Non Accessible Area - Area inaccessible					
Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible					

Interior

B00B - R0001 - Staff - Toilet

Ceiling Structures/Linings	Flat AC Sheeting	2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00B - R0002 - Ancillary Staff

Floor Coverings Res/Textile	Vinyl Tiles					
	8244/B00B/R0002/Floor Coverings Res/Textile/S18					**No Asbestos Detected**
Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00B - R0003 - General Storeroom

Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
Floor Coverings Res/Textile	Vinyl Tiles					
	8244/B00B/R0002/Floor Coverings Res/Textile/S18					**No Asbestos Detected**

B00B - R0004 - Student Canteen

Floor Coverings Res/Textile	Vinyl Tiles					
	8244/B00B/R0002/Floor Coverings Res/Textile/S18					**No Asbestos Detected**
Ceiling Structures/Linings	Flat AC Sheeting	41m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00B - R0005 - Maintenance Bulk Store

Ceiling Structures/Linings	Flat AC Sheeting	12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00B - R0006 - Sport Equipment Store

Wall Linings Internal	Flat AC Sheeting					
	8244/B00B/R0006/Wall Linings Internal/S15					**No Asbestos Detected**
Ceiling Structures/Linings	Flat AC Sheeting	28m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00B - R0007 - Movement

Ceiling Structures/Linings	Flat AC Sheeting	236m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

B00B - R0008 - General Storeroom

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
No Asbestos						
B00B - R0009 - Movement						
Ceiling Structures/Linings	Compressed AC Sheet	5m2	Entrance	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
B00B - R0010 - Cleaning Store - Distributed						
Ceiling Structures/Linings	Flat AC Sheeting	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
B00B - R0012 - General Storeroom						
Ceiling Structures/Linings	Flat AC Sheeting	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
B00B - R0013 - Shower/Change						
Wall Linings Internal	Flat AC Sheeting					
	8244/B00B/R0013/Wall Linings Internal/S17					**No Asbestos Detected**
Ceiling Structures/Linings	Flat AC Sheeting	96m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
B00B - R0014 - Toilets - Boys						
Partition Walls (Cubicles)	Compressed AC Sheet					
	8244/B00B/R0014/Partition Walls (Cubicles)/S16					**No Asbestos Detected**
Ceiling Structures/Linings	Flat AC Sheeting	126m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00B/R0004/Ceiling Structures/Linings/S28					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

B00C - Technological & Applied Studies - 1956 - Brick/Block (Brick/Block)

Exterior

Eaves Linings	Flat AC Sheeting	30m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0009/High level fill panel/S24				Chrysotile (white asbestos) , Amosite (brown asbestos)	
Underfloor Voids	No Asbestos Found					
Ceiling Voids - Raked Ceiling	Non Accessible Area					
	- Area inaccessible					

Interior

B00C - M0001 - Resource/Project Store

No Asbestos

B00C - M0002 - Resource/Project Store

No Asbestos

B00C - R0001 - Computer Learning Space

Wall Linings Internal	Flat AC Sheeting	15m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0009/High level fill panel/S24				Chrysotile (white asbestos) , Amosite (brown asbestos)	

B00C - R0002 - Computer Store

High level fill panel	Flat AC Sheeting	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0009/High level fill panel/S24				Chrysotile (white asbestos) , Amosite (brown asbestos)	

B00C - R0003 - Materials Store

High level fill panel	Flat AC Sheeting	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0009/High level fill panel/S24				Chrysotile (white asbestos) , Amosite (brown asbestos)	

B00C - R0004 - Resource/Project Store

High level fill panel	Flat AC Sheeting	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0009/High level fill panel/S24				Chrysotile (white asbestos) , Amosite (brown asbestos)	

B00C - R0005 - Design L.S.

High level fill panel	Flat AC Sheeting	40m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0009/High level fill panel/S24				Chrysotile (white asbestos) , Amosite (brown asbestos)	

B00C - R0006 - Materials Store

High level fill panel	Flat AC Sheeting	40m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0009/High level fill panel/S24				Chrysotile (white asbestos) , Amosite (brown asbestos)	

B00C - R0007 - Materials Technology L.S.

High level fill panel	Flat AC Sheeting	40m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0009/High level fill panel/S24				Chrysotile (white asbestos) , Amosite (brown asbestos)	

B00C - R0008 - Welding Area

High level fill panel	Flat AC Sheeting	20m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0009/High level fill panel/S24				Chrysotile (white asbestos) , Amosite (brown asbestos)	

B00C - R0009 - Materials Technology L.S.

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result
High level fill panel	Flat AC Sheeting	20m2	East and West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0009/High level fill panel/S24					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00C - R0010 - Materials Store						
Stored Furnace	Encapsulated Insulation material within unit	1Unit	Shelving	Minimal Damage (2)	Medium (2)	Medium Priority (4-5)
	8244/B00C/R0010/Stored Furnace/S23					Chrysotile (white asbestos) , Amosite (brown asbestos)
High level fill panel	Flat AC Sheeting	NA	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Height Restriction					
B00C - R0011 - Materials Store						
Wall Linings Internal	Flat AC Sheeting					
	8244/B00C/R0036/Wall Linings Internal/S6					No Asbestos Detected
B00C - R0012 - Resource/Project Store						
No Asbestos						
B00C - R0013 - Materials Technology L.S.						
Wall Linings Internal	Flat AC Sheeting					
	8244/B00C/R0036/Wall Linings Internal/S6					No Asbestos Detected
B00C - R0014 - Materials Technology L.S.						
No Asbestos						
B00C - R0015 - Materials Store						
No Asbestos						
B00C - R0016 - Staff Study						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	19m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0016/Floor Coverings Res/Textile/S25					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive					
	8244/B00C/R0016/Floor Coverings Res/Textile/S26					No Asbestos Detected
B00C - R0017 - Staff - Toilet						
High level fill panel	Flat AC Sheeting	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0009/High level fill panel/S24					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00C - R0018 - Cleaning Store - Distributed						
No Asbestos						
B00C - R0019 - Staff Study						
Floor Coverings Res/Textile	Adhesive					
	8244/B00C/R0016/Floor Coverings Res/Textile/S26					No Asbestos Detected
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	26m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0016/Floor Coverings Res/Textile/S25					Chrysotile (white asbestos)
B00C - R0020 - Materials Technology L.S.						
No Asbestos						
B00C - R0021 - Materials Store						
No Asbestos						
B00C - R0022 - Movement						
Ceiling Structures/Linings	Flat AC Sheeting	2m2	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0022/Ceiling Structures/Linings/S4					Chrysotile (white asbestos) , Amosite (brown asbestos)
B00C - R0024 - Movement						
No Asbestos						
B00C - R0029 - Sport Equipment Store						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result
Ceiling Structures/Linings	Flat AC Sheeting	22m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0029/Ceiling Structures/Linings/S10					**Chrysotile (white asbestos)**
B00C - R0030 - Cleaning Store - Distributed						
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0030/Floor Coverings Res/Textile/S20					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adesive					
	8244/B00C/R0030/Floor Coverings Res/Textile/S21					**No Asbestos Detected**
Ceiling Structures/Linings	Flat AC Sheeting	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0030/Ceiling Structures/Linings/S22					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
B00C - R0033 - Movement						
No Asbestos						
B00C - R0034 - Distribution Board Cupboard						Note: No inspection of live electrical installation.
Electrical Backing Board	Resinous Board	2Unit	West	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					
B00C - R0035 - Dust Extraction Space						
Flooring	Compressed AC Sheet					
	8244/B00C/R0036/Floor Coverings Res/Textile/S7					**No Asbestos Detected**
B00C - R0036 - Dust Extraction Space						
Wall Linings Internal	Flat AC Sheeting					
	8244/B00C/R0036/Wall Linings Internal/S6					**No Asbestos Detected**
Flooring	Compressed AC Sheet					
	8244/B00C/R0036/Floor Coverings Res/Textile/S7					**No Asbestos Detected**
B00C - R0037 - External Movement						
No Asbestos						
B00C - R0038 - Laundry						
No Asbestos						
B00C - R0039 - Preparation						
No Asbestos						
B00C - R0040 - Food Technology L.S.						
No Asbestos						
B00C - R0041 - General Learning Space						
No Asbestos						
B00C - R0042 - Movement						
Floor Coverings Res/Textile	Adesive					
	8244/B00C/R0030/Floor Coverings Res/Textile/S21					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	25m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0030/Floor Coverings Res/Textile/S20					**Chrysotile (white asbestos)**
Ceiling Structures/Linings	Vermiculite					
	8244/B00C/R0032/Ceiling Structures/Linings/S8					**No Asbestos Detected**
B00C - R0043 - Toilets-Boys						
Ceiling Structures/Linings	Flat AC Sheeting	2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0030/Ceiling Structures/Linings/S22					**Chrysotile (white asbestos) , Amosite (brown asbestos)**
B00C - R0044 - Shower						
Ceiling Structures/Linings	Flat AC Sheeting	44m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0030/Ceiling Structures/Linings/S22					**Chrysotile (white asbestos) , Amosite (brown asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
B00C - R0045 - Movement						
No Asbestos						
B00C - R0046 - Plant						
Flue Pipe	Fibre Cement Pipe	6m	Variable positions	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00C/R0046/Flue Pipe/S19					**Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

B00D - Performing Arts - 1960 - Brick/Block (Brick/Block)

Exterior

Eaves Linings	Flat AC Sheeting	30m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00D/R0015/Ceiling Structures/Linings/S13					Chrysotile (white asbestos)
Ceiling Voids - Raked Ceiling	Non Accessible Area					
	- Area inaccessible					
Underfloor Voids - Slab on Ground	Non Accessible Area					
	- Area inaccessible					

Interior

B00D - M0001 - Control Room

No Asbestos

B00D - M0002 - Performing Arts Store

No Asbestos

B00D - R0001 - Cleaning Supplies Store

Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00D/R0006/Floor Coverings Res/Textile/S37					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive					
	8244/B00D/R0006/Floor Coverings Res/Textile/S38					**No Asbestos Detected**

B00D - R0002 - Toilets-Girls

No Asbestos

B00D - R0003 - Performing Arts Changeroom

No Asbestos

B00D - R0004 - Performing Arts Changeroom

No Asbestos

B00D - R0005 - Toilets-Boys

No Asbestos

B00D - R0006 - Cleaning Supplies Store

Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00D/R0006/Floor Coverings Res/Textile/S37					Chrysotile (white asbestos)
Floor Coverings Res/Textile	Adhesive					
	8244/B00D/R0006/Floor Coverings Res/Textile/S38					**No Asbestos Detected**

B00D - R0007 - Movement

Ceiling Structures/Linings	Flat AC Sheeting	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00D/R0007/Ceiling Structures/Linings/S14					Chrysotile (white asbestos)

B00D - R0008 - Performing Arts Store

No Asbestos

B00D - R0009 - Cleaning Store - Distributed

No Asbestos

B00D - R0010 - Stage

No Asbestos

B00D - R0011 - Performing Arts Chair Store

No Asbestos

B00D - R0012 - Movement

Ceiling Structures/Linings	Flat AC Sheeting	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00D/R0007/Ceiling Structures/Linings/S14					Chrysotile (white asbestos)

B00D - R0013 - Movement

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Ceiling Structures/Linings	Flat AC Sheeting	30m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00D/R0015/Ceiling Structures/Linings/S13					**Chrysotile (white asbestos)**
B00D - R0014 - Multi-Purpose Space						
No Asbestos						
B00D - R0015 - Movement						
Ceiling Structures/Linings	Flat AC Sheeting	30m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00D/R0015/Ceiling Structures/Linings/S13					**Chrysotile (white asbestos)**
B00D - R0016 - Staff Kitchen						
No Asbestos						
B00D - R0017 - Toilets-Boys						
No Asbestos						
B00D - R0018 - Movement						
Ceiling Structures/Linings	Flat AC Sheeting	23m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00D/R0015/Ceiling Structures/Linings/S13					**Chrysotile (white asbestos)**
B00D - R0019 - Toilets-Girls						
No Asbestos						
B00D - R0020 - Performing Arts Chair Store						
No Asbestos						
B00D - R9001 - General Assistants						
No Asbestos						
B00D - R9002 - General Storeroom						
No Asbestos						
B00D - R9003 - Maintenance Bulk Store						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority

	Sample No	Test Result

B00I - Building Services - 2009 - Brick/Veneer (Brick/Veneer)

Exterior

Ceiling Voids	No Asbestos Found
Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible

Interior

B00I - R0001 - Machine Storage

No Asbestos

B00I - R0002 - External Movement

No Asbestos

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

B00K - Art/General Learning - 1972 - Brick/Block (Brick/Block)

Exterior

Ceiling Voids - Flat Roof	Non Accessible Area - Area inaccessible					
Underfloor Voids - Slab on Ground	Non Accessible Area - Area inaccessible					

Interior

B00K - R0001 - Kiln Space

Ceiling Structures/Linings	Vermiculite 8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**

B00K - R0002 - Darkroom Space

Ceiling Structures/Linings	Vermiculite 8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles 8244/B00K/R0005/Floor Coverings Res/Textile/S11	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive 8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**

B00K - R0003 - Cleaning Store - Distributed

No Asbestos

B00K - R0004 - Distribution Board Cupboard

Note: No inspection of live electrical installation.

Electrical Mounting Board	Resinous Board **Assumed Asbestos - Electrical Hazard**	2m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)

B00K - R0005 - Toilets-Boys

Floor Coverings Res/Textile	Vinyl Tiles 8244/B00K/R0005/Floor Coverings Res/Textile/S11	5m2	South	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**
Ceiling Structures/Linings	Vermiculite 8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive 8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**

B00K - R0006 - General Storeroom

Ceiling Structures/Linings	Vermiculite 8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles 8244/B00K/R0005/Floor Coverings Res/Textile/S11	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive 8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**

B00K - R0007 - Staff Study

Ceiling Structures/Linings	Vermiculite 8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**

B00K - R0008 - Computer Resource

Ceiling Structures/Linings	Vermiculite 8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles 8244/B00K/R0005/Floor Coverings Res/Textile/S11	26m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3) **Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive 8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result
B00K - R0009 - Resources Store						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	10m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
B00K - R0010 - Machine Storage						
No Asbestos						
B00K - R0011 - Art Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	53m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
B00K - R0012 - Laboratory L.S.						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0013 - Commonroom						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0014 - Preparation						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0015 - Laboratory L.S.						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0016 - Cleaning Store - Distributed						
No Asbestos						
B00K - R0017 - Chemical Store						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	26m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R0018 - Staff Study						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	26m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive	26m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R0019 - Movement						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0020 - Distribution Board Cupboard						Note: No inspection of live electrical installation.

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result
Electrical Mounting Board	Resinous Board	1Unit	North	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					
B00K - R0021 - Cleaning Store - Distributed						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
B00K - R0022 - Staff - Toilet						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0023 - General Storeroom						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	17m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R0024 - Bulk Store						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0025 - Laboratory L.S.						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0026 - Apparatus Store						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0027 - Preparation						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0028 - Resources Store						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
B00K - R0029 - General Storeroom						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
B00K - R0030 - Art Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result
Floor Coverings Res/Textile	Vinyl Tiles	59m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
B00K - R0031 - Art Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0032 - Movement						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R0033 - Stairs						
No Asbestos						
B00K - R0034 - Stairs						
No Asbestos						
B00K - R0035 - Movement						
No Asbestos						
B00K - R0036 - Movement						
No Asbestos						
B00K - R1001 - General Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	46m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1002 - Cleaning Store - Distributed						
No Asbestos						
B00K - R1003 - Distribution Board Cupboard					Note: No inspection of live electrical installation.	
Electrical Mounting Board	Resinous Board	1m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					
B00K - R1004 - Interview/Office - Type 1						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1005 - Staff Study						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	20m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1006 - Art Learning Space						
Floor Coverings Res/Textile	Vinyl Tiles	52m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
B00K - R1007 - Resources Store						
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
B00K - R1008 - General Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	60m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1009 - General Storeroom						
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
B00K - R1010 - General Storeroom						
Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
B00K - R1011 - General Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	52m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1012 - General Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result
Floor Coverings Res/Textile	Vinyl Tiles	52m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00K - R1013 - General Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					No Asbestos Detected
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					No Asbestos Detected
Floor Coverings Res/Textile	Vinyl Tiles	52m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00K - R1014 - General Storeroom						
Floor Coverings Res/Textile	Vinyl Tiles	6m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					No Asbestos Detected
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					No Asbestos Detected
B00K - R1015 - General Storeroom						
Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					No Asbestos Detected
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					No Asbestos Detected
B00K - R1016 - General Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					No Asbestos Detected
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					No Asbestos Detected
Floor Coverings Res/Textile	Vinyl Tiles	59m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00K - R1017 - Staff Study						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					No Asbestos Detected
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					No Asbestos Detected
Floor Coverings Res/Textile	Vinyl Tiles	52m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00K - R1018 - Cleaning Store - Distributed						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					No Asbestos Detected
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					No Asbestos Detected
Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					Chrysotile (white asbestos)
B00K - R1019 - Staff - Toilet						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R1020 - Movement						
No Asbestos						
B00K - R1021 - Distribution Board Cupboard						Note: No inspection of live electrical installation.
Electrical Mounting Board	Resinous Board	NA	North	Good Condition (1)	Low (1)	Low Priority (2-3)
	Assumed Asbestos - Electrical Hazard					
B00K - R1022 - General Storeroom						
No Asbestos						
B00K - R1023 - Study Space						
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	17m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
B00K - R1024 - General Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	59m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1025 - General Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	52m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1026 - General Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	52m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1027 - General Storeroom						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1028 - Study Space						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					**Test Result**
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	23m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1029 - Interview/Office - Type 1						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	12m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1030 - Movement						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	2m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
B00K - R1031 - General Learning Space						
Ceiling Structures/Linings	Vermiculite					
	8244/B00K/R0005/Ceiling Structures/Linings/S12					**No Asbestos Detected**
Floor Coverings Res/Textile	Adhesive					
	8244/B00K/R0009/Floor Coverings Res/Textile/S27					**No Asbestos Detected**
Floor Coverings Res/Textile	Vinyl Tiles	38m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)
	8244/B00K/R0005/Floor Coverings Res/Textile/S11					**Chrysotile (white asbestos)**
B00K - R1032 - Movement						
No Asbestos						
B00K - R1033 - Cleaning Store - Distributed						
No Asbestos						
B00K - R1034 - Stairs						
No Asbestos						
B00K - R1035 - Stairs						
No Asbestos						

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority
	Sample No					Test Result

Demountables

There are no Demountable(s) located at this school as per the AMS records as of 15 Feb 2017.

2017

Product	Material Description	Extent	Location Reference	Material Condition	Risk Status	Control Priority

	Sample No	Test Result

Listing of Electronic Attachments as of 22/03/2017

Available Asbestos Related Electronic Files

8244_ASB_010713_AMP.pdf

* Note : Refer to AMS for details of the attachment(s).

2017
